

# New Middle School @ Polo Club



Week Ending July 7, 2023

# New Middle School @ Polo Club


## ➤ Completed Work:

- Poured the rest of Area A and B slabs
- Continue CMU in Area A
- Continue MEP in Area A and C
- Prep for curb and gutter
- Fire vault set in place and underground fire/water line ran
- Hollow core set in area C and grouted
- Steel columns set in stage area

## ➤ Upcoming Work/Look Ahead:

- Start pouring curbs and gutter
- Start setting joist in area F locker room
- Continue ICF in Area A
- Continue MEP in Area A, C and D
- Continue to lay CMU in Area A
- Continue to install Stala Frames at Windows in Area A
- Continue to install Wood Bucks at Windows in Area A
- **Continue Geothermal Drilling (can be loud)**

Key Plan

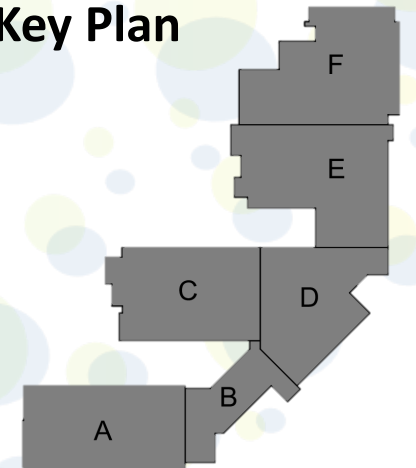



## Area A – CMU Continues to 2<sup>nd</sup> Floor



Week Ending July 7, 2023

## Area A – ICF Concrete Pour



Week Ending July 7, 2023



## Area A – Stala Frame Install



Week Ending July 7, 2023

## Area A – Wood Buck Install Continues



Week Ending July 7, 2023



## Area A and B – Slab Pour



Week Ending July 7, 2023

## Area B – Underslab Rough in Slab Prep



Week Ending July 7, 2023



## Area C – 2<sup>nd</sup> Floor Hollow Core Installed



Week Ending July 7, 2023

## Area F – Gym ICF Continues to Bearing



Week Ending July 7, 2023



## Area F – ICF Concrete Pour



Week Ending July 7, 2023

## Front Entry/Media Center Rendering



Week Ending July 7, 2023
