

New Middle School @ Polo Club



Week Ending May 26, 2023

New Middle School @ Polo Club


➤ Completed Work:

- Foundations in Area A are 90% complete
- ICF walls in Area A are 1/3 complete, Area C complete to hollow core level
- Starting CMU in Area A, 80% complete in Area C to hollow core level
- MEP Following Foundations and CMU/ICF in All Areas
- Storm Sewer continues on the south side of the building
- Grading entrance and roadway for DGA, curbs and gutter

➤ Upcoming Work:

- Complete footers in Area A
- Begin footers in Area D
- Finish CMU in Area C
- ICF to continue in Area A
- Prep Slab on grade in Area A
- MEP following along with structure
- Continue Geothermal (can be loud)
- Continue Storm Sewer along southern drive

Key Plan

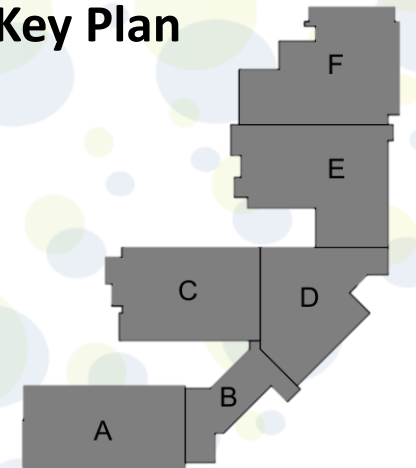

Area A - Slab Prep



Week Ending May 26, 2023

Area A – Concrete Pour in ICF



Week Ending May 26, 2023

Area A – Concrete Footings and ICF



Week Ending May 26, 2023

Area C – Next Course of ICF Continuing



Week Ending May 26, 2023

Area E – ICF Continuing



Week Ending May 26, 2023

Area E – Corridor Stala Frame Install



Week Ending May 26, 2023

Area E – Windows Installed



Week Ending May 26, 2023

Area E – Corridor Wood Buck and Stala Frame Install



Week Ending May 26, 2023

Front Entry/Media Center Rendering



Week Ending May 26, 2023
