

New Middle School @ Polo Club



Week Ending June 30, 2023

New Middle School @ Polo Club


➤ Completed Work:

- Poured 95% of Area A slab on grade
- Area B foundations to 100% complete
- ICF in Area C tomorrow
- Area F Locker Room pour. Complete ICF at Locker Room.
- ICF pour at Area E. ICF Complete Area E
- Subgrade and stone ready for curb and Gutter/Paving at east parking lot
- Continue Geothermal Continuing (62 Complete)
- MEP Continuing in Area B and D
- CMU continuing in Area A
- Doors are 90% set in Area A
- CMU at locker room nearly complete
- Hollow core in Area C is set
- Underground fire protection line to the vault and the vault itself is installed

➤ Upcoming Work/Look Ahead:

- Pouring Slab on Grade in Area A and part of Area B on Friday 6-30
- Complete Slab on Grade in Area A
- Complete Foundations in Area A and C
- Finish Prep for curb and gutter
- Storm Sewer at west drive to bus parking
- ICF in Area A and Complete Area E
- CMU Complete at Area C
- CMU in Area A
- Door Frames Area A
- Continue MEP Rough in
- Continue Geothermal (Can be loud)
- Slab pours should be 100% in future

Key Plan

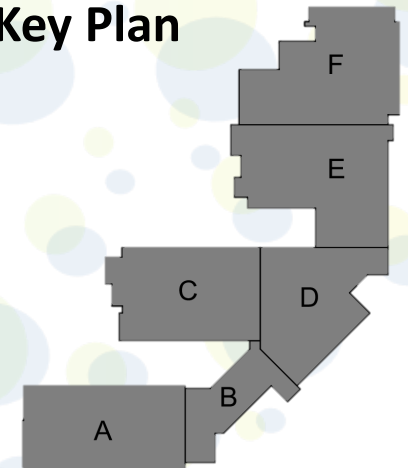

Area A – CMU Continues up to 2nd Floor



Week Ending June 30, 2023

Area A – Setting Hollow Metal Frames



Week Ending June 30, 2023

Area A – Slab Prep



Week Ending June 30, 2023

Area A – Wood Buck Install Continues



Week Ending June 30, 2023

Area C – Hollow Core over Corridor Complete



Week Ending June 30, 2023

Area C – VoAg Lab Hollow Core Almost Complete



Week Ending June 30, 2023

Area F – Gym ICF Continues to Bearing



Week Ending June 30, 2023

Area E & F – Hollow Core at Platform



Week Ending June 30, 2023

Front Entry/Media Center Rendering



Week Ending June 30, 2023
