

BOND UPDATE #215


7.28.23

Here's what is going on with our bond projects.


Enjoy!

Kristi

1. This final storm water systems are now being installed along Golden Eagle Drive and Shuksan Street. This area is almost ready for asphalt.
2. The grass that was planted at the north end of the football field is now growing quickly and taking root.
3. The main parking area is making good progress to be ready for the opening of school this fall.
4. The PAC and Weight room will be receiving new paint over the next month and so the siding on those building match the new building colors.
5. The structural seismic upgrade work has been completed over the auditorium and new roofing is now being installed.
6. The ticket booth has taken shape and interior finishes will start over the next week or two.
7. One of the final items in the new athletic field area is the rubberized track surfacing, this should get started very soon.
8. Landscaping preparation continues and soils are being placed. The actual plantings will occur in the fall to prevent the plants from struggling to take root and survive.
9. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](http://ferndalesd.org)
10. Below is the FHS project timeline as of July 1. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

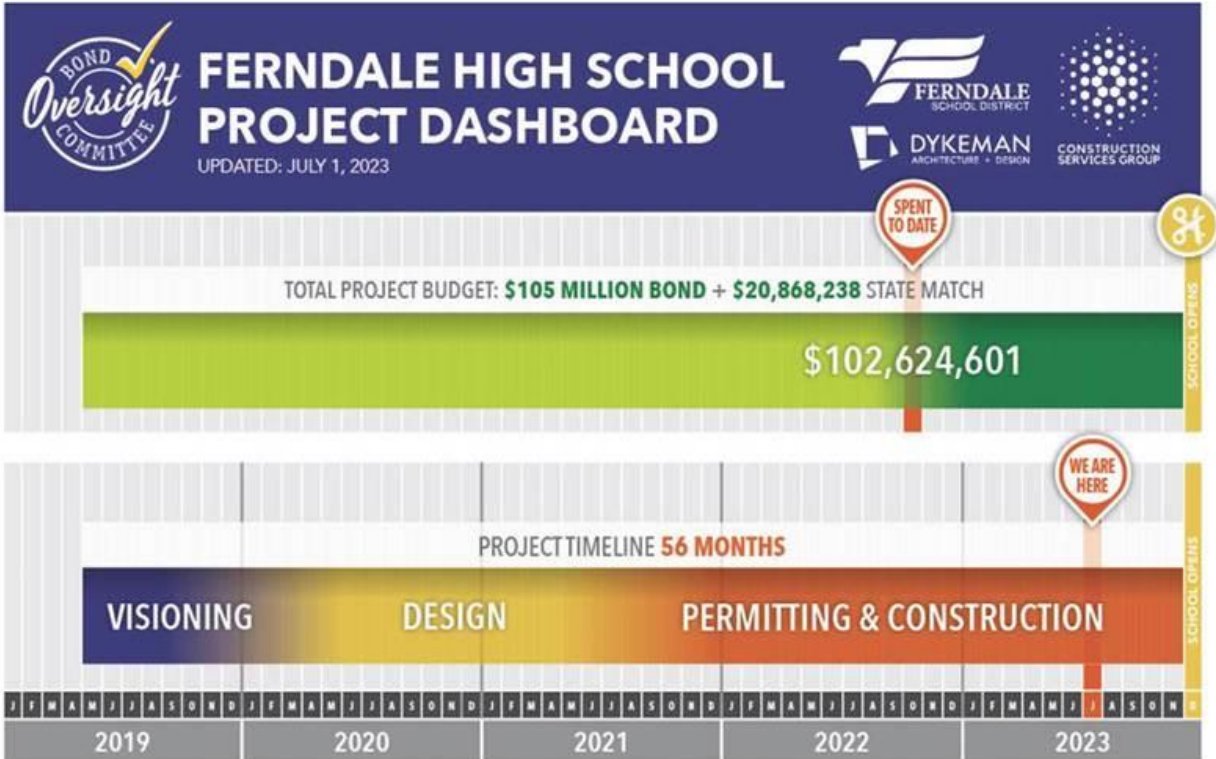

Below is a map showing the various components of the new FHS campus and when they'll be completed.

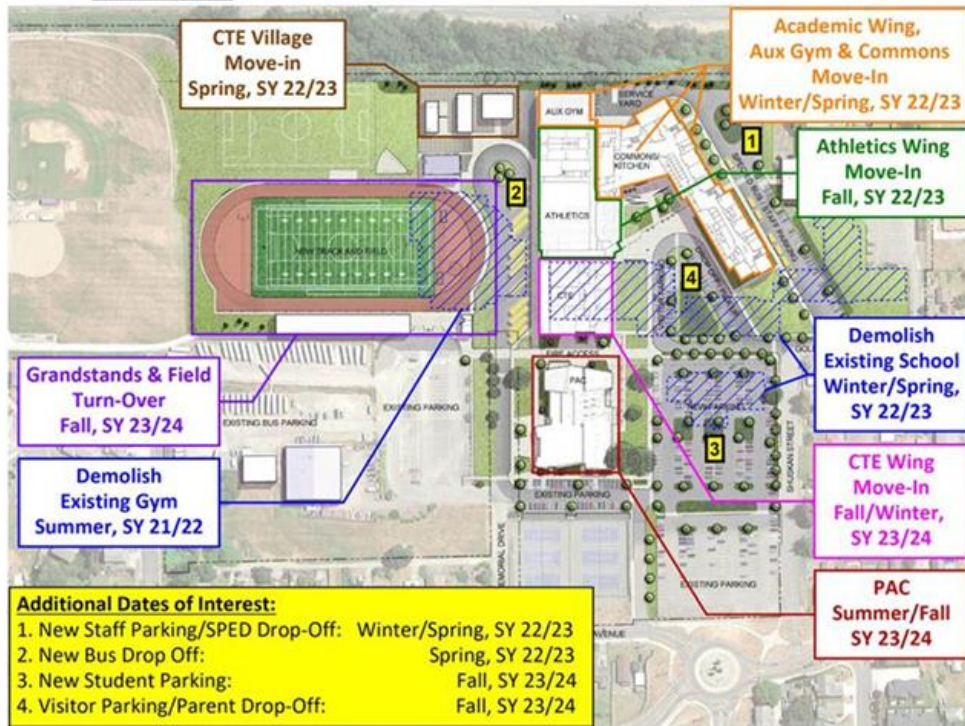

FHS Move-In Plan



If you have questions or comments about any of the content of this update, please feel free to reach out to me.

Kristi



Progress continuing on the entry way to the Athletic Wing.



The final siding on the CTE Wing is complete and the area is now ready for the masonry block to be installed.



Roofing being installed on the Performing Arts Center.



Curbs continue in the new parking area in preparation for asphalt being laid in August.



Finished flooring the in the main kitchen walk in coolers has been installed over the summer months.



New light poles being installed around the parking area.
