

New Middle School @ Polo Club Blvd.



Week Ending August 4, 2023




New Middle School @ Polo Club Blvd.

➤ Completed Work:

- Poured the rest of slabs Area B.
- Continue CMU in Area A and D.
- Continue MEP in Area A, C and D.
- Poured ICF Area and second floor starter course in Area C.
- Set steel in Area A.
- Set Frames in Area D.
- Storm drain and backfill curb.

➤ Upcoming Work/Look Ahead:

- Continue to install and pour ICF in Area C second floor, in cafeteria.
- Continue MEP in Areas A, C and D.
- Continue to lay CMU in Area B and D.
- Continue rock prep for asphalt and roadways.
- Continue to stack ICF in Area F in gymnasium.
- Wreck ICF start course in area C.
- Prep for second floor slab.
- Continue to set hollow core in Area A.
- Continue to brace ICF in Area F Gymnasium with 2x4 lumber.
- **Geothermal Drilling (can be loud)**

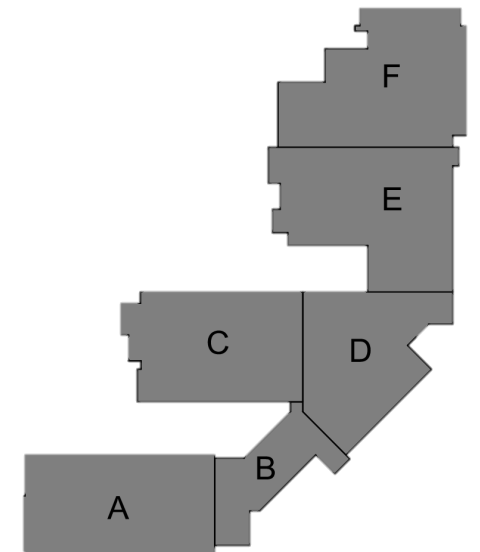

New Middle School @ Polo Club Blvd.

Area A – Wood Bucks Installed



Week Ending August 4, 2023

New Middle School @ Polo Club Blvd.

Area B – Admin Suite Layout



Week Ending August 4, 2023

New Middle School @ Polo Club Blvd.

Area B – Stala Frames Set



Week Ending August 4, 2023

New Middle School @ Polo Club Blvd.

Area C – Restroom Plumbing Rough in at Sinks



Week Ending August 4, 2023

New Middle School @ Polo Club Blvd.



Area D – Media Center Hollow Metal Frames Set



Week Ending August 4, 2023

New Middle School @ Polo Club Blvd.

Area D – Media Center Ready For CMU



Week Ending August 4, 2023

New Middle School @ Polo Club Blvd.

Mockup – Vapor Barrier Installed, ready for Brick, Stone and Metal Panels



Week Ending August 4, 2023

New Middle School @ Polo Club Blvd.

Site – Curb Install Complete Ready For Asphalt



Week Ending August 4, 2023

New Middle School @ Polo Club Blvd.



Front Entry/Media Center Rendering



Week Ending August 4, 2023
