

CONSTRUCTION UPDATE



CONSTRUCTION UPDATE - 7/12/2023

Deasy Elementary School – Elevator / Stair Tower

- Branch onsite 7/10/2023 starting chimney demolition
- Irwin Contracting to place site fencing after chimney demolition complete
- Reviewed site logistics and site fencing plan with Director of Facilities and Principal
- Irwin Contracting will begin with implementing temporary egress plan with interior wall construction and temporary signage projected start week of 7/17/2023

Projected Elevator/Stair Completion – Summer 2024





CONSTRUCTION UPDATE - 7/12/2023

Deasy Elementary School – Patio Construction

- Total Construction completed retaining wall repairs
- Existing pavers removed 50% along with existing waterproofing
- Concrete pad removal ongoing to prepare for new waterproofing
- New patio drains and drain piping to be installed after new waterproofing installed

Projected Patio Completion – August 2023










CONSTRUCTION UPDATE - 7/12/2023

Deasy Elementary School – Photos week of 7/10/2023

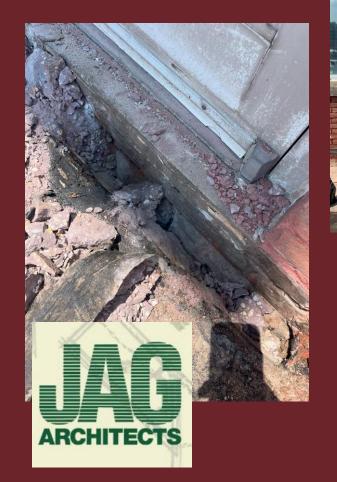



#### CONSTRUCTION UPDATE - 7/12/2023

#### Landing Elementary School – Classroom Addition

- Met onsite with Stalco and major subcontractors. Excavation to begin after stair abatement complete – Projected start 7/17/2023
- Met with Maccarone Plumbing and National Grid to discuss relocation of gas header. Relocation application form signed and submitted to National Grid
- Site fencing to be installed on 7/14/2023
- Working with Stalco and subcontractors to relocate major utilities out of the way of excavation and still maintain utility services to the building during construction
- Director of Facilities provided temporary parking area for construction crews during construction. Stalco will maintain temporary fencing for contractor parking area.

Projected Completion of Extention – September 2024





CONSTRUCTION UPDATE - 7/12/2023

Landing Elementary School – Photos week of 7/10/2023









### CONSTRUCTION UPDATE - 7/12/2023

#### Bond Update – Phase I

Classroom & Office Doors & Locks Districtwide	Winter 2023
---	-------------

Exterior Door Replacements Winter 2023

High School Main Field November 2023

High School Lockers Fall 2023

High School PA System Fall 2023

Tennis Court Replacement August – November 2023

Tennis Court Parking lot, Curb, Walkway Replacement August – November 2023

Handball Court Reconstruction August – November 2023





<sup>\*\*</sup> Coordination and discussions with all concerns parties regarding use of fields during construction duration

### CONSTRUCTION UPDATE - 7/12/2023

#### Bond Update – Phase II

High School – Science Labs	Summer 2024

High School – Cafeteria and Kitchen Summer 2024

High School – Bathrooms Summer 2024

Courtyard Curtain Wall Replacement Summer 2024

High School – HVAC Summer 2025

Incoming Electrical Service Summer 2025



