

New Middle School @ Polo Club Blvd.



Week Ending August 11, 2023




New Middle School @ Polo Club Blvd.

➤ Completed Work:

- Poured topping in Area C eastside.
- Continue CMU in Area B and D.
- Continue MEP in Area A,C,B,D and installing temp lights.
- Set hollow core in Area A and Grouted.
- Wreck ICF in Area C, B and F.
- Stacking ICF in gym.
- Poured ICF Area B, F and D.
- Installed stala frames in Area B.
- Continue to install Storm drain.
- Continue drill and grout geothermal wells.

➤ Upcoming Work/Look Ahead:

- Continue to install and pour ICF in Area B, D and F.
- Continue MEP in Areas A,C,B and D.
- Continue to lay CMU in Area B and D.
- Continue to stack ICF in Area F in gymnasium.
- Wreck ICF in Area B, D and F.
- Prep for second floor slab in Area C.
- Start Fire protection.
- Continue to drill and grout geothermal wells (could be loud)
- Finish setting steel in Area B and D.
- Finish CMU in area B and D to hollow core level.

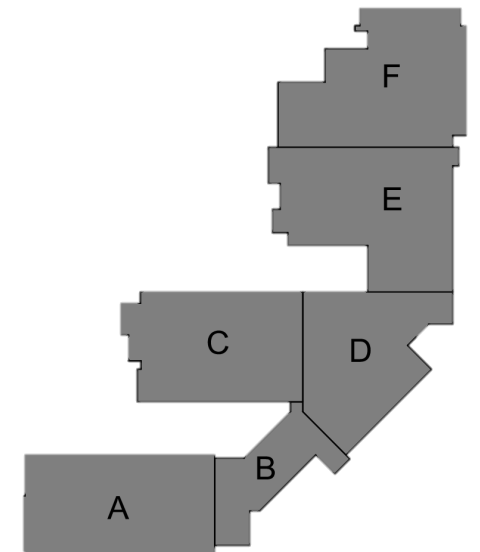

New Middle School @ Polo Club Blvd.

Area B – ICF Concrete Pour at Admin Window



Week Ending August 11, 2023

New Middle School @ Polo Club Blvd.

Area B – Main Entrance Window Frame Install



Week Ending August 11, 2023

New Middle School @ Polo Club Blvd.




Area C – Before Pour of First Area of Topping Slab on 2nd Floor



Week Ending August 11, 2023

New Middle School @ Polo Club Blvd.

Area C – Poured First Area of Topping Slab on 2nd Floor

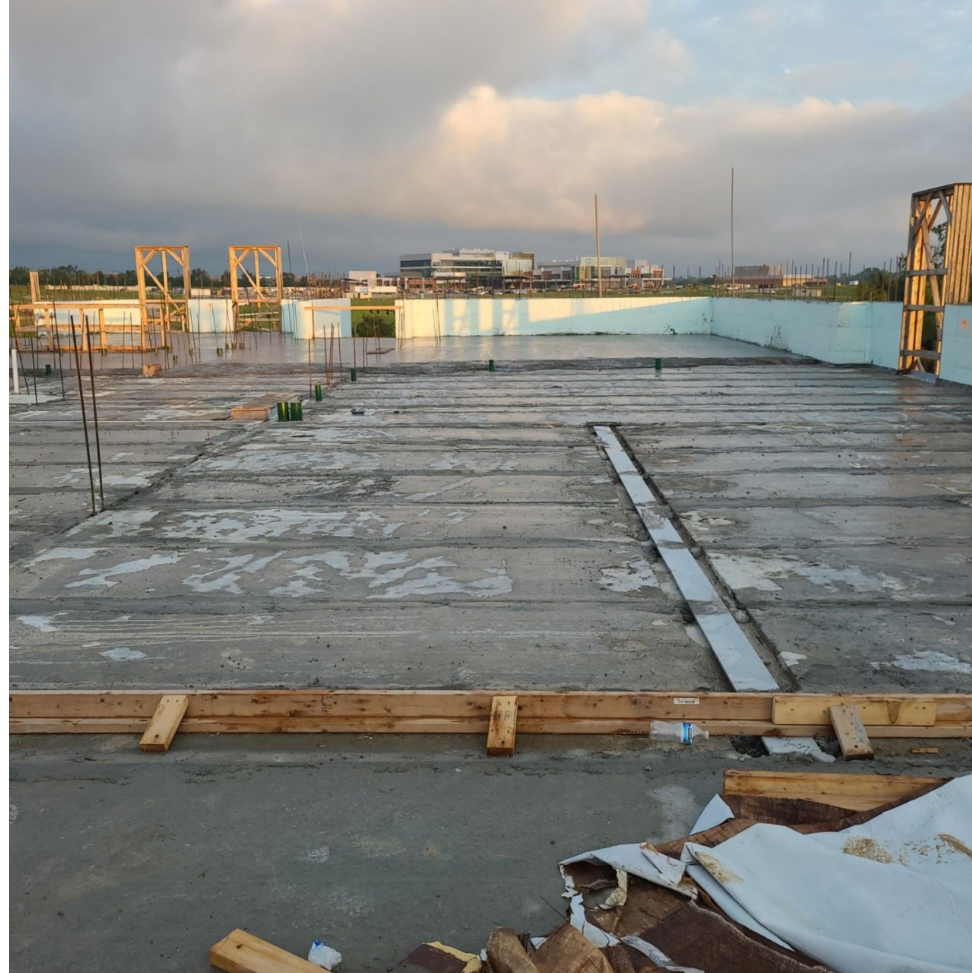

Week Ending August 11, 2023

New Middle School @ Polo Club Blvd.



Area D – Media Center CMU



Week Ending August 11, 2023

New Middle School @ Polo Club Blvd.

Area E – Wood bucks Installed at Cafeteria



Week Ending August 11, 2023

New Middle School @ Polo Club Blvd.

Area F – Above Ceiling Roughins Continue



Week Ending August 11, 2023

New Middle School @ Polo Club Blvd.

Area F – ICF Stacking Continues at Gym



Week Ending August 11, 2023



New Middle School @ Polo Club Blvd.

Front Entry/Media Center Rendering



Week Ending August 11, 2023
