


# BOND UPDATE #217

8.11.23



Here's what is going on with our bond projects.

Enjoy!  
Kristi

1. Now that most of the upgrades are finished along Golden Eagle Drive, crews will remove the existing asphalt during the week of August 21. After that, they'll lay new asphalt.
2. Crews are preparing the main parking lot west of campus for asphalt to be laid next week.
3. Grass is starting to grow in the new practice athletic field to the east of the main Athletic Field. Soon, it'll be at the same level as the new grass of the area's north end.
4. Crews are still adding the new rubberized track surface. This work should be done sometime next week.
5. The weight room was painted this week to match the rest of the new campus.
6. Code-required seismic upgrade work in the Performing Arts Center is close to complete! Now that much of the PAC's structural work is finished, crews are repainting the building and adding new sheetrock.
7. Masonry work on the CTE Wing continued this week and is nearly finished. The final cleaning and sealing of the block will likely occur next week.
8. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](https://ferndalesd.org/Bond-2019)
9. Below is the FHS project timeline as of July 1. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

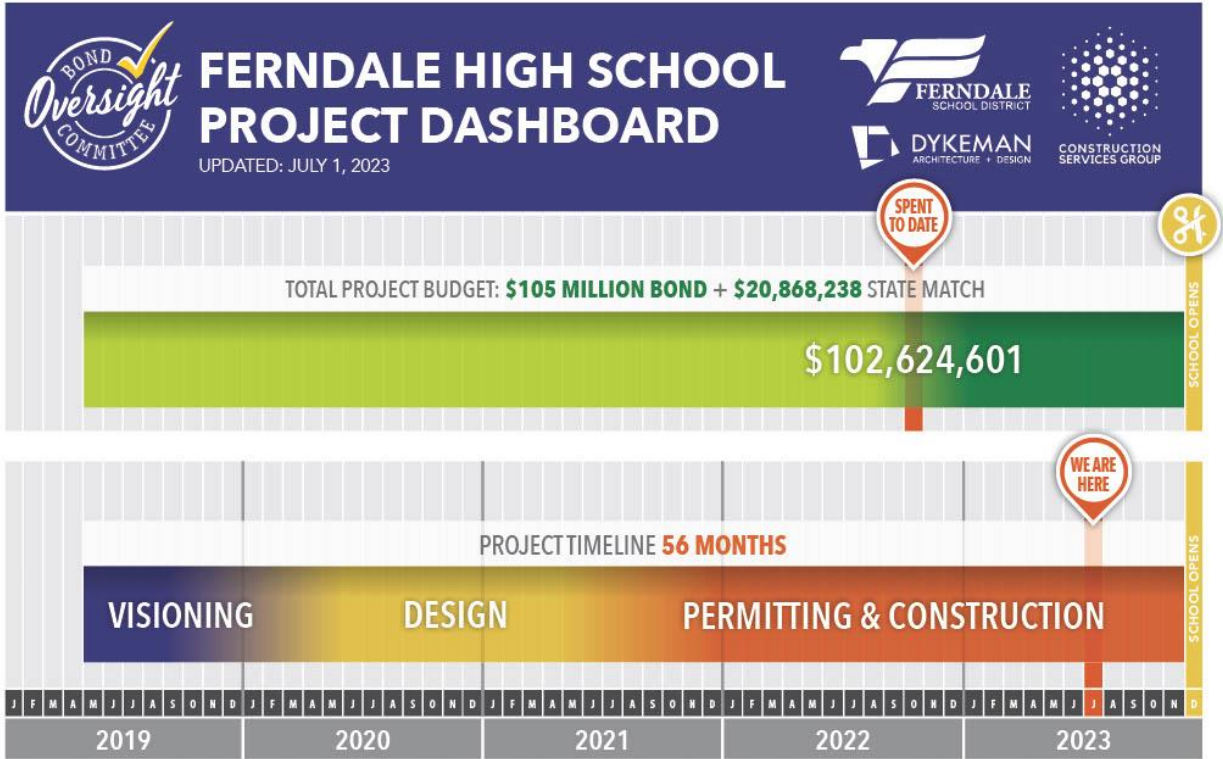

10. Below is a map showing the various components of the new FHS campus and when they'll be completed.

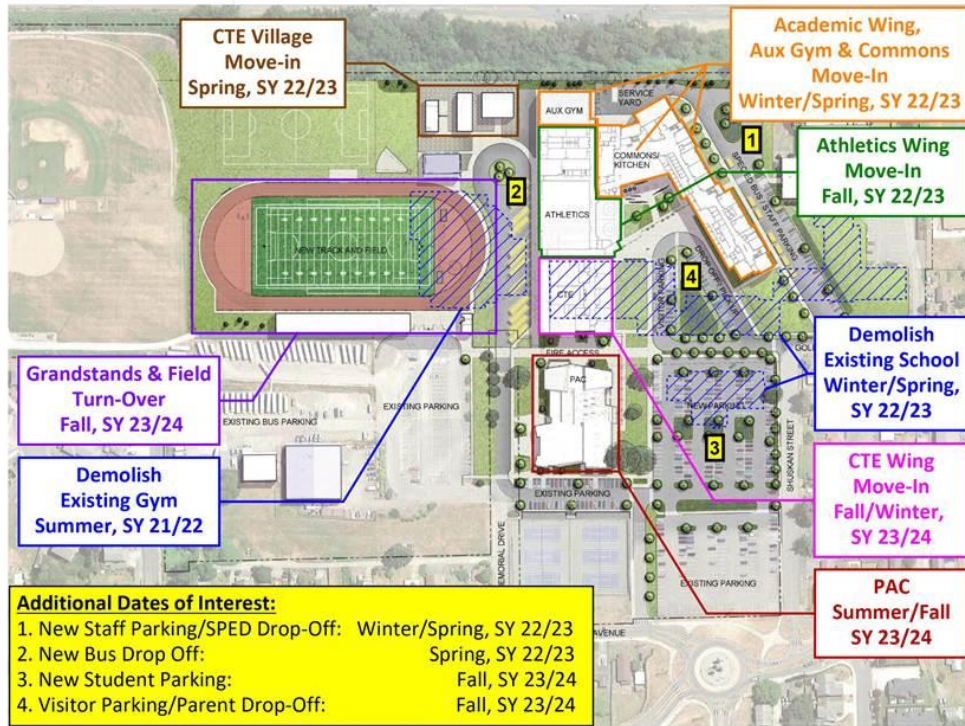

# FHS Move-In Plan

If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues.

Kristi



**Weight room being painted to match the rest of the new campus**





**Many rooms in the PAC are having new carpet installed to match the new building**



**Crews making progress on the rubberized track surface**





**Mechanical and electrical infrastructure being installed in the new CTE Wing**



**Masonry block around the CTE Wing is still being installed**





**Crews making final preparations for asphalt being laid next week**
