

New Middle School @ Polo Club Blvd.



Week Ending August 18, 2023




New Middle School @ Polo Club Blvd.

➤ Completed Work:

- Continue CMU in Area B and D.
- Continue MEP in Area A, C, B, D and installing temp lights.
- Grouted Area A hollow core.
- Form ICF in Area C, A and F.
- Poured ICF in Area D.
- Drilled and grouted 153 geothermal wells. 70%
- Installed stala frames in Area B.
- Continue to install Storm drain.

➤ Upcoming Work/Look Ahead:

- Continue to install and pour ICF in Area B, D and F.
- Continue MEP in Areas A, C, B and D.
- Continue to lay CMU in Area B and D.
- Continue to stack ICF in Area F in gymnasium.
- Continue to install ICF in Area B, D and F.
- Start Fire protection.
- Continue to drill and grout geothermal wells (could be loud)
- Finish setting steel in Area B and D.
- Finish CMU in Area B and D to hollow core level.

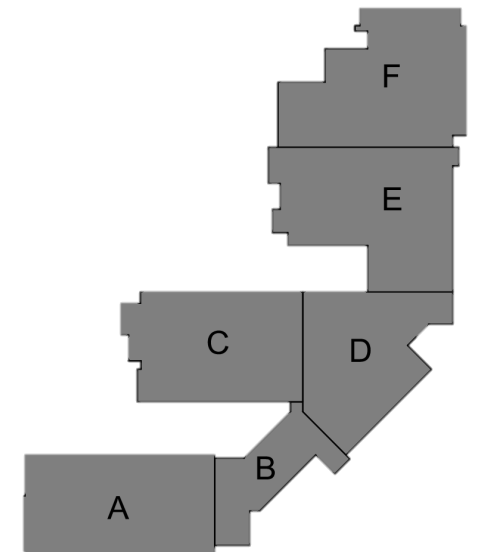

New Middle School @ Polo Club Blvd.

Aerial – Curbs and Asphalt Installed at Front Parking Lot



Week Ending August 18, 2023

New Middle School @ Polo Club Blvd.



Aerial – CMU continuing in the Media Center



Week Ending August 18, 2023

New Middle School @ Polo Club Blvd.



Area B – Main Entry Vestibule



Week Ending August 18, 2023

New Middle School @ Polo Club Blvd.

Area B – Admin CMU Walls up to 2nd Floor



Week Ending August 18, 2023

New Middle School @ Polo Club Blvd.

Area D – CMU install at Art Room Display



Week Ending August 18, 2023

New Middle School @ Polo Club Blvd.

Area E – Structural Steel at Stage Complete



Week Ending August 18, 2023

New Middle School @ Polo Club Blvd.

Area F – ICF Continuing at the Gym



Week Ending August 18, 2023

New Middle School @ Polo Club Blvd.

Mockup – Brick and Stone on site for installation



Week Ending August 18, 2023

New Middle School @ Polo Club Blvd.



Front Entry/Media Center Rendering



Week Ending August 18, 2023
