


BOND UPDATE #218

8.18.23


Here's what is going on with our bond projects.

Enjoy!
Kristi

1. Final curbs, gutters and perimeter concrete along Golden Eagle Drive and Shuksan Street are being completed this week. Asphalt will be laid next week.
2. The main parking lot has now had the final asphalt installed. Road striping and light pole installation will start next week.
3. The exterior walls of the weight room have now been painted to match the rest of the new buildings. Soon, crews will paint the exterior of the Performing Arts Center (PAC) as well, to bring some color consistency across campus.
4. The rubberized track surface is now complete! Final striping will occur either over the weekend or at the beginning of next week.
5. The Athletic Field's new ticket booth had its roofing and signage installed this week.
6. Crews are putting the finishing touches on the PAC's sheetrock, paint, carpet and ceiling tile upgrades, so it can be ready for students' return on August 30.
7. Code-required seismic upgrade work in the PAC is almost wrapped up. The building has now been seismically improved.
8. Masonry work on the CTE Wing continues to make progress; Most of the brick has now been cleaned, and is ready to be sealed. The masons have one more wall to complete.
9. The Bond Oversight Committee will hold their next regular meeting at 6 p.m. Tuesday at Mountain View.
10. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](http://ferndalesd.org)
11. Below is the FHS project timeline as of July 31. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

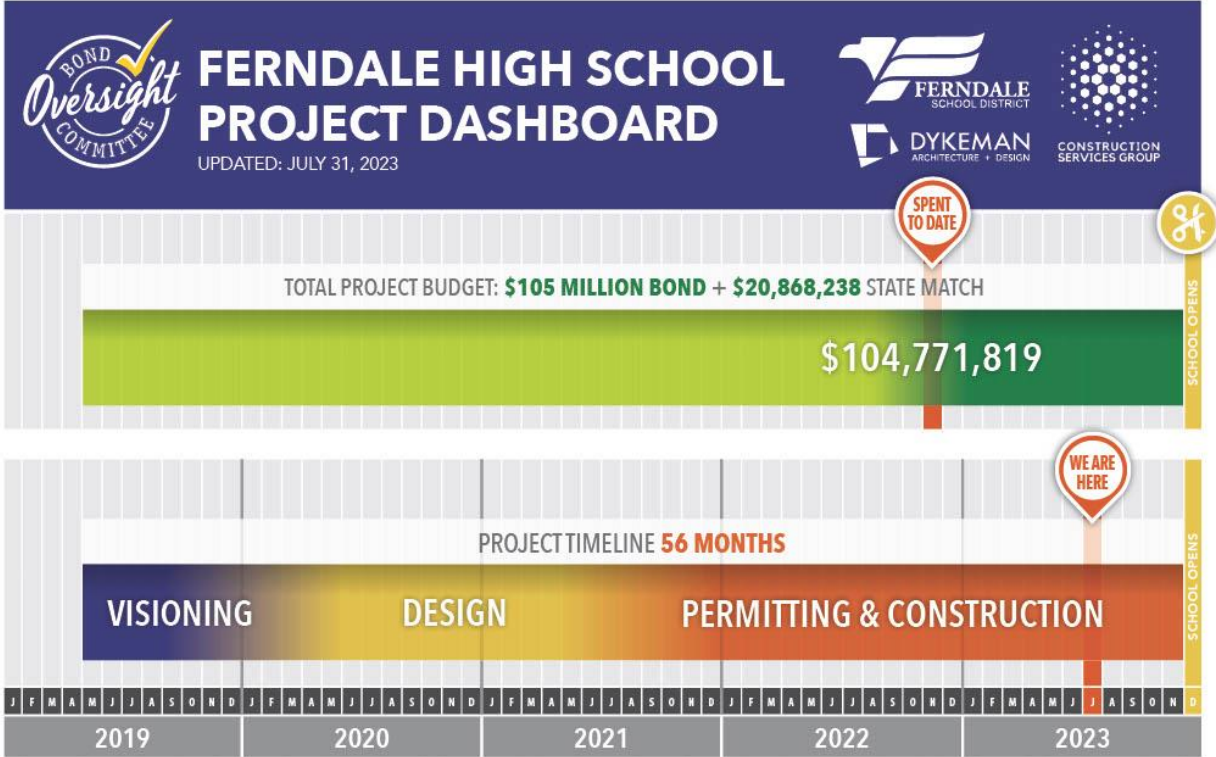

12. Below is a map showing the various components of the new FHS campus and when they'll be completed.

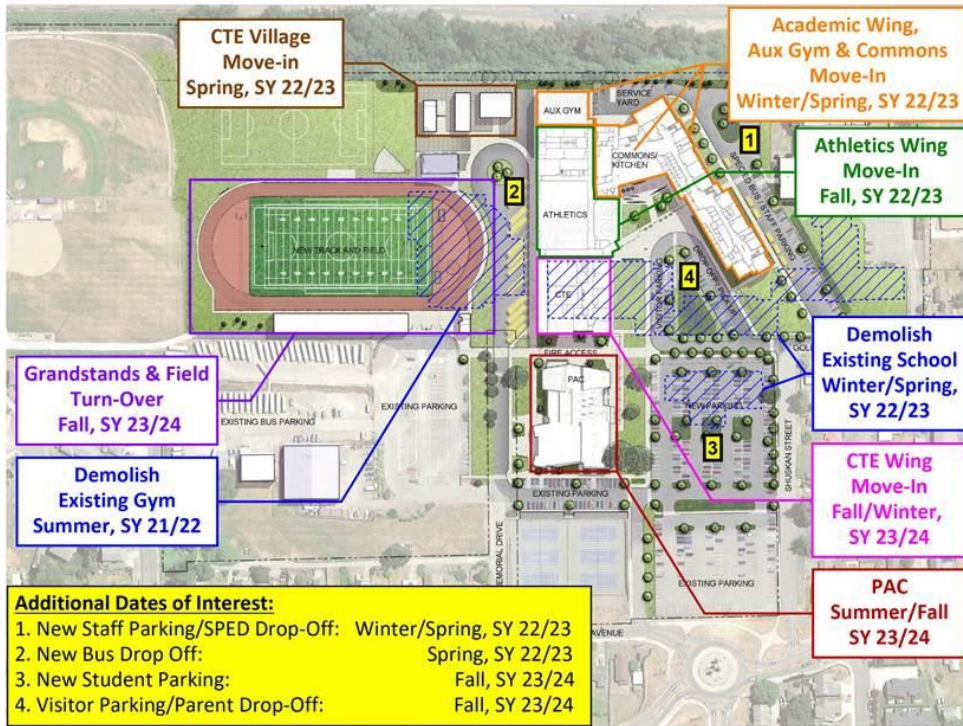

FHS Move-In Plan



If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues.

Kristi



The rubberized track surface is fully installed and ready for final striping



Crews installing rubberized track surface



The new student parking lot is almost complete



Asphalt being installed around the new parent drop-off area



Asphalt being laid in the new student parking lot



Asphalt being rolled in the new student parking lot



The new ticket booth is almost finished!
