




New Middle School @ Polo Club Blvd.

➤ Completed Work:

- Continue CMU in Area B, D, F, E and Second Floor Area C.
- Continue MEP in Area A, C, B, D and installing temporary lights.
- Grouted Area A hollow core planks.
- Form ICF in Area C, A and F.
- Poured concrete at ICF in Area C.
- Continue to install Storm Drain.
- Continue to drill and grout geothermal wells.
- Set Steel in Area D.

➤ Upcoming Work/Look Ahead:

- Continue to install and pour ICF in Area B, D and F.
- Continue MEP in Areas A, C, B, F and D.
- Continue to lay CMU in Area B, D, F, E and Second Floor Area C.
- Continue to stack ICF in Area C Second Floor and Area F in Gym.
- Stack ICF in Area B, D, and F.
- Continue Fire Protection in Area C.
- Continue to drill and grout geothermal wells (could be loud)
- Finish setting steel in Area B and D.
- Finish CMU in Area B and D to hollow core level.
- Pour topping in Area A on Second Floor.

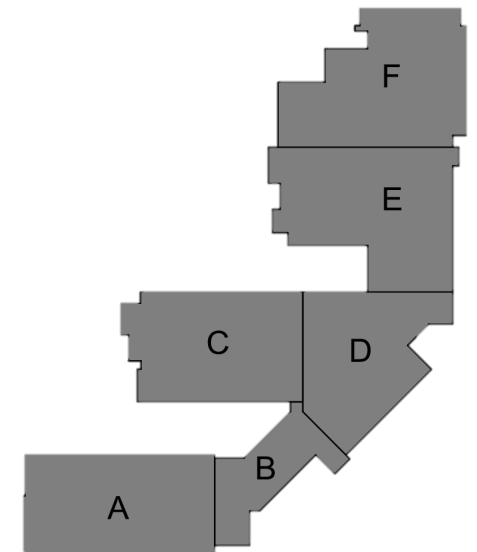

New Middle School @ Polo Club Blvd.




Area A – Hollow Core Planks Set on 2nd Floor



Week Ending August 25, 2023

New Middle School @ Polo Club Blvd.

Area C – 1st Floor MEP Rough in Above Ceiling Continues

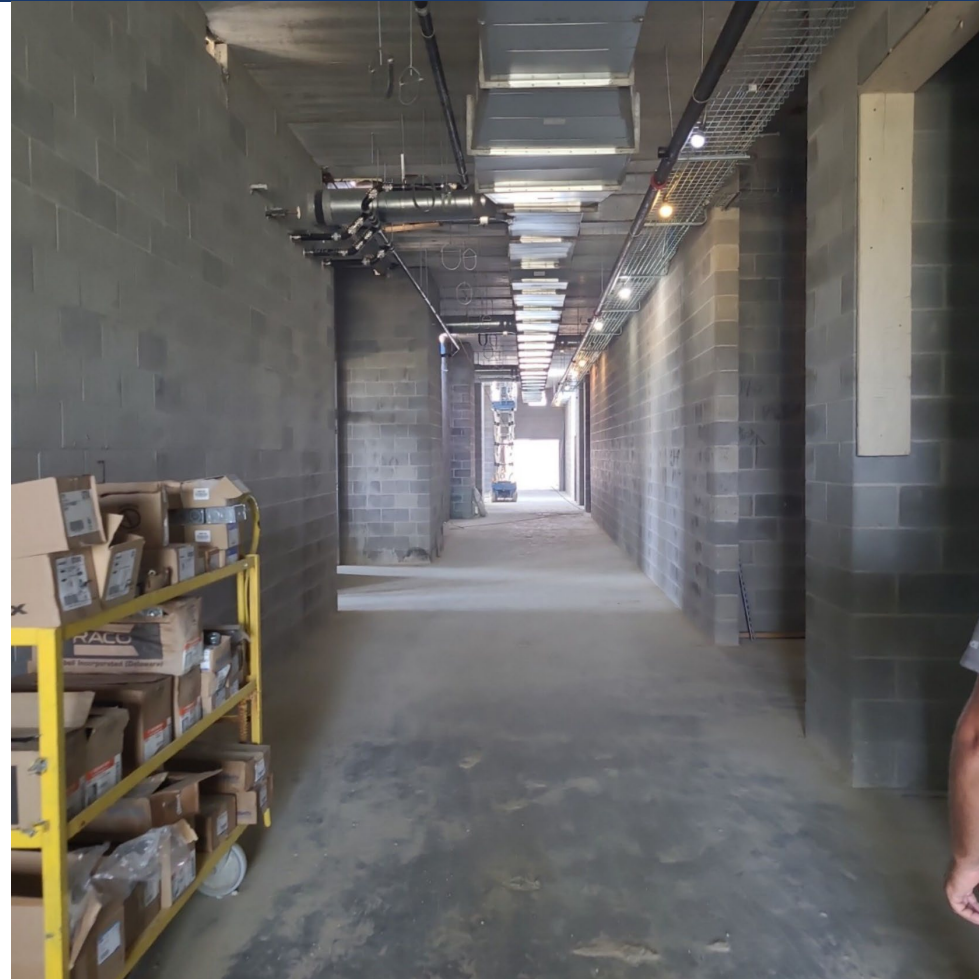

Week Ending August 25, 2023

New Middle School @ Polo Club Blvd.

Area D – Media Center Steel Columns Set at Overhang



New Middle School @ Polo Club Blvd.

Area E – Cafeteria Stala Frame Windows Set



Week Ending August 25, 2023

New Middle School @ Polo Club Blvd.

Area E – CMU Install at Cafeteria Started



Week Ending August 25, 2023

New Middle School @ Polo Club Blvd.

Area F – Continue to Stack ICF Walls at Gym



Week Ending August 25, 2023

New Middle School @ Polo Club Blvd.

Mockup –Brick and Stone Install Continues



Week Ending August 25, 2023

New Middle School @ Polo Club Blvd.

Site – Geothermal Drilling Continues



Week Ending August 25, 2023
