
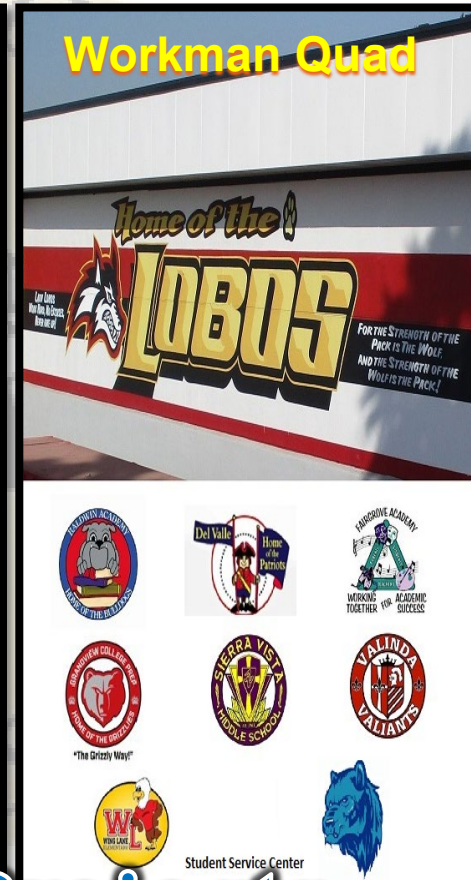


HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



School Site Improvement Projects

Business Services

Regular Board Meeting
June 22, 2023



PROJECT COMPLETE LIST 2022-2023



Site	Item Description	Funding Source	Completed Date
Cedarlane	Asphalt Installation Behind Locker Room	Facilities	1/2023
Los Altos HS	Path of Travel – ADA Issues	Facilities	1/2023
District Office	Fencing Replacement	Facilities	2/2023
Student Service Center	Flooring	Child Development	2/2023
Wilson HS	Flooring – Conference Room	Facilities	2/2023
Willow	New Interior Painting – IRS	Adult ED	2/2023
Amar	Ceiling Tiles & Lighting (14 Classrooms)	Facilities	3/2023
District Office	HVAC & Electrical Upgrades Building C	Facilities	3/2023
5 Sites	Civic Learning Award Signage	District	4/2023
Cedarlane	Drainage Repair	Facilities	4/2023
Los Altos HS	Flooring – H8	Facilities	4/2023
Workman HS	Kitchen Floor Repair	Facilities	4/2023
Student Service Center	Store Front Renovation Room 12	Child Development	5/2023
La Puente HS	Office Administration – Single Point of Entry	Facilities	6/2023
La Puente HS	Gym & Locker Room HVAC	Project Funds	05/2023 *

* Units are operational, 100% project completion pending air balance and duct painting

PROJECT COMPLETE LIST 2022-2023




Site	Item Description	Funding Source	Completed Date
Willow	Bottle Filling Stations	Adult ED	7/2022
Sparks ES	Carpet – Classroom 12	Facilities	7/2022
Lassalette	Front Exterior Turf	Facilities	7/2022
La Puente HS	Dream Center	Facilities	8/2022
Workman HS	Exterior Lighting (Solar Power) at Lobo Lane	Facilities	8/2022
District Office	Flooring and Lights – Board Room	Facilities	8/2022
Wing Lane	Parking Lot Striping	Facilities	8/2022
La Puente HS	Kitchen	COPS/Facilities	9/2022
La Puente HS	Pool	COPS/Facilities	9/2022
Workman HS	Additional Exterior Lighting (Solar Power) at Lobo Lane	Facilities	10/2022
Sparks MS	Front Exterior Turf	Facilities	10/2022
Workman HS	Railing	Facilities	10/2022
Lassalette	Ramps Repaired	Facilities	11/2022
Sparks ES	Flooring - Classroom 24	Facilities	12/2022
Wilson HS	Flooring – B4, B8	Facilities	12/2022
District Wide	Pivot Award Signage	District	12/2022

Projects Completed as of June 22, 2023

5 Sites – Civic Learning Award (4/2023)

NEW!

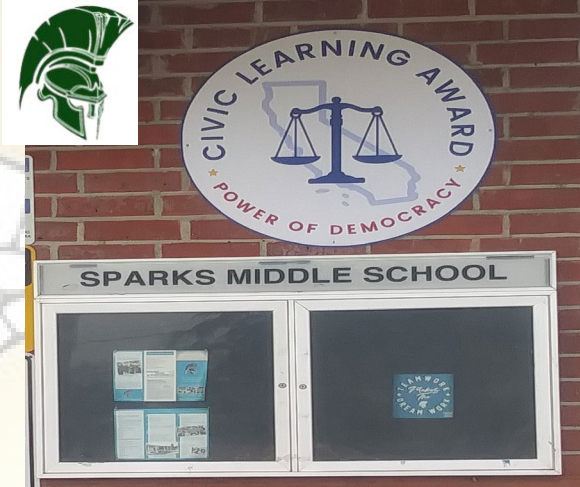

Projects Completed as of June 22, 2023

Cedarlane – Drainage Repair Admin Area (4/2023)

NEW!



Projects Completed as of June 22, 2023

Los Altos HS – Flooring H8 (4/2023)

NEW!



NEW!

Projects In Process

Wedgeworth K-5 Permanent



NEW!

Projects In Process

Wedgeworth K-5 Permanent



Projects In Progress

2022-2023



Projects In Progress as of June 22, 2023

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Workman HS	Phase II Stadium and Baseball Field (Phase I Track & Field and Softball Field Complete)	Complete	Complete	Pending	Pending	Various - Estimate Cost \$18 M	10/2024
Baldwin ES Cedarlane Fairgrove Sparks ES Lassalette	Blacktop Asphalt & Striping	NA	NA	Bidding	Pending	Facilities	12/2023
California ES Cedarlane District Office Bldg C Grazide ES Lassalette Los Altos HS SSC (Sierra Vista) Sparks ES Stimson LC Stimson ADJ Portable Valley Alt HS – CDS Workman ES 6/27 Workman HS	Reroof Various Buildings	In Progress	NA	Bidding	Pending	Deferred Maint.	01/2024
Wedgeworth	K-5 Permanent School	Complete	Complete	Complete	9/2022	COPS	06/2025
Dibble AS	HVAC Replacement	Complete	NA	Complete	In Progress	Adult Ed	12/2023
Willow AS	HVAC Replacement	Complete	NA	Complete	In Progress	Adult Ed	12/2023
Willow AS	Fire Alarm Installation	Complete	NA	Complete	In Progress	Adult Ed	12/2023

Projects In Progress as of June 22, 2023

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Dibble AS	Fire Alarm Installation	Complete	NA	Complete	In Progress	Adult Ed	12/2023
District Office	Fuel Station Repairs	NA	NA	Complete	Pending	Facilities	09/2023





Projects with Division of State Architect (DSA) Waiting on Approval

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
Los Altos HS	Gym & Locker Room HVAC (65 tons of temporary HVAC units have been installed)	Complete	Pending	Complete	TBD	Approx. 3 months after DSA approval
Kwis Elementary	Baseball Fields (Two Youth)	Complete	Pending	Pending	6/2023	8/2024
Center for the Performing Arts	Site Demolition	Complete	N/A	In Progress	08/2023	10/2023
Center for the Performing Arts	Construction of NEW Performing Arts Center with approx. 500 seat capacity	Complete	Pending	Pending	TBD	2/2025

Projects in Design

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
Districtwide	HVAC System Replacements	Pending	Pending	In Progress	TBD	TBD
District Office	Portable Installation meeting/flex space	In Progress	NA	Pending	9/2023	1/2024

The background features a large, faded circular logo for Unifield School District. The logo contains the text "UNIFIELD SCHOOL DISTRICT" around the perimeter, "1970" at the bottom, and a central graphic of a stone archway with three openings. A horizontal bar with a green-to-yellow gradient is positioned at the top of the page.

Next Report – July 20, 2023
