

HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



School Site Improvement Projects

Regular Board Meeting
August 24, 2023

Business Services



PROJECT COMPLETE LIST 2023-2024



Site	Item Description	Funding Source	Completed Date
Wing Lane	K1 & K2 Flooring	Facilities	6/2023
La Puente HS	Weight Room – Flooring and Painting	Facilities	6/2023
Amar	Ramp Repair	Child Development	6/2023
Mesa Robles	Kinder Asphalt	Facilities	6/2023
Nelson ES	Asphalt Slurry and Paint	Site	7/2023
Bixby	Parking Lot Re-Striping	Facilities	7/2023
Del Valle	Parking Lot Re-Striping	Facilities	7/2023
Nelson Elementary	Parking Lot Re-Striping	Facilities	7/2023
Sierra Vista MS	Parking Lot Re-Striping	Facilities	7/2023
Sparks ES	Parking Lot Re-Striping	Facilities	7/2023
Sparks MS	Parking Lot Re-Striping	Facilities	7/2023
Fairgrove	3 Bottle Filling Station	Facilities	7/2023
Kwis	3 Bottle Filling Station	Facilities	7/2023
La Puente HS	2 Bottle Filling Station	Facilities	7/2023
Sparks MS	3 Bottle Filling Station	Facilities	7/2023
Wilson HS	3 Bottle Filling Station	Facilities	7/2023
Stimson Building / Adjacent District Equity & Access	Refurbish (Facilities, Flooring, Painting, Ramp, and Roofing)	Facilities	7/2023
Valley HS	C1 & C2 Renovations (Ceiling Tiles, Flooring and Painting)	Facilities	7/2023
Cedarlane	Synthetic Turf	Facilities	7/2023

Deep Cleaning of all School Facilities completed during Summer Break

Projects Completed as of August 24, 2023

Wing Lane – K1 & K2 Flooring (6/2023)


NEW!



Projects Completed as of August 24, 2023

La Puente HS – Weight Room Flooring and Painting (6/2023)

NEW!

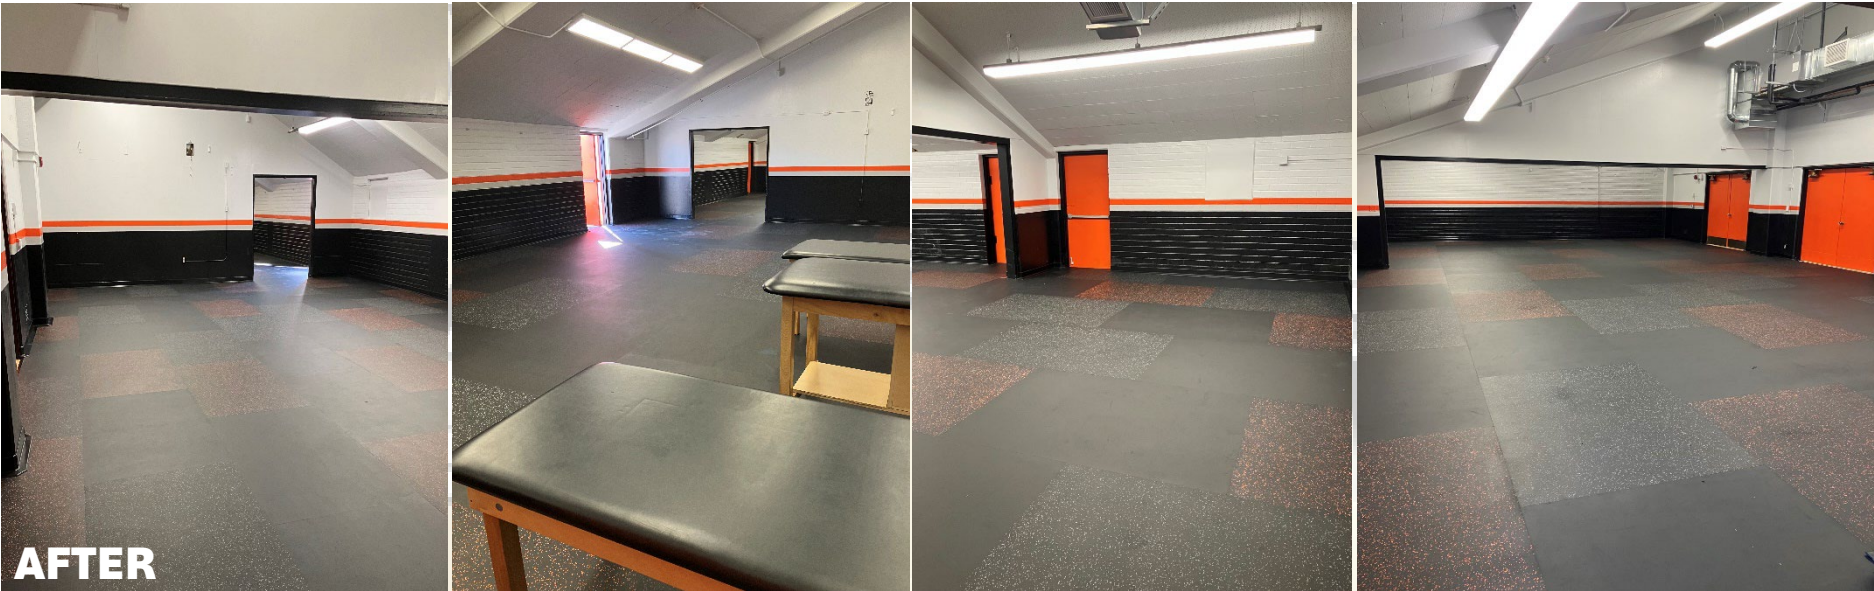

AFTER



BEFORE

Projects Completed as of August 24, 2023

Mesa Robles – Kinder Asphalt (6/2023)

NEW!



Projects Completed as of August 24, 2023

Nelson – Asphalt Slurry & Paint (7/2023)

NEW!



Projects Completed as of August 24, 2023

Parking Lot Striping at Various Sites (7/2023)

NEW!




BEFORE


Sparks ES



AFTER

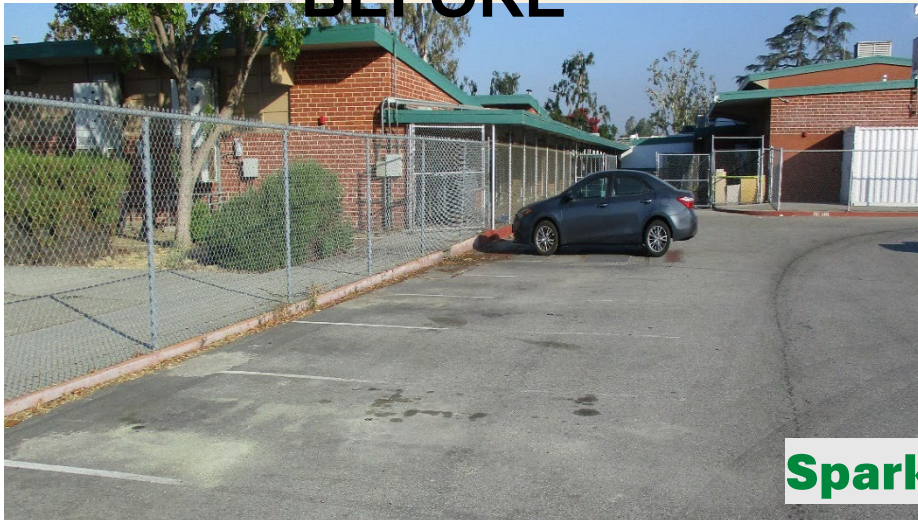

Sparks MS

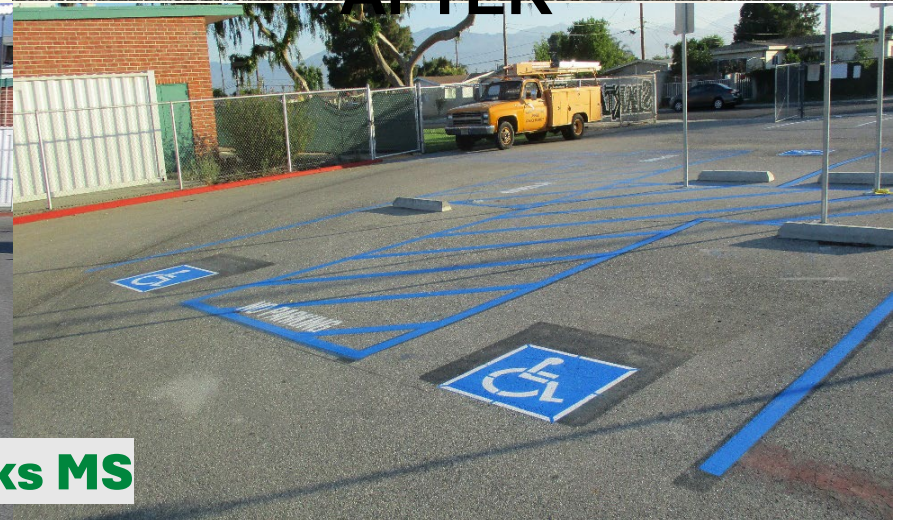

Projects Completed as of August 24, 2023

Bottle Filling Stations at Various Sites (7/2023)

NEW!



Bottle Filling Stations



Site:	# of Stations	Site:	# of Stations	Site:	# of Stations
Baldwin Academy	3	Lassalette	3	Sparks ES	2
Bixby ES	2	Los Altos ES	1	Sparks MS	3
California Academy	2	Los Altos HS	3	Sunset ES	3
Cedarlane	3	Los Molinos ES	1	Valinda School of Academics	2
Del Valle ES	0	Los Robles Academy	0	Valley Alternative	0
Fairgrove Academy	2	Mesa Robles	3	Wedgeworth ES	0
Glen A Wilson HS	4	Nelson ES	2	William Workman HS	2
Grandview, College Preparatory Academy	3	Newton MS	3	Wing Lane ES	2
Grazide ES	3	Orange Grove MS	1	Workman ES	2
Kwis ES	3	Palm ES	2		
La Puente HS	2	Sierra Vista MS	3		

Projects Completed as of August 24, 2023

Cedarlane – Artificial Turf (7/2023)

NEW!



AFTER

Projects In Progress

2023-2024



Projects In Progress as of August 24, 2023

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Workman HS	Phase II Stadium and Baseball Field (Phase I Track & Field and Softball Field Complete)	Complete	Complete	Pending	Pending	Various - Estimate Cost \$18 M	12/2024
Baldwin ES Cedarlane Fairgrove Lassalette	Blacktop Asphalt & Striping	NA	NA	Bidding	Pending	Facilities	12/2023
California ES Cedarlane District Office Bldg C Grazide ES Lassalette Los Altos HS SSC (Sierra Vista) Sparks ES Stimson LC Valley Alt HS – CDS Workman ES 6/27 Workman HS	Reroof Various Buildings	In Progress	NA	Bidding	Pending	Deferred Maint.	01/2024
Wedgeworth	K-5 Permanent School	Complete	Complete	Complete	9/2022	COPS	06/2025
Dibble AS	HVAC Replacement	Complete	NA	Complete	In Progress	Adult Ed	12/2023
Willow AS	HVAC Replacement	Complete	NA	Complete	In Progress	Adult Ed	12/2023
Willow AS	Fire Alarm Installation	Complete	NA	Complete	In Progress	Adult Ed	12/2023

Projects In Progress as of August 24, 2023

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Dibble AS	Fire Alarm Installation	Complete	NA	Complete	In Progress	Adult Ed	12/2023
District Office	Fuel Station Repairs	NA	NA	Complete	Pending	Facilities	09/2023





Projects with Division of State Architect (DSA) Waiting on Approval

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
Los Altos HS	Gym & Locker Room HVAC (65 tons of temporary HVAC units have been installed)	Complete	Pending	Complete	TBD	Approx. 3 months after DSA approval
Kwis Elementary	Baseball Fields (Two Youth)	Complete	Approved (7/5/23)	In Progress	9/2023	8/2024
Center for the Performing Arts	Site Demolition	Complete	N/A	In Progress	08/2023	10/2023
Center for the Performing Arts	Construction of NEW Performing Arts Center with approx. 500 seat capacity	Complete	Pending	Pending	TBD	2/2025

Projects in Design

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
Districtwide	HVAC System Replacements	Pending	Pending	Pending	TBD	TBD
District Office	Portable Installation meeting/flex space	In Progress	NA	Pending	9/2023	1/2024

Projects In Progress of August 24, 2023

Wedgeworth Update

NEW!



Wedgeworth Update

16



The background features a large, semi-transparent watermark of the Unifield School District logo. The logo is circular and contains the text "UNIFIELD SCHOOL DISTRICT" around the perimeter and "1970" at the bottom. In the center is a stylized archway with three smaller arches underneath. A horizontal bar with a green-to-teal gradient is positioned across the top of the page, partially overlapping the logo.

Next Report – September 26, 2023
