




New Middle School @ Polo Club Blvd.

➤ Completed Work:

- Continue CMU in Area B, D, F, E and Second Floor Area C.
- Continue MEP in Area A, C, B, D and installing temporary lights.
- Form ICF in Area A, C and F.
- Poured ICF in Area F.
- Continue to install Storm Drain.
- Continue to drill and grout geothermal wells.
- Set Steel in Area D.
- Poured topping slab in Area A.

➤ Upcoming Work/Look Ahead:

- Continue to install and pour ICF in Area B, D and F.
- Continue MEP in Areas A, C, B, F and D.
- Continue to lay CMU in Area B, D, F, E and Second Floor Area A.
- Continue to stack ICF in Area C Second Floor and Area F in Gym.
- Continue ICF in Area B, D, and F.
- Continue Fire Protection in Area C.
- Continue to drill and grout geothermal wells (could be loud)
- Finish setting steel in Area B and D.
- Finish CMU in Area B and D to hollow core level. CMU in Area F Gymnasium.
- Start roof joist in Area F at Gym.

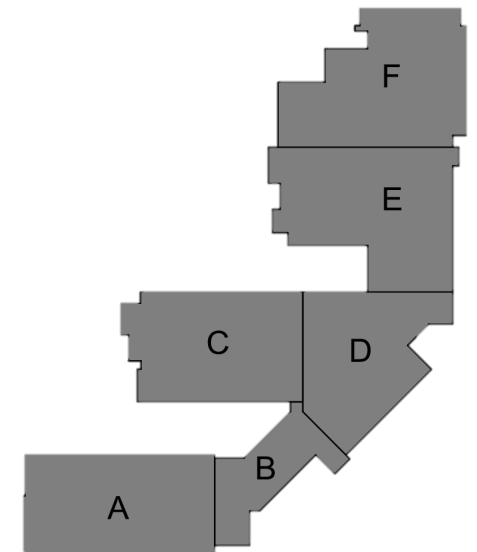



New Middle School @ Polo Club Blvd.

Area A – Concrete Topping Poured on 2nd Floor



Week Ending September 1, 2023

New Middle School @ Polo Club Blvd.

Area C – 2nd Floor CMU and ICF Continues



Week Ending September 1, 2023

New Middle School @ Polo Club Blvd.

Area C – ICF Continues Past 2nd Floor



Week Ending September 1, 2023

New Middle School @ Polo Club Blvd.



Area D – Restroom CMU has started



Week Ending September 1, 2023

New Middle School @ Polo Club Blvd.

Area E – CMU at Kitchen Continues to Roof



Week Ending September 1, 2023

New Middle School @ Polo Club Blvd.

Area F – Gym Locker Room with Temporary Roof



Week Ending September 1, 2023

New Middle School @ Polo Club Blvd.

Area F – Gym Wall Topping out to Roof Level



Week Ending September 1, 2023

New Middle School @ Polo Club Blvd.



Site – Geothermal Drilling Continues



Week Ending September 1, 2023
