


Completed Work:

- Continue CMU in Area B, D, F, E, and Second Floor Area C.
- Continue MEP in Area A, B, C, and D and installing temporary lights.
- Formed ICF in Area C, E and F.
- Poured ICF in Area C, E and F.
- Continue to install Storm Drains
- Set Steel in Area D.
- Poured rest of slab in Area A.
- Continue Sanding CMU in Area A first floor.

Upcoming Work/Look Ahead:

- > Continue to install and pour ICF in Area F on 9/7 at 1pm.
- > Slab pour for stage in Area E on 9/14.
- > Setting rest of hollow core on 9/7 in Area C.
- Continue MEP in Area A, B, C, D and F.
- Continue to lay CMU in Area B, D, F, E and second floor Area A.
- > Continue to stack ICF in Area A second floor, C second floor and F in gymnasium.
- Wreck ICF in Area C Second Floor and F.
- Continue Fire protection in Area C.
- Continue to drill and grout geothermal wells (could be loud)
- Finish setting steel in Area B and D.
- Finish CMU in Area B and D to hollow core level. CMU in Area F Gymnasium.
- > Start roof joists in Area F.





Area A – 2nd Floor Topping Slab Poured






Area A – Setting Door Frames on 2nd Floor





Area C – ICF Continues on 2nd Floor

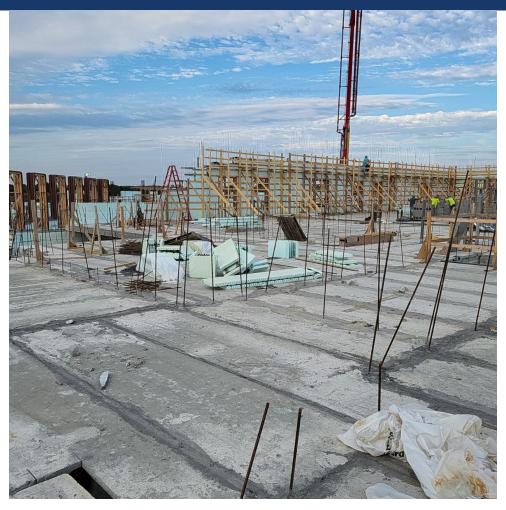



Area D – Cafeteria CMU Continues on Exterior Walls






Area D – Columns at Stairs Installed






Area D – Media Center ICF Base Course installed

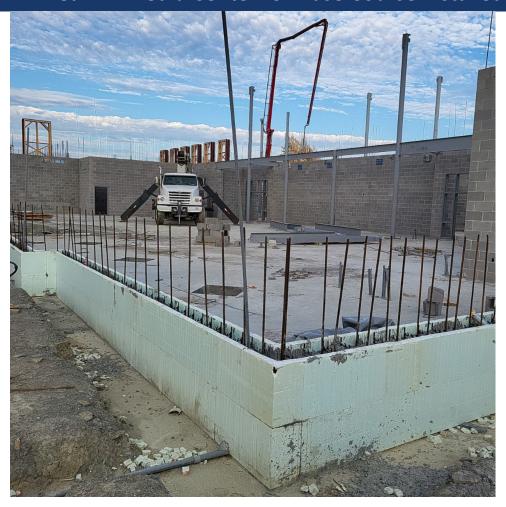



Area F – CMU Wall to Roof on 2 Sides of Gym

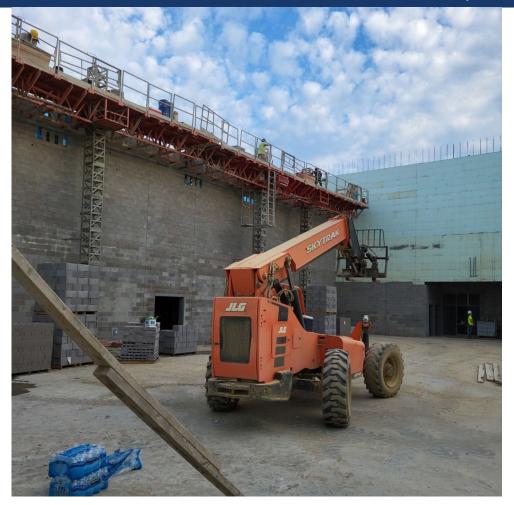



Area F – Gym Locker Room Roof Drain Piping Installed

