




# Mary E. Britton Middle School

## ➤ Completed Work:

- Truss install Complete at Gym
- Truss install Complete at Kitchen and Mechanical Room
- ICF to Mechanical Platform complete in Area A and Area C
- Geothermal Wells (3 Wells remaining)
- Continue Sprinkler and MEP Above Ceiling Rough In
- Site Sanitary Sewer Start
- Start Air Barrier at Gym
- Next ICF Pour on 10/5
- Started Metal Stud Framing Area A and Area C

## ➤ Upcoming Work/Look Ahead:

- Pour ICF Top out at Kitchen Area
- Pour ICF at Cafeteria
- Continue Steel at Area B and Area D
- Platform Area C ready for Hollow Core (10/16/23)
- Continue Excavation for Site Sanitary
- Continue Air Barrier efforts at Area C and F.
- Pour Topping Slab at Area F and Area C
- Continue MEP Rough Ins at many areas
- Continue Site Sanitary
- Start Installing Zone Piping for Geothermal Loops
- **Finish last 3 Geothermal Wells (Could be loud)**

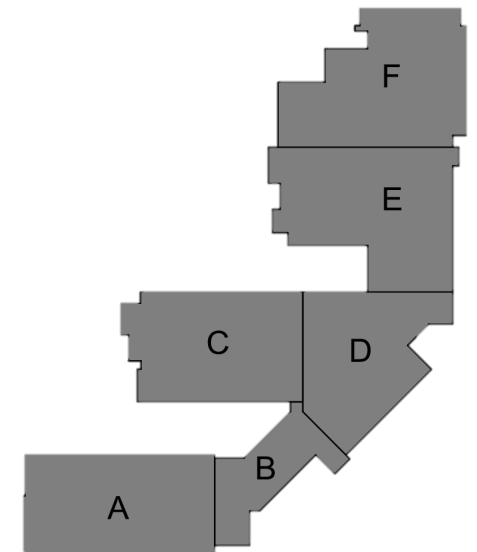

# Mary E. Britton Middle School



Aerial – Overall Site View



Week Ending October 6, 2023



# Mary E. Britton Middle School



## Aerial – Geothermal Drilling Continues



Week Ending October 6, 2023



# Mary E. Britton Middle School



Area A & C – ICF Installed to Mezzanine Level



Week Ending October 6, 2023



# Mary E. Britton Middle School



Area A – CMU and Hollow Metal Frame Setting Continues



Week Ending October 6, 2023

# Mary E. Britton Middle School



Area C – Second Floor Wall Layout has begun



Week Ending October 6, 2023



# Mary E. Britton Middle School



## Area E - Steel Trusses Installed at Kitchen



Week Ending October 6, 2023



# Mary E. Britton Middle School



Area E & F – Hollow Core Planks Installed at Mezzanine



Week Ending October 6, 2023



# Mary E. Britton Middle School



## Area F – Steel Trusses Installed at the Gym



Week Ending October 6, 2023
