

HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



School Site Improvement Projects

Regular Board Meeting
November 9, 2023

Business Services



PROJECT COMPLETE LIST 2023-2024



Site	Item Description	Funding Source	Completed Date
District Wide	National Blue Ribbon Banners	District	10/2023
Valinda	Bottle Filler (MPR)	Facilities	10/2023
Wedgeworth	Bottle Filler (MPR)	Facilities	10/2023
Newton	Exterior Paint Basketball Backboards	Facilities	10/2023
La Puente HS	Pool Gate Closures	Facilities	9/2023
Los Altos HS	Boys Locker Room Wall Repairs	Facilities	9/2023
Equity & Access	Parking Lot Re-Striping	Facilities	9/2023
District Office	Reflooring (Education Services)	Facilities	9/2023
District Office	Wayfinding & Accessible parking in Police Dept.	Facilities	8/2023
Lassalette	Restroom Upgrades	Facilities	8/2023
Wing Lane	K1 & K2 Flooring	Facilities	6/2023
La Puente HS	Weight Room – Flooring and Painting	Facilities	6/2023
Amar	Ramp Repair	Child Development	6/2023
Mesa Robles	Kinder Asphalt	Facilities	6/2023
Nelson ES	Asphalt Slurry and Paint	Site	7/2023
Bixby	Parking Lot Re-Striping	Facilities	7/2023
Del Valle	Parking Lot Re-Striping	Facilities	7/2023
Nelson Elementary	Parking Lot Re-Striping	Facilities	7/2023
Sierra Vista MS	Parking Lot Re-Striping	Facilities	7/2023
Sparks ES	Parking Lot Re-Striping	Facilities	7/2023
Sparks MS	Parking Lot Re-Striping	Facilities	7/2023

PROJECT COMPLETE LIST 2023-2024



Site	Item Description	Funding Source	Completed Date
Fairgrove	3 Bottle Filling Station	Facilities	7/2023
Kwis	3 Bottle Filling Station	Facilities	7/2023
La Puente HS	2 Bottle Filling Station	Facilities	7/2023
Sparks MS	3 Bottle Filling Station	Facilities	7/2023
Wilson HS	3 Bottle Filling Station	Facilities	7/2023
Stimson Building / Adjacent District Equity & Access	Refurbish (Facilities, Flooring, Painting, Ramp, and Roofing)	Facilities	7/2023
Valley HS	C1 & C2 Renovations (Ceiling Tiles, Flooring and Painting)	Facilities	7/2023
Cedarlane	Synthetic Turf	Facilities	7/2023

Projects Completed as of October 26, 2023

District Wide – National Blue Ribbon Banners (10/2023)


NEW!




Projects Completed as of October 26, 2023

District Office – ReFlooring Education Services (9/2023)

NEW!

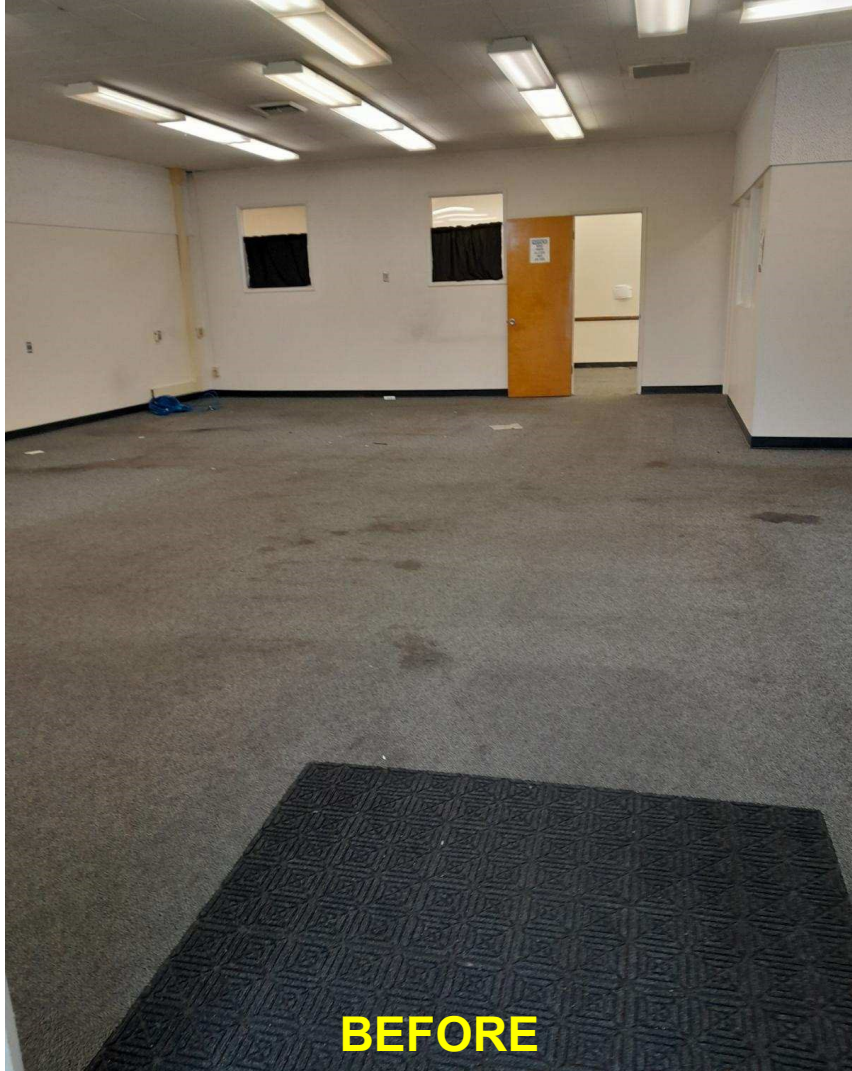

BEFORE

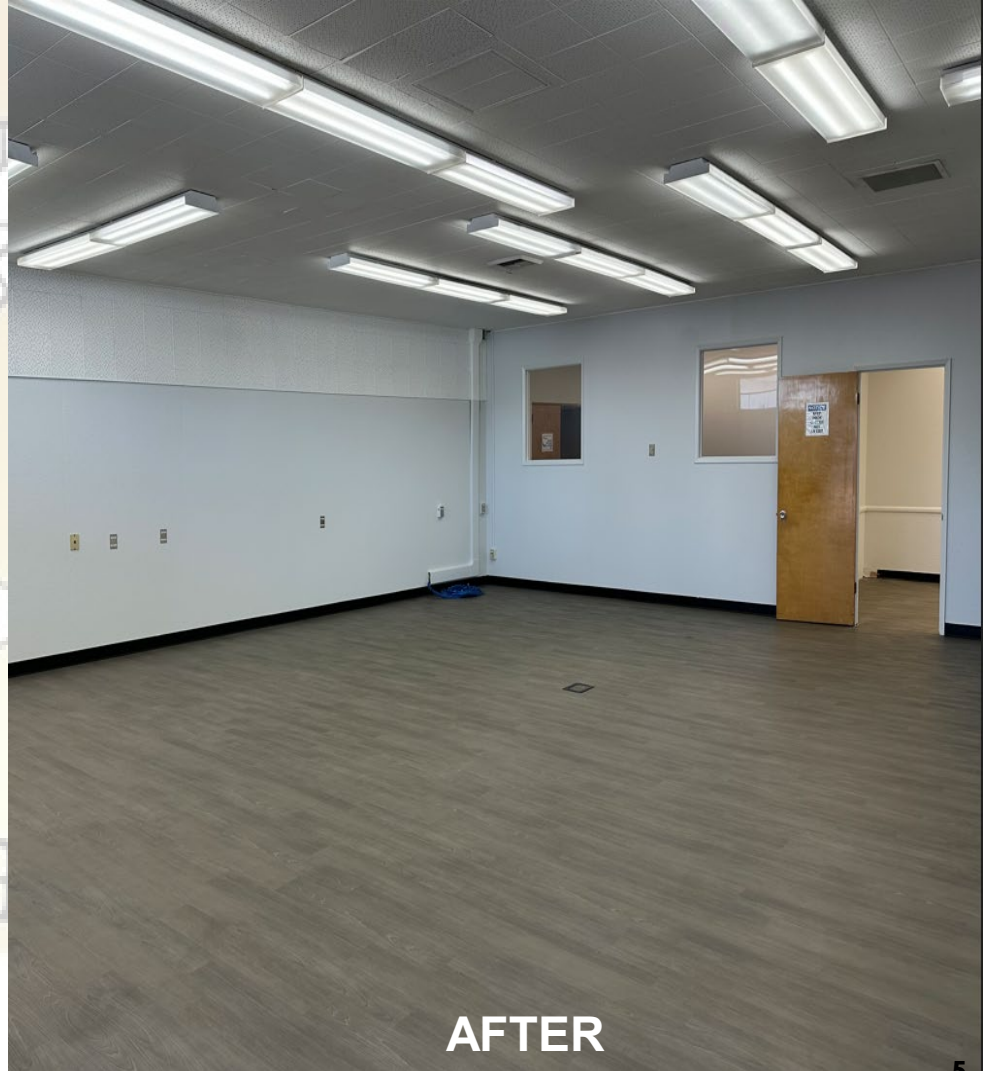

AFTER

Projects Completed as of October 26, 2023

Valinda MPR – Bottle Filler (10/2023)



BEFORE



AFTER



Projects Completed as of October 26, 2023

Wedgeworth – Bottle Filler (10/2023)

NEW!

BEFORE



AFTER



Projects Completed as of October 26, 2023

Equity & Access – Parking Lot Re-Striping

(9/2023)



Projects In Progress

2023-2024



Projects In Progress as of October 26, 2023

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Baldwin ES Cedarlane Fairgrove Lassalette Sparks ES	Blacktop Asphalt & Striping	NA	NA	Bidding	Pending	Facilities	12/2023
Willow AS	Fire Alarm Installation	Complete	NA	Complete	In Progress	Adult Ed	12/2023
Dibble AS	HVAC Replacement	Complete	NA	Complete	In Progress	Adult Ed	12/2023
Willow AS	HVAC Replacement	Complete	NA	Complete	In Progress	Adult Ed	12/2023
Wedgeworth	K-5 Permanent School	Complete	Complete	Complete	In Progress	COPS	06/2025
California ES Cedarlane District Office Bldg C Grazide ES Lassalette Los Altos HS SSC (Sierra Vista) Sparks ES Stimson LC Valley Alt HS – CDS Workman ES 26/27 Workman HS	Reroof Various Buildings	In Progress	NA	Complete	In Progress	Deferred Maint.	01/2024
Workman HS	Phase II Stadium and Baseball Field (Phase I Track & Field and Softball Field Complete)	Complete	Complete	In Progress	Pending	Various - Estimate Cost \$18 M	12/2024

Projects In Progress as of October 26, 2023

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Kwis Elementary	Baseball Fields (Two Youth)	Complete	Complete	In Progress	01/2024	County & TBD	07/2024
Dibble AS	Fire Alarm Installation	Complete	NA	Complete	In Progress	Adult Ed	12/2023
District Office	Fuel Station Repairs	NA	NA	Complete	09/2023	Facilities	11/2023
Center for the Performing Arts	Site Demolition	Complete	NA	Complete	Complete	Adult Ed	10/2023
Center for the Performing Arts	Construction of NEW Performing Arts Center with approx. 500 seat capacity	Complete	Complete	Pending	02/2024	Adult Ed	08/2025
District Office	Portable Installation Meeting/Flex Space	Complete	NA	Pending	11/2023	Facilities	04/2024
Willow AS	Two Story Renovation	Complete	NA	Complete	In Progress	Adult Ed	02/2024
District Office	Warehouse Freezer	Complete	NA	Pending	Pending	Food Services	04/2024



Projects with Division of State Architect (DSA) Waiting on Approval

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
Los Altos HS	Gym & Locker Room HVAC (65 tons of temporary HVAC units have been installed)	Complete	Pending	Complete	TBD	Approx. 3 months after DSA approval
Wing Lane ES	Headstart Portable	Complete	Pending	Pending	TBD	TBD

Projects in Design

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
Districtwide	HVAC System Replacements	Pending	Pending	Pending	TBD	TBD

The background features a large, faded circular logo for Unifield School District. The logo contains the text "UNIFIELD SCHOOL DISTRICT" around the perimeter, "1970" at the bottom, and a central illustration of a building with three arches. A horizontal bar with a green-to-yellow gradient is positioned at the top of the page.

Next Report – January 2024
