




Mary E. Britton Middle School

➤ Completed Work:

- Roofing at Gym started
- ICF in Area C Nearly Complete
- ICF in Area E Cafeteria Continuing
- Stala Frames at Area D are complete
- Masonry at Cafeteria
- Structural Steel at Roof Area C
- Structural Steel at Area D
- Mockup Wall Framing – ACM Panels on Site
- Continue MEP and Sprinkler Rough In

➤ Upcoming Work/Look Ahead:

- Roofing at Gym start
- ICF in Area C to Complete
- Complete CMU in Areas C/D to elevator and lobby stairs
- Set Roof Steel in Area A and Area C with additional erection crew
- Continue Site Sanitary
- Continue Domestic/Fire Lines
- Continue MEP and Sprinkler
- Continue Metal Stud Framing
- Geothermal Underground to building
- Continue Work on Mockup

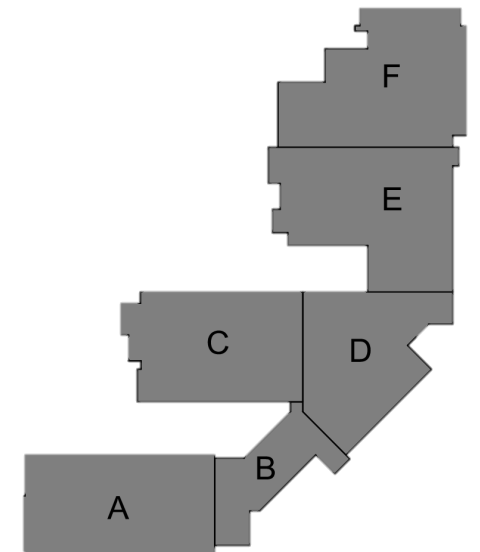

Mary E. Britton Middle School



Area B – Hollow Core at 2nd Floor Media Center



Week Ending November 17, 2023

Mary E. Britton Middle School



Area B – Steel Joists being Installed



Week Ending November 17, 2023

Mary E. Britton Middle School



Area C – ICF End Wall Complete



Week Ending November 17, 2023

Mary E. Britton Middle School



Area C – Mechanical Platform Hollow Core Planks Installed



Week Ending November 17, 2023

Mary E. Britton Middle School



Area E – High Roof Framing Installed at Cafeteria



Week Ending November 17, 2023

Mary E. Britton Middle School



Area E – ICF Installed to Bearing Height



Week Ending November 17, 2023



Mary E. Britton Middle School

Area F – Installing Gym Roof



Week Ending November 17, 2023

Mary E. Britton Middle School



Area F – Mechanical Roof Decking Installed



Week Ending November 17, 2023
