



Kerrville

Independent School District

Bond 2018

2018 Bond Program Update

7.22.19



Project Calendar Expectations



Our Goal: All projects completed on time, under budget, with highest quality

Safety Items

- Package 1 and Package 3 - Vestibules completed (August 2019)

Roofs, HVAC, MEP, et al.

- Package 2 completed (December 2020)

New Construction – HPMS

- July 24th 95% Construction Documents to CM&R
- August 20th Bid Opening
- September 16th GMP for Board Approval
- September 24th Break Ground

- 18+1 Months Construction w/ Final Completion (May 2021)



Summer 2019 Progress

Package 1: Safety


PBK Architects

Door locks (August 9th substantial completion)

Package 1: Safety

PBK Architects

Safety Cameras (August 9th substantial completion)

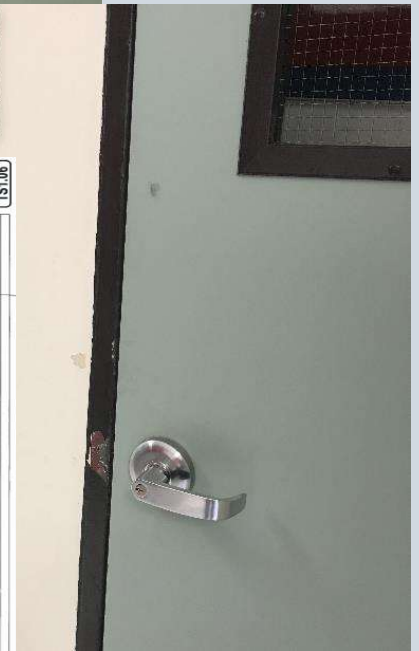

Summer 2019 Progress

Package 3: Secured Vestibules

Huckabee, Inc. Architects

(August 2nd Substantial completion)



Summer 2019 Progress

HPMS
Huckabee, Inc. Architects



More Information To Come

