




ID		Task Mode	Task Name	Duration	Start	Finish	22	T	W	T	F	S	Jun 19, '22	S	M	T	W	T
1			Mobilization	3 days	Wed 6/15/22	Fri 6/17/22												
2			TESC and DEMO	5 days	Mon 6/20/22	Fri 6/24/22												
3			DOE permit shutdown	12 days	Tue 6/28/22	Wed 7/13/22												
4			excavate to subgrade	20 days	Mon 6/27/22	Fri 7/22/22												
5			Concrete flatwork/Curbing	9 days	Mon 7/25/22	Thu 8/4/22												
6			Structural fill and field subgrade	8 days	Mon 7/25/22	Wed 8/3/22												
7			Field drainage and storm	10 days	Thu 8/4/22	Wed 8/17/22												
8			Permeable base,top course and fine grading	10 days	Thu 8/18/22	Wed 8/31/22												
9			Paving and fencing	10 days	Thu 8/18/22	Wed 8/31/22												
10			synthetic turf installation	14 days	Mon 8/29/22	Thu 9/15/22												
11																		



Project: Aberdeen Stewart Field Date: Thu 7/14/22	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

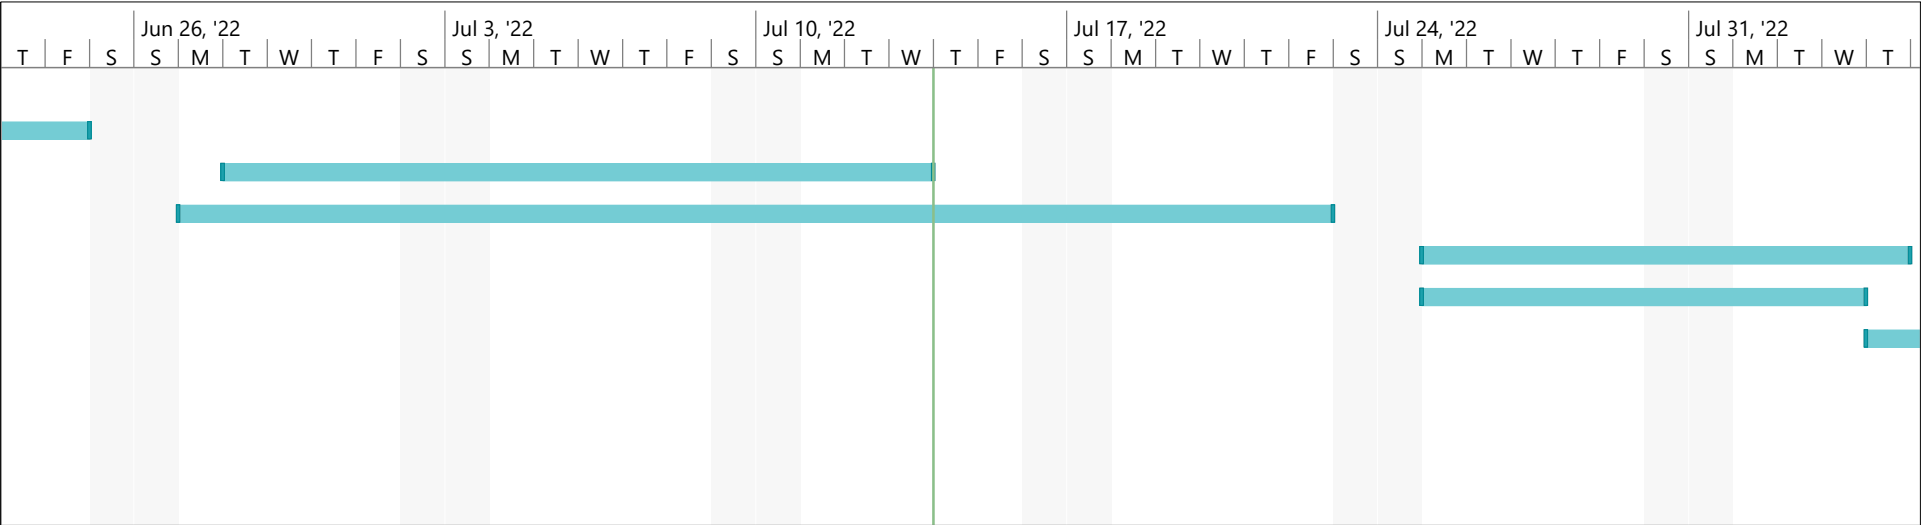

Project: Aberdeen Stewart Field Date: Thu 7/14/22	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

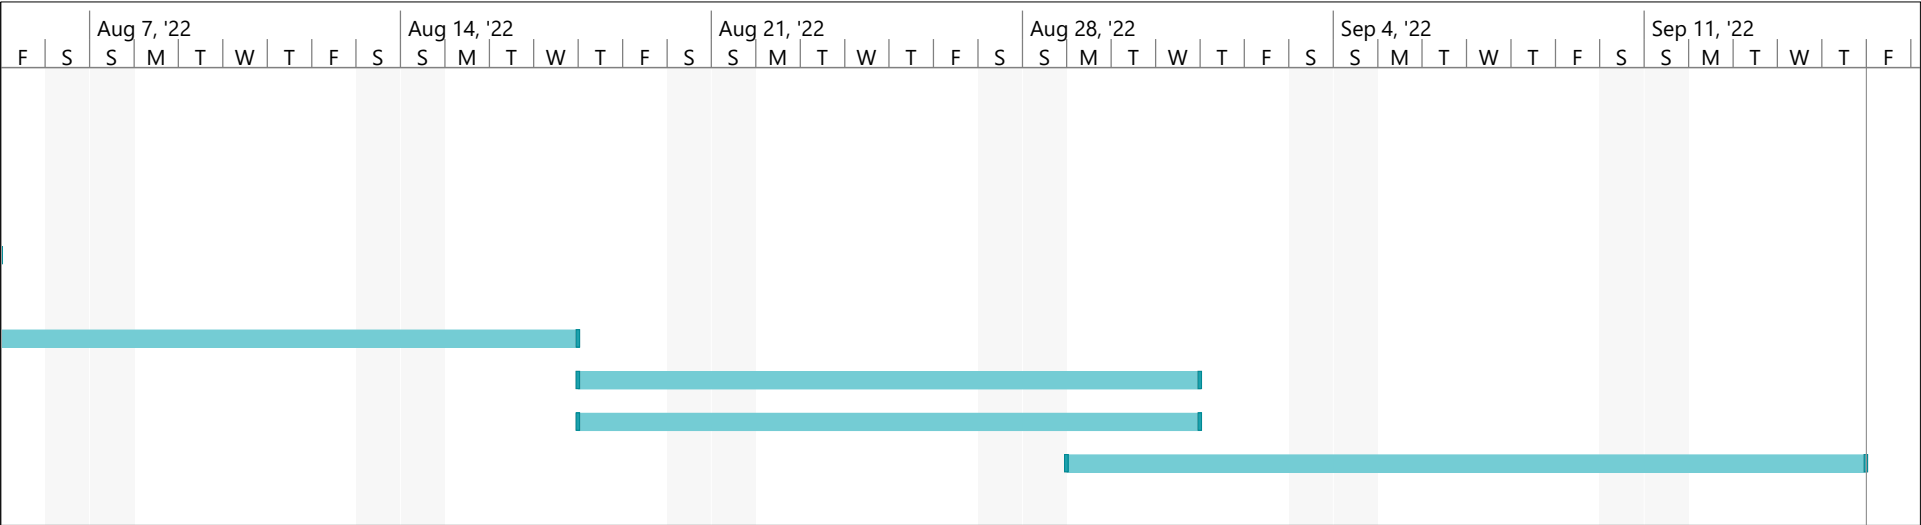

Project: Aberdeen Stewart Field Date: Thu 7/14/22	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			
