

**Financial Report: December 2023** 

#### Overview



66 Projects Underway



\$767,102,930 Current Budget



\$152,646,642 Current Commitments \$57,729,775 Actuals Paid



\$614,456,287 Uncommitted Budget

### **Executive Summary**

#### **Budget Perspective**


- \$2,120,720 in interest earned for October December 2023.
- Energy Trust of Oregon reimbursement received for Five Oaks Seismic in the amount of \$141,198.
- \$400K transferred from Westview HS Modernization to the Office Relocation project.

#### **Schedule Perspective**

• Substantial completion for Aloha HS Office Relocation has been extended to 2/29/2024.

#### **Challenges and Opportunities**

• Subcontractor availability in the local market is showing signs of improvement (greater competition among subcontractors).



## **Overall Financial Summary**

Project Name	Original Project Budget	Contingency Transfers	Other Budget Transfers	Current Budget (C+D+E)	Committed to Date	Paid to Date	Current Percent Paid (H/F)	Uncommitted Budget
01 Beaverton HS Replacement	253,000,000	0	0	253,000,000	19,692,249	9,713,687		233,307,751
01 Beaverton HS Rebuild	253,000,000			253,000,000	19,692,249	9,713,687	3.84%	233,307,751
02 Raleigh Hills Replacement	66,821,753	0	0	66,821,753	61,217,958	4,370,661		5,603,795
02.001 Raleigh Hills Replacement	66,821,753			66,821,753	61,217,958	4,370,661	6.54%	5,603,795
03 Allen Transportation Replacement	11,000,000	0	0	11,000,000	20,000	0		10,980,000
03 Allen Transportation Replacement	11,000,000			11,000,000	20,000		0.00%	10,980,000
04 Physical Education & Athletics	17,500,000	0		17,500,000	285.244	152.972		17.214.756
04.001 PhysEd/Athletics: Barnes Gym & Cafeteria	7,500,000			7,500,000			0.00%	7,500,000
04.002 Southridge HS SB/BB Artificial Turf	2,000,000		1,500,000	3,500,000	285,244	152,972	4.37%	3,214,756
04.003 Aloha HS SB/BB Artificial Turf	2,000,000		, , ,	2,000,000	,	,	0.00%	2,000,000
04.004 Westview HS SB/BB Artificial Turf	2,000,000			2,000,000			0.00%	2,000,000
04.005 Beaverton HS SB/BB Artificial Turf	2,500,000			2,500,000			0.00%	2,500,000
05 Additional Classrooms	17.500.000	0	1,089,858	18,589,858	4,175,004	3,281,578		14,414,854
05.001 Sato Classroom Addition	3,000,000		-135,196	2,864,804	2,864,804	2,548,379	88.95%	0
05.002 Oak Hills Classroom Addition	2,500,000		1.000.000	3,500,000	27.000	_,	0.00%	3,473,000
05.003 Stoller Gym & Added Classrooms	12,000,000		225.054	12,225,054	1,283,200	733,200	6.00%	10.941.854
06 Office Relocations	10,000,000	985,000	400.000	11,385,000	6,997,907	2,426,147	0.0070	4,387,093
06.001 AHS Office Relocation	6,000,000	985,000	400,000	6,985,000	6,549,261	2,283,768	32.70%	435,739
06.002 WHS Office Relocation	2,500,000	303,000	400.000	2,900,000	424,646	142,379	4.91%	2.475.354
06.003 Cooper Mtn. Office Relocation	1,500,000		+00,000	1,500,000	24,000	142,013	0.00%	1,476,000
07 Athletic Facilities	6,000,000	0	0	6,000,000	668,847	59,866	0.00%	5,331,154
07.001 Athletic Facilities: WHS Pride Plaza	2.000.000	0	U	2,000,000	668.847	59,866	2.99%	1.331.154
07.002 Athletic Facilities: AHS	2,000,000			2,000,000	000,047	59,600	0.00%	2.000.000
07.002 Athletic Facilities: SRHS	2,000,000			2,000,000			0.00%	2,000,000
	1			1			0.00%	, ,
08 Outdoor Learning	5,000,000	0	-1,000,000	4,000,000	71,715	31,393	0.4.40/	3,928,285
08.001 Outdoor Learning: Springville	1,000,000			1,000,000	71,715	31,393	3.14%	928,285
08.002 Outdoor Learning: Aloha Huber	2,000,000			2,000,000			0.00%	2,000,000
08.003 Outdoor Learning: Oak Hills	1,000,000		-1,000,000	0			0.00%	0
08.004 Outdoor Learning: McKinley	1,000,000			1,000,000			0.00%	1,000,000
09 Seismic Upgrades	40,000,000	0		60,161,827	13,837,569	6,864,917		46,324,258
09.001 Five Oaks Seismic	6,600,000		6,200,000	12,800,000	12,117,280	6,167,948	48.19%	682,720
09.002 Mtn. View Seismic	6,600,000		13,961,827	20,561,827	1,591,344	629,372	3.06%	18,970,483
09.003 Meadow Park Seismic	6,600,000			6,600,000			0.00%	6,600,000
09.004 Cedar Park Seismic	6,600,000			6,600,000			0.00%	6,600,000
09.005 Whitford Seismic	6,600,000			6,600,000			0.00%	6,600,000
09.006 Highland Park Seismic	6,600,000			6,600,000			0.00%	6,600,000
09.007 Seismic Planning	400,000			400,000	128,945	67,596	16.90%	271,055
10 School Modernization	24,000,000	0	-1,433,881	22,566,119	4,380,691	3,340,500		18,185,428
10.001 Aloha HS Modernization	1,935,022		-69,326	1,865,696	124,721	9,367	0.50%	1,740,976
10.003 Barnes Modernization	584,050			584,050	7,197	7,197	1.23%	576,853
10.004 Beaver Acres Modernization	529,569		-18,973	510,596	65,025	16,525	3.24%	445,571
10.008 Cedar Mill Modernization	285,739			285,739	67,519	28,057	9.82%	218,220
10.013 Elmonica	530,331		-19,000	511,331	18,467	11,742	2.30%	492,864
10.016 Fir Grove	409,178			409,178	39,446	30,766	7.52%	369.732
10.019 Greenway	334,886			334,886	127,259	20,115	6.01%	207,627
10.022 ISB	630,149		-22,576	607,573	52,373	8.696	1.43%	555,200
10.025 McKay	297,168		,o	297,168	46,368	19,324	6.50%	250,800
10.027 Meadow Park	659,104		-23,614	635,490	32.266	31,986	5.03%	603.224
10.028 Merlo Station	62,482		20,014	62,482	19,700	460	0.74%	42.782
10.029 Montclair	222,495			222,495	73,328	50.794	22.83%	149,167
10.029 Montein 10.030 Mountain View	984,084		-844,084	140,000	2,327	2,327	1.66%	137,673
10.034 Ridgewood	282,691		-044,084	272,563	50,385	2,327	8.01%	222,178
10.034 Ridgewood 10.041 Sunset	1,459,934		-10,128 -52,306	1.407.628	170,820	170.820	12.14%	1.236.808
			-52,306	1 2 12 2				1
10.043 West TV 10.044 Westview	236,211		-443,296	236,211 765,188	12,450 93,800	1,745	0.74%	223,761
	, , .		-443,296					<u>671,388</u>
10.045 Whitford	866,359		000.005	866,359	28,382	1,515	0.17%	837,977
10.046 Modernization Tech/AV	2,999,995		630,605	3,630,600	3,299,759	2,821,729	77.72%	330,841

10.047 Modernization Planning	100,000			100,000	49,100	22,511	22.51%	50,900
11 Deferred Maintenance	120,000,000	0	-19,353,000	100,647,000	14,387,465	4,471,318		86,259,535
11.002 SRHS HVAC Upgrades	4,000,000		5,000,000	9,000,000	6,397,895	812,379	9.03%	2,602,105
11.003 Sunset HS Track	2,000,000		455,640	2,455,640	2,322,743	2,205,702	89.82%	132,897
11.004 Mercury Gym Floor Replacements	2,000,000		-916,000	1,084,000	136,347	131,510	12.13%	947,654
11.005 Capital Center HVAC	4,000,000		336,000	4,336,000	4,017,181	314,820	7.26%	318,819
11.006 MS & SRHS Stage Improvements	20,000			20,000	14,500	14,500	72.50%	5,500
11.007 Landscape Assessment	200,000			200,000	36,000	25,156	12.58%	164,000
11.008 Maintenance Repair Projects 22/23	1,000,000			1,000,000	892,978	687,974	68.80%	107,022
11.009 ISB Boiler	135,000		-25,599	109,401	109,401	109,401	100.00%	0
11.010 Capital Center Paging	741,000			741,000	66,575	23,247	0.00%	674,425
11.012 SRHS Stadium Turf Replacement	1,000,000			1,000,000	20,000	2,700	0.27%	980,000
11.013 WHS Stadium Turf Replacement	1,000,000			1,000,000			0.00%	1,000,000
11.014 West TV HVAC	100,000			100,000	45,065	8,425	8.43%	54,935
11.015 Terra Linda Roof Replacement								0
11.017 Aloha HS HVAC Upgrade	35,000			35,000	30,500		0.00%	4,500
11.018 Kinnaman Cafe Roof								0
11.019 West TV Café Roof								0
11.020 Dishwasher Replacements	200,000			200,000	13,428	3,511	1.76%	186,572
11.022 Capital Center Café Roof								0
11.023 Sexton Mountain ES Drainage	200,000			200,000	30,000		0.00%	170,000
11.501 5th St. South Catch Basin	11,000			11,000	8,475	8,475	77.05%	2,525
11.502 Stoller Freezer	526,000			526,000	62,478		0.00%	463,522
11.800 Maintenance Repair Projects 23/24	2,000,000			2,000,000	142,500	82,117	4.11%	1,857,500
Uncategorized Deferred Maintenance	41,400			41,400	41,400	41,400	100.00%	0
Unallocated	100,790,600		-24,203,041	76,587,559				76,587,559
12 Security Upgrades	10,000,000	0	0	10,000,000	865,065	522,115		9,134,935
12.001 Security Assessment	200,000			200,000	179,924	136,417	68.21%	20,076
12.002 HS Card Readers	1,000,000			1,000,000	277,392	108,877	10.89%	722,608
12.003 Security Cameras	3,000,000			3,000,000	287,499	276,821	9.23%	2,712,501
12.004 Paging Improvements	150,000			150,000	120,250		0.00%	29,750
Unallocated	5,650,000			5,650,000			0.00%	5,650,000
13 NS Upgrades	5,000,000	0	0	5,000,000	116,435	55,585	0.000/	4,883,565
13.001 BA Kitchen	750,000			750,000	11.000		0.00%	750,000
13.002 Bottle Fillers	1,360,000			1,360,000	44,990	55 505	0.00%	1,315,010
13.003 Greenway Kitchen Improvements	777,144	-	-	777,144	71,445	55,585	0.00%	705,699
14 Critical Equipment	7,000,000	0	0	7,000,000	1,690,301	1,519,232	40.000/	5,309,699
14.001 CE - Copiers	1,500,000			1,500,000	270,937	270,937	18.06%	1,229,063
14.002 CE - Athletic Director	1,000,000			1,000,000	103,342	102,996	10.30%	896,658
14.003 CE - Band Equipment	2,500,000			2,500,000	1,213,790	1,043,067	41.72%	1,286,210
14.004 CE - Maint Equipment	1,000,000			1,000,000	100.000	100.000	0.00%	1,000,000
14.005 CE - Furniture	1,000,000	-		1,000,000	102,232	102,232	10.22%	897,768
15 Management & OH	50,000,000	0	0	50,000,000	8,635,747	8,615,202	400.000/	41,364,253
15.001 Year 1 - 22/23 Bond Program Management	5,731,850			5,731,850	5,731,850	5,731,850	100.00%	0
15.002 Year 2 - 23/24 Bond Program Management	7,000,000	-	-	7,000,000	2,903,897	2,883,352	41.19%	4,096,103
16 Bus Replacements	10,000,000	0	0	10,000,000	5,500,000	2,573,287	05 700/	4,500,000
16 Bus Replacements	10,000,000			10,000,000	5,500,000	2,573,287	25.73%	4,500,000
17 Technology	44,000,000	0	0	44,000,000	10,057,316	9,684,185	00.049/	33,942,684
17 Technology	44,000,000			44,000,000	10,057,316	9,684,185	22.01%	33,942,684
18 SPED Upgrades	2,000,000	0	0	2,000,000	47,129	47,129	E0.070/	1,952,871
18.001 Rock Creek ISC Modifications	90,000	-		90,000	47,129	47,129	52.37%	42,871
19 Kinder Upgrades	1,000,000	0	0	1,000,000			0.000/	1,000,000
19 Kinder Upgrades	1,000,000	00.000.450	(0= 400	1,000,000			0.00%	1,000,000
20 Contingency	43,000,000	23,296,176	135,196	66,431,372				66,431,372
Grand Totals	742,821,753	24,281,176	0	767,102,929	152,646,642	57,729,775	7.53%	614,456,287

#### **Financial Statement**

	Revenue	
Bond Proceeds	\$723,000,000	*Bond sale amount
OSCIM Grant	\$8,000,000	*Included in Original Budget for Raleigh Hills
Raleigh Hills funding from 2014 Bond	\$11,821,753	*Included in Original Budget for Raleigh Hills
2022 Bond Sale Premium	\$16,637,675	
Interest on Investments	\$7,481,404	*Interest earned Q4 2023 - \$2,120,720
Energy Trust of Oregon Reimbursements	\$162,098	
SB1149 Reimbursements	\$0	
Total Revenue		\$767,102,930
	Expenditures t	o Date
Bond Issuance Costs	\$1,910,446	
Salaries & Overhead Expenses	\$6,704,756	
Building Improvements	\$35,337,868	
Equipment Purchases	\$13,776,704	
Total Expenditures		\$57,729,77
Bond Cash Balance		\$709,373,15

#### **Contingency Transfers**

Starting Balance Current Balance

\$ 43,000,000.00 \$ 66,431,372.46


	. , ,
Purpose	Amount
Bond Premium	\$16,637,675.00
AHS Office Relocation - Early	\$2 500 00

Budget Change No.	Date	From	То	Purpose	Amount
1	Sep-22		2022 Bond Contingency	Bond Premium	\$16,637,675.00
2	1/11/2023	ETO Incentive Checks	2022 Bond Contingency	AHS Office Relocation - Early Design Assistance	\$2,500.00
3	1/26/2023	ETO Incentive Checks	2022 Bond Contingency	Raleigh Hills - Early Design Assistance	\$5,000.00
4	1/26/2023	ETO Incentive Checks	2022 Bond Contingency	Raleigh Hills - Daylighting Study	\$8,400.00
5	1/26/2023	ETO Incentive Checks	2022 Bond Contingency	BHS Replacement - Early Design Assistance	\$5,000.00
6	3/6/2023	2022 Bond Contingency	Aloha HS Office Relocation		-\$985,000.00
7	4/30/2023		2022 Bond Contingency	Interest Earned to Date	\$1,935,704.00
8	5/31/2023		2022 Bond Contingency	Interest Earned	\$378,729.00
9	6/30/2023		2022 Bond Contingency	Interest Earned	\$2,051,052.00
10	9/30/2023		2022 Bond Contingency	Interest Earned	\$995,198.82
11	11/30/2023	05.001 Sato Classroom Addition	2022 Bond Contingency	Project Savings	\$135,196.00
12	12/31/2023		2022 Bond Contingency	Interest Earned - Q4 2023	\$2,120,720.09
13	12/31/2023	ETO Incentive Checks	2022 Bond Contingency	Five Oaks Seismic - Roof Insulation	\$141,197.55

Other Budget Transfers									
Budget Change No.	Date	From Master Project	Subproject	To Master Project	Subproject	Amount			
1	6/28/2022	Deferred Maintenance	N/A	Seismic	9.001 Five Oaks Seismic and Roof	\$4,000,000.00			
2	11/29/2022	Deferred Maintenance	N/A	Deferred Maintenance	11.002 SRHS HVAC Upgrades	\$5,000,000.00			
3	12/1/2022	Deferred Maintenance	N/A	Deferred Maintenance	11.005 Capital Center HVAC	\$336,000.00			
4	1/20/2023	Deferred Maintenance	N/A	Seismic	9.002 Mountain View Seismic	\$3,300,000.00			
5	2/1/2023	Deferred Maintenance	N/A	Seismic	9.001 Five Oaks Seismic and Roof	\$1,284,000.00			
6	2/1/2023	Deferred Maintenance	11.004 Mercury Gym Floor Replacements	Seismic	9.001 Five Oaks Seismic and Roof	\$916,000.00			
7	3/6/2023	Outdoor Learning	08.003 Outdoor Learning: Oak Hills	Additional Classrooms	5.002 Oak Hills Classroom Addition	\$1,000,000.00			
8	4/30/2023	Deferred Maintenance	11.013 WHS Stadium Turf Replacement	Athletic Facilities	07.001 Athletic Facilities: WHS Pride Plaza	\$1,000,000.00			
9	6/30/2023	School Modernizations	Reallocation of Modernization funds	School Modernizations	10.046 Modernization Tech/AV	\$630,605.00			
10	7/31/2023	School Modernizations	10.040 Stoller Modernization	Additional Classrooms	5.003 Stoller Gym & Added Classrooms	\$225,054.00			
11	8/10/2023	School Modernizations	10.030 Mountain View Modernization	Seismic	9.002 Mountain View Seismic	\$808,827.00			
12	8/30/2023	Deferred Maintenance	N/A	Seismic	9.002 Mountain View Seismic	\$9,853,000.00			
13	9/30/2023	Athletic Facilities	7.001 WHS Pride Plaza	Deferred Maintenance	11.013 WHS Stadium Turf Replacement	\$1,000,000.00			
14	10/15/2023	Deferred Maintenance	11.009 ISB Boiler (Project Complete)	Deferred Maintenance	N/A	\$25,599.00			
15	11/20/2023	Physical Education & Athlet		Physical Education & Atl	04.002 Southridge HS SB/BB Artificial Turf	\$1,500,000.00			
16	12/31/2023	School Modernization	10.044 Westview HS Modernization	Office Relocations	6.002 Westview HS Office Relocation	\$400,000.00			

#### 2022 Bond Project Status Report Schedule

	2022	2023	2024	2025	2026	2027	2028	2029	
Project	JJASON	D J F M A M J J A S O N	D J F M A M J J A S O N E	JFMAMJJASOND	J F M A M J J A S O N D	JFMAMJJASOND	JFMAMJJASOND	JFMAMJJASOND	Current Status
01 Beaverton HS Rebuild									50% CD
02.001 Raleigh Hills ES Replacement									Permitting
03 Allen Transportation Replacement									Not Yet Started
04.001 Barnes Gym + Cafeteria									Not Yet Started
04.002 Southridge HS SB/BB Artificial Turf									100% CD
05.003 Stoller MS Gym + Added Classrooms									80% CD
06.001 Aloha HS Office Relocation	1								50% Construction
06.002 Westview HS Office Relocation									50% CD
07.001 Athletic Facilities: Westview HS Pride Plaza									100% DD
08.001 Outdoor Learning: Springville K8									100% CD
09.001 Five Oaks MS Seismic									50% Construction
09.002 Mountain View MS Seismic									80% CD
10.001 Aloha HS Modernization									Planning
10.003 Barnes Modernization									
10.004 Beaver Acres Modernization									Planning
10.013 Elmonica Modernization									Planning
10.022 ISB Modernization									Planning
10.041 Sunset HS Modernization									Planning
10.044 Westview HS Modernization									Planning
10.045 Whitford Modernization									Planning
11.002 Southridge HS HVAC Upgrades									20% Construction
11.003 Sunset HS Track									Substantially Complete
11.004 Mercury Gym Floor Replacements									20% Construction
11.005 Capital Center HVAC									Permitting
11.010 Capital Center Paging									80% CD
11.012 Southridge HS Stadium Turf									Planning
11.013 Westview HS Stadium Turf									100% DD
11.014 West TV HVAC									Planning
11.015 Terra Linda Roof									Planning
11.017 Aloha HS HVAC									Planning
11.018 Kinnaman Café Roof									Planning
11.502 Stoller Freezer									Planning
12.002 HS Card Readers									Planning
13.002 Bottle Fillers									Planning
13.003 Greenway Kitchen Improvements									100% CD
				1					1

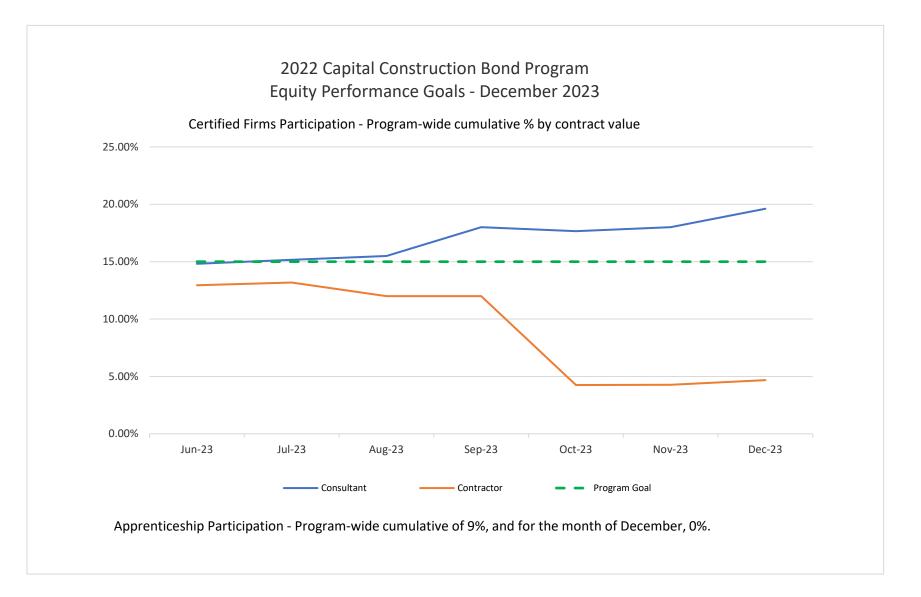Design Permitting Construction 

## **Project Updates**

### **Beaverton HS Rebuild**

- 50% construction documents have been submitted; design review scheduled for January.
- Merle Davies demolition permit, site grading and erosion control submitted and in review. Clean Water Services is now requiring a full 1200c vs. 1200cn erosion control permit.
- Early Work Amendment #5 was approved at December board meeting in the amount of \$2,934,848.
- Guaranteed Maximum Price proposal expected in 1/2024.

- Project team is working on revisions to site development permit to accommodate contractor parking and other minor revisions to the building and site.
- Leadership is working on athletic site use coordination for displaced programs. Top 5 hard hat stickers:



# **Raleigh Hills ES Rebuild**

- Bidding period has closed and Pence is in the process of confirming bids, results will be available end of January.
- Site plumbing permit has been approved.
- Construction start: Summer 2024.



### **Stoller MS**

#### Aux Gym + Classroom Addition

- Grading permit application submitted.
- 100% Construction Documents due 2/2024.
- Early Work Amendment for generator and electrical gear is pending execution.
- Targeting Guaranteed Maximum Price Amendment for January board meeting.
- Construction Start: Late Spring 2024.
- Substantial Completion: 3/2025.



### Aloha HS

#### **Office Relocation**

- Vapor barrier installed on roof.
- Interior framing underway; concrete stairs and ramp poured.
- Furniture Fixtures & Equipment has been ordered; Installation early 3/2024.
- Concrete layout and quality issues were discovered by BSD team which required remedial work. Substantial completion delayed as a result.
- Substantial Completion: 2/29/2024 (Previously 1/30/2024).
- Occupancy: 3/2024. (Previously 2/2024)



### **Westview HS**

#### **Office Relocation**

- CM/GC cost estimates received and are on budget.
- Tracking Guaranteed Maximum Price Amendment for February board meeting.
- Transferring \$400k from modernization funds.
- Design: 1/2023 to 3/2024.
- Construction Start: Summer 2024
- Substantial Completion: 8/2024



### **PE & Athletics**

#### Westview HS Pride Plaza

- Cost estimate received came in over budget; Value Engineering underway.
- Removing \$15K in concession equipment and building being shortened by 8 feet.
- Guaranteed Maximum Price Amendment expected 2/2024
- Substantial Completion: 9/2024.


#### Southridge HS Softball/Baseball Artificial Turf

- Design complete; construction documents have been submitted to Field Turf for pricing.
- We are required to add significant detention and treatment facilities that have increased the cost of the project.
- Field Turf has begun pre-construction services with Cameron McCarthy to complete design and provide cost information.

## **Outdoor Learning**

#### Springville ES

- Design is complete.
- Field Turf contract approved in the amount of \$712,592.



# **Seismic Upgrades**

#### Mt. View MS

- Guaranteed Maximum Price Amendment approved in the amount of \$17,161,251.
- Will need three portables for swing space.
- Electrical investigation over winter break on lack of groundwire at distribution panels. May need to order switchgear with GFI breakers.
- Electrical submittals pending due to long-lead times.

#### **Five Oaks MS**

- Energy Trust of Oregon reimbursement received in the amount of \$141,198.
- 2024 Construction:
  - Begin 5/2024
  - Substantial Completion 8/2024
  - Final Completion: 9/2024

#### Modernization projects currently underway:

- Aloha HS: Kickoff meeting held for counseling office and gym/auditorium restroom renovations.
- Barnes ES: Bilingual wayfinding, sensory room, tack boards in new wing, and carpet replacement in library/B-wing in planning phase. Library tables and chairs pending district standard. Fencing/gate completed.
- Cedar Mill ES: Student restrooms near library in planning/design. Gym storage and staff room/restrooms flooring completed over winter break. Gym curtains scheduled for spring break.
- Elmonica ES: Pre-K playground in planning.
- Fir Grove ES: Pre-K playground and main office carpeting in planning/design. Exterior gate for pre-K playground completed.

Beaver Acres ES: New track in design.
Washington County cancelled pre-app conference as they determined it wasn't required.







• Greenway ES: Library furniture was installed over winter break. Woodburn Construction awarded contract for main office update.

- ISB: Stage classroom masking curtains completed over winter break. Relocation of weight/exercise room, installation of washer/dryer, update to gym sound system, and new cafeteria stage microphones in planning/design. Installation of owner provided projector and speakers in cafeteria completed.
- McKay ES: Library update and office remodel in design. Woodburn Construction has been awarded contract for office update. Classroom furniture pending district standard.
- Montclair ES: Music room storage and magnetic marker boards installation in multiple classrooms completed. Covered walkway in design/permitting. Classroom furniture pending district standard.

- Mtn. View MS: Exterior signage complete, Tech/AV underway.
- Ridgewood ES: Office upgrade and storage project in planning/design.
- Westview HS: Gym AV in planning/design. \$400K transferred to Westview HS Office Relocation project to enhance the counseling suite and add a community meeting room. Engage page is live for hallway reimaging.
- West TV ES: Carpet and window coverings in some classrooms in planning/design. Reader board update and gym projector completed. Classroom furniture pending district standard.
- Whitford MS: Window coverings, folding wall for counselors' offices, bilingual signage and gym/hallways rebranding in planning. Classroom furniture pending district standard. New mascot completed.

• Sunset HS: Update of digital lab iMacs completed. Cafeteria/commons reimaging in planning. A-Hall commons furniture pending district standard.



### **Deferred Maintenance**

#### Southridge HS HVAC

- Long lead submittals are complete and Roof Top Units (RTUs) have been ordered.
- Substantial Completion: 9/2024.

#### **Capital Center HVAC**

• RTUs have been ordered and submittals are being reviewed.

#### **Capital Center Paging**

• 100% Construction Documents due in January.

#### Southridge HS Stadium Turf

- Design is underway.
- Substantial Completion: 9/2024.

#### Westview HS Stadium Turf

- Resurfacing of the track has been added to the project scope.
- Cost estimates and schedules are being developed.
- First two home games will be played at an alternate field.
- Construction Start: 6/2024.

# **Security Upgrades**

#### **High School Card Readers**

- A/E proposal requested to design card readers at nine schools to facilitate dark drops at off hours at the request of Nutrition Services. Layout and cost estimates being generated.
- Substantial Completion: 9/2024.

#### **Security Systems**

• Preparing a Request for Proposal to select a security vendor for the remainder of the bond.

### **Nutrition Services**

#### **District-wide Water Bottle Fillers**

- Design is underway.
- R&W Engineering has been contracted for engineering services.

#### Greenway ES Kitchen Improvements

- 100% Construction Documents complete.
- Contract approved for Petra Design Build in the amount of \$288,530.

#### **Contact: Gabby Urenda, Bond Communications Specialist**

Email: gabby\_urenda@beaverton.k12.or.us Phone: 503-356-4611

#### **Contact: Aaron Boyle, Administrator for Facilities Development**

Email: aaron\_boyle@beaverton.k12.or.us Phone: 503-356-4364
