

Citizen's Bond Oversight Committee

January 24, 2024








New Gymnasium

30,297 SF

- 3-Court Gymnasium
- Lobby and Interior Corridors
- (5) Team Rooms
- (2) Sets of Gendered Restrooms
- (4) Gender Neutral Restrooms
- Concessions
- Storage

Add Alternate Weight Room 3,065 SF


Total 33,362 SF

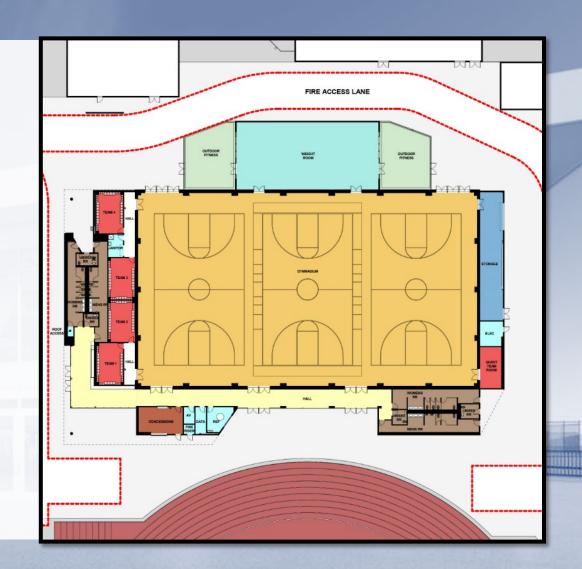




New Gymnasium Weight Room



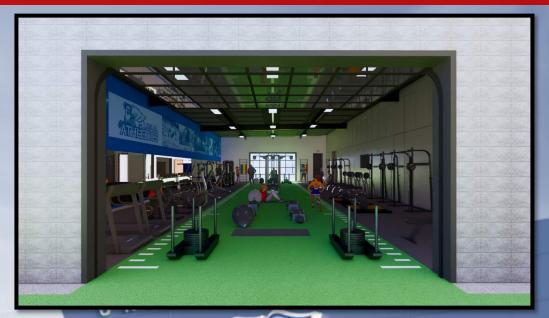





Weight Room - 3,065 SF

- (2) Overhead Roll Up Doors
- Indoor/Outdoor Synthetic Turf




New Gymnasium Location and Logistics Plan





Portable Relocation Site Plan and Schedule




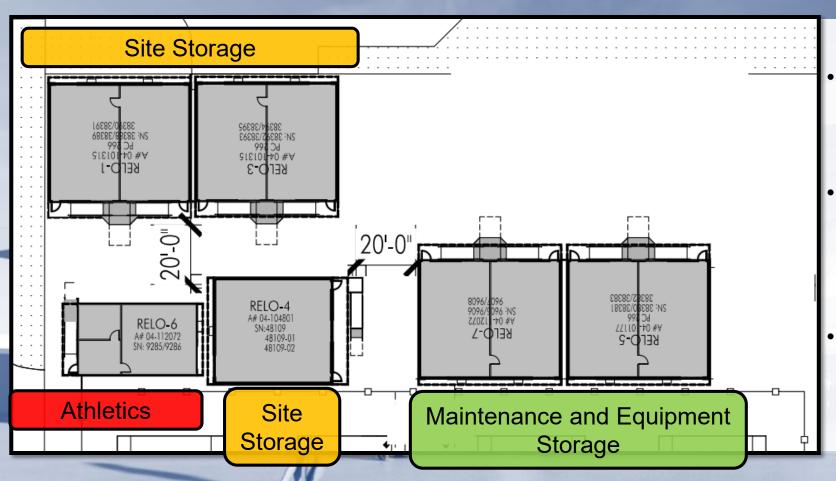

- An over-the-counter review with DSA is scheduled for November 30th
- Relocation of portable classrooms and containers scheduled to take place over Winter Break
- Utility infrastructure and setting of portable classrooms scheduled for January 2024



New Gymnasium Schedule

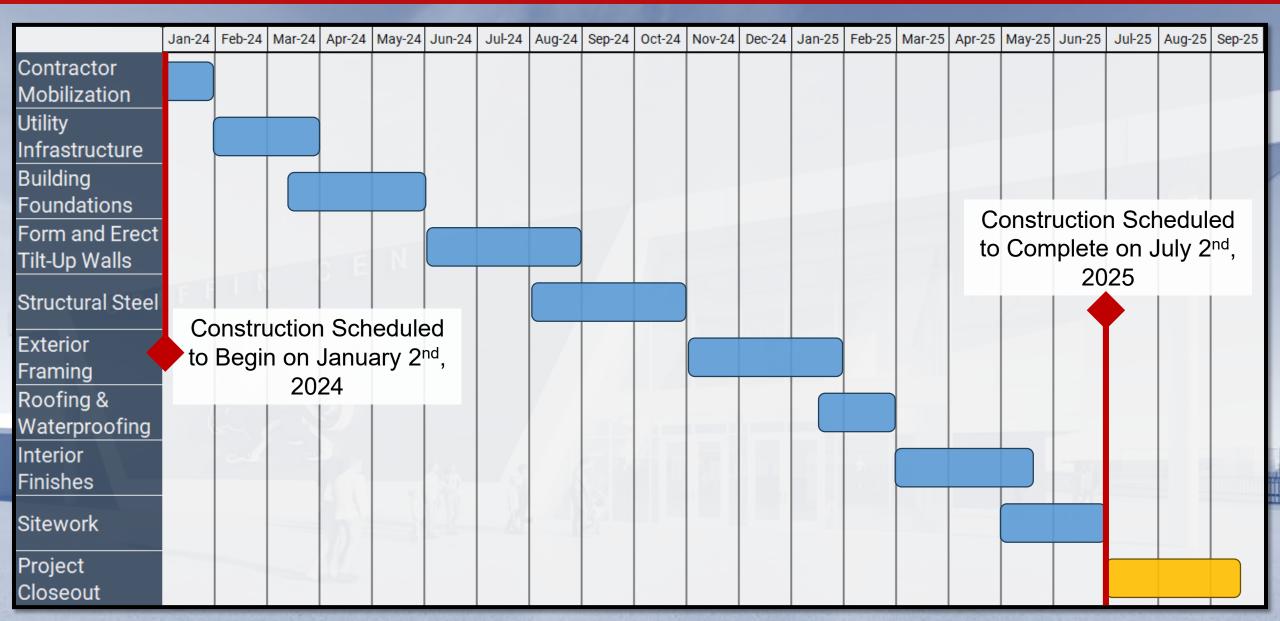





Previous Project Estimate – Board Workshop 9/20/2022

Second Gymnasium Comprehensive **Estimate** Estimated Cost and Estimated Cost Design Contingency Contingency Contingency Soft Costs & 3,586,774 Planning \$ 2.739.278 \$ 847.496 22,229,166 Construction Costs \$ 20,208,333 2.020.833 \$ TOTAL PROJECT 25,815,940 22,947,611 \$ 847.496 \$ 2.020.833 PHASE 2 - Weight Room \$ 2.469.907 246.991 \$ 2,716,898 TOTAL PROJECT COST with PHASE 2 25,417,518 \$ 847,496 \$ 2,267,824 \$ 28,532,838

- Bids from General Contractors were received on November 9th ranging from \$23.6M to \$27.5M in construction costs with a 10% contingency included.
- The General Contractor bids forecast a total project cost (construction costs and soft costs), including the weight room, ranging from \$27M to \$31M.
- Following an extensive interview process it was determined that Erickson Hall Construction was the best value contractor with a total construction cost of \$26,088,907.00.
 - This cost includes a 10% construction contingency.
- Erickson Hall has mobilized and officially began construction on January 2nd, 2024.



Classroom Renovations and Roof Replacements

- Classroom renovations are scheduled or the 600's, 700's, and 800's classrooms this summer.
 - The overall scope remains similar to the previous classroom renovations with:
 - Flooring
 - Paint
 - Projectors and A/V Integration
 - Whiteboards
 - Removal of Wiremold
 - New Clocks and Speakers
 - New scope for this phase includes:
 - 600's Building Improvements to Art Classrooms
 - 700's Classroom Reconfiguration at Round Building
- We will also be performing roof replacements for the 150's, 600's, 800's, and PAC Buildings.



