




Mary E. Britton Middle School

➤ Completed Work:

- ICF Area E – Final Lift
- CMU Area B
- Grouting CMU Area E and B
- Structural Steel – Finish Roof at Area A and Area C
- Roofing Delivery for Area A and Area C
- Kitchen Roof dried in
- Wood blocking in multiple areas
- Metal Stud Framing at Area F and Area C second Floor
- Air Barrier continuing at Area C and Area A
- MEP and Sprinkler rough-in overhead and in wall at multiple buildings
- Geothermal underground piping install nearly complete

➤ Upcoming Work/Look Ahead:

- Pour final lift at Area C on the 15th
- Begin Stala and ICF at remaining Area D walls
- Finish Roof Structure Area A
- Start Roofing Insulation at Area A
- Finish CMU Area B and Area D
- Continue CMU Area E
- Continue Steel Area C
- Start Roof Structure Area B
- Continue Block Fill and Caulking Control Joints at Mechanical Room and Area A
- Continue MEP Rough-Ins and inspections
- Continue Metal Stud Framing
- Continue Geothermal
- Set Switch Gear in Mechanical Room

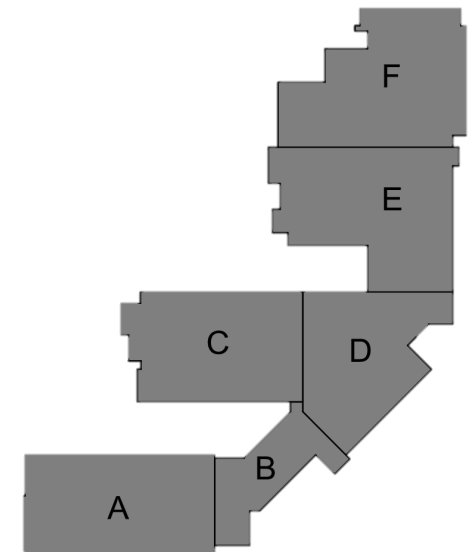

Mary E. Britton Middle School



Area A – Stud Framing above CMU Partitions



Week Ending February 9, 2024

Mary E. Britton Middle School



Area B – CMU Continues at 2nd Floor Corridor



Week Ending February 9, 2024




Mary E. Britton Middle School

Area B – CMU Continues at 2nd Floor



Week Ending February 9, 2024



Mary E. Britton Middle School

Area C – Air Barrier Continuing around building



Week Ending February 9, 2024



Mary E. Britton Middle School

Area C – Roof Soffit Framing



Week Ending February 9, 2024

Mary E. Britton Middle School



Area C – Wood Fascia Installing at Roof Edge



Week Ending February 9, 2024

Mary E. Britton Middle School



Area D – Roof Work Continues



Week Ending February 9, 2024



Mary E. Britton Middle School

Area F – Exterior Stud Framing at Mezzanine



Week Ending February 9, 2024
