


Brookwood Elementary Construction Logistics and Phasing V4.0

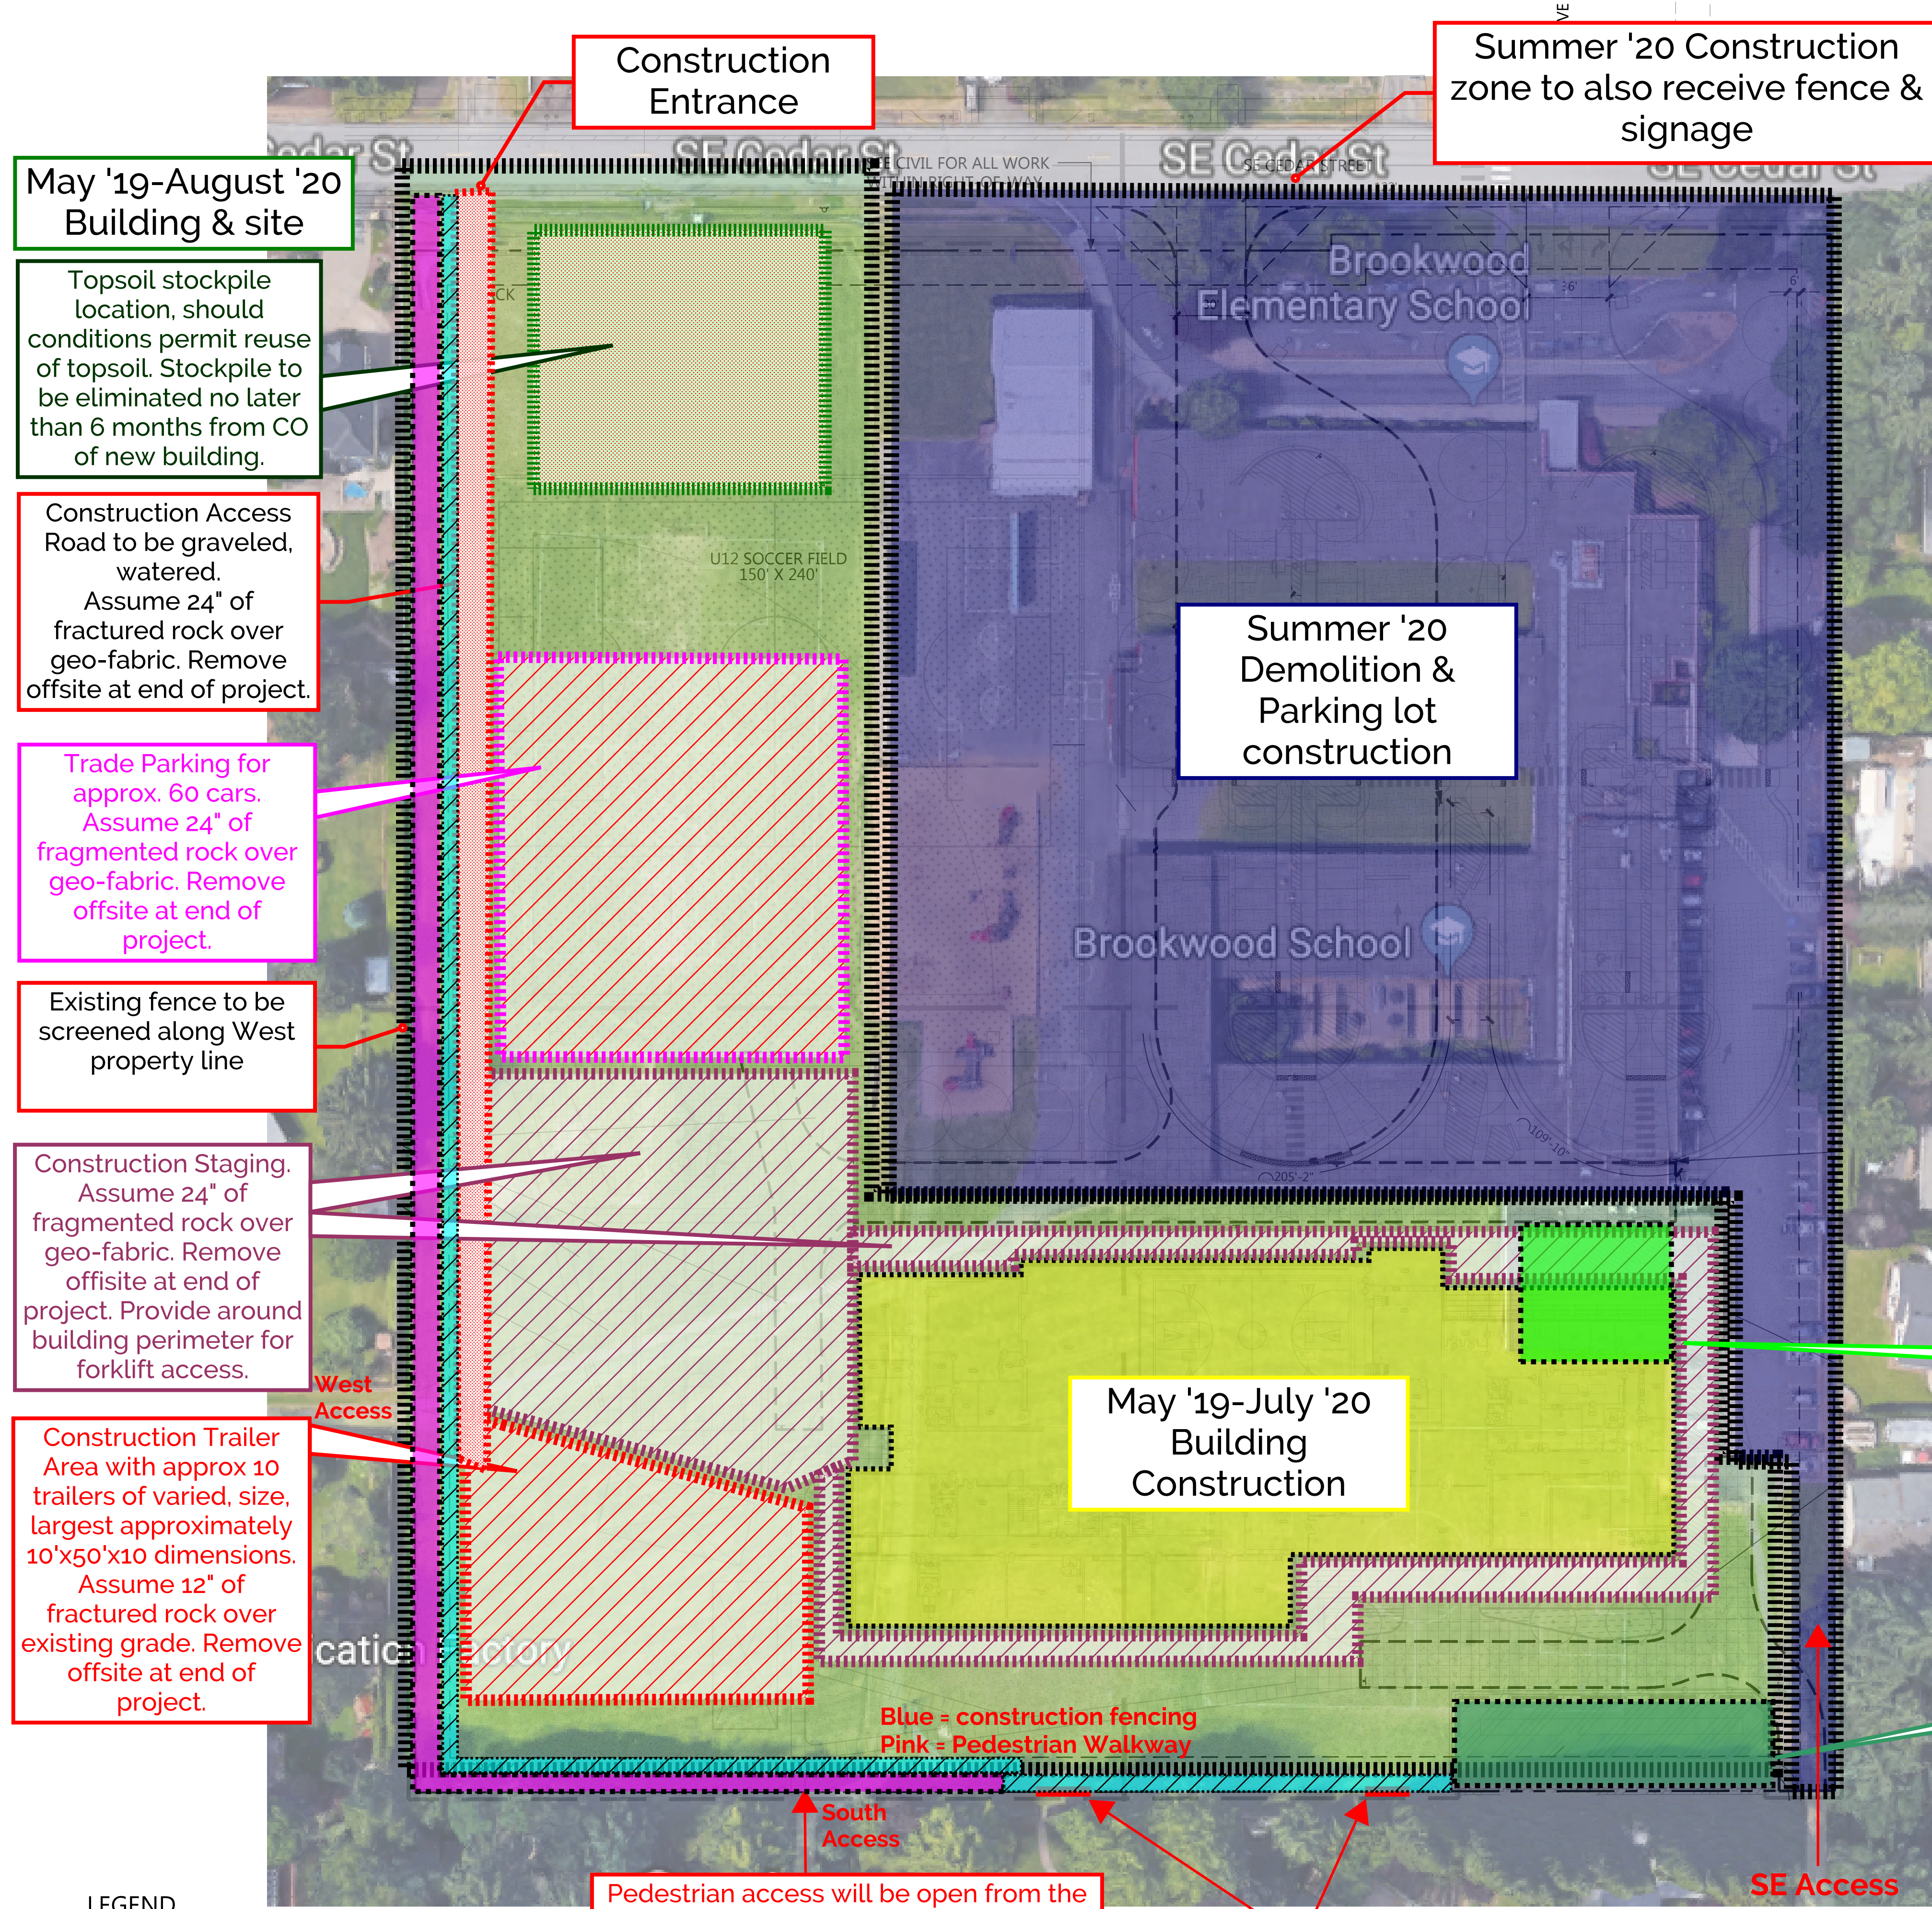

May '19-August '20 Building & site

Topsoil stockpile location, should conditions permit reuse of topsoil. Stockpile to be eliminated no later than 6 months from CO of new building.

Construction Access Road to be graveled, watered. Assume 24" of fractured rock over geo-fabric. Remove offsite at end of project.

Trade Parking for approx. 60 cars. Assume 24" of fragmented rock over geo-fabric. Remove offsite at end of project.

Existing fence to be screened along West property line

Construction Staging. Assume 24" of fragmented rock over geo-fabric. Remove offsite at end of project. Provide around building perimeter for forklift access.

Construction Trailer Area with approx 10 trailers of varied, size, largest approximately 10'x50'x10 dimensions. Assume 12" of fractured rock over existing grade. Remove offsite at end of project.

Summer '20 Construction zone to also receive fence & signage

Summer '20 Demolition & Parking lot construction

May '19-July '20 Building Construction

Work hours: 7 AM to 5 PM. Special hours with application to City.

Kindergarten wing canopy to be demolished May 2019. 2 classes will be relocated to the portable classrooms beginning Fall 2019 for the duration of construction.

City of Hillsboro swale

Pedestrian access will be open from the South and the West, but there will be no access into South entrance of the school and pedestrian pathways will route around the North outside the construction area.

Neighbors' gates to backyards will be blocked off with fencing.

- LEGEND**
- PROPERTY LINE
 - PROJECT LIMIT OF WORK LINE

Created by: Lee Zumwalt
November, 2018
leez@lcfgp.com
503-576-0610

