

Completed MEASURE S PROJECTS



2012 GENERAL OBLIGATION BOND MEASURE

Measure S Completed Projects to Date



1. Cloverly Elementary School



2. Emperor Elementary School



3. La Rosa Elementary School



4. Longdon Elementary School



5. Oak Avenue Elementary School



6. Dr. Doug Sears Learning Center



7. Temple City High School


2012 GENERAL OBLIGATION BOND MEASURE

Cloverly Elementary School – Project Overview



Cloverly Elementary School serves grades 4-6. Cloverly Elementary School received the following improvements under Measure S:

- ✓ New administration offices and a new layout
- ✓ New staff restrooms
- ✓ New mechanical units and ducting
- ✓ New aluminum window system
- ✓ New doors and frames
- ✓ New ceiling grid, tiles and lighting
- ✓ New LVP flooring
- ✓ Interior painting
- ✓ Selective exterior painting
- ✓ Relocation of the main electrical room, data and fire alarm systems
- ✓ Repaired and repainted exterior dry rot damage at portable classroom
- ✓ Installed 2 new 30' trench drains in front of the two story to help alleviate flooding issues
- ✓ Installed rain gutters and down spouts at the two story building

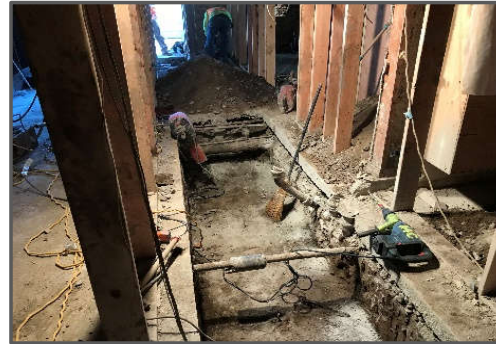

2012 GENERAL OBLIGATION BOND MEASURE

Project Expenditure Breakdown – Cloverly Phase I



	District Object Code	Cost Category	District Goal Number	Estimated Project Budget *	Project Commitments to Date	Project Expenditures to Date	Remaining Budget (Budget - Exp.)	Budget Percentage Spent
PLANNING COSTS								
1	6210	Architect & Engineering Fees	92100	\$296,977.35	\$296,977.35	\$296,977.35	\$0.00	100.00%
2	6220	DSA Fees	92100	16,021.50	16,021.50	16,021.50	0.00	100.00%
3	5950	Preliminary Tests	92100	11,629.00	11,629.00	11,629.00	0.00	100.00%
4	5970	Printing/Legal/Advertising	92100	13,197.02	13,197.02	13,197.02	0.00	100.00%
5	5890	Program Administration	92100	<u>229,090.63</u>	<u>229,090.63</u>	<u>229,090.63</u>	<u>0.00</u>	100.00%
Total Planning Costs:				\$566,915.50	\$566,915.50	\$566,915.50	\$0.00	
CONSTRUCTION COSTS								
6	6250	Construction Costs	92100	\$2,420,456.45	\$2,420,456.45	\$2,420,456.45	\$0.00	100.00%
7	6272	Construction Management	92100	123,859.00	123,859.00	123,859.00	0.00	100.00%
8	6290	Abatement	92100	0.00	0.00	0.00	0.00	0.00%
9	6278	Labor Compliance	92100	0.00	0.00	0.00	0.00	0.00%
10	6295	Legal Fees - Construction	92100	0.00	0.00	0.00	0.00	0.00%
11	6276	Interim Housing/Moving & Storage	92100	62,072.12	62,072.12	62,072.12	0.00	100.00%
12	6270	Construction Testing/Inspection	92100	69,530.32	69,530.32	69,530.32	0.00	100.00%
13	6450	Technology Improvements	92100	71,671.32	71,671.32	71,671.32	0.00	100.00%
14	6410	Furniture & Equipment	92100	25,117.65	25,117.65	25,117.65	0.00	100.00%
15	6292	Construction Contingency	92100	<u>0.00</u>	<u>0.00</u>	<u>0.00</u>	<u>0.00</u>	0.00%
Total Construction Costs:				\$2,772,706.86	\$2,772,706.86	\$2,772,706.86	\$0.00	
COMBINED PROJECT TOTALS:				\$3,339,622.36	\$3,339,622.36	\$3,339,622.36	\$0.00	100.00%

* Project is complete. Therefore, budget equals total commitments.

District Financial 6-30-2023

2012 GENERAL OBLIGATION BOND MEASURE

Project Expenditure Breakdown - Cloverly Phase II



	District Object Code	Cost Category	District Goal Number	Estimated Project Budget *	Project Commitments to Date	Project Expenditures to Date	Remaining Budget (Budget - Exp.)	Budget Percentage Spent
PLANNING COSTS								
1	6210	Architect & Engineering Fees	92100	\$225,970.00	\$225,970.00	\$225,970.00	\$0.00	100.00%
2	6220	DSA Fees	92100	29,343.60	29,343.60	29,343.60	0.00	100.00%
3	5950	Preliminary Tests	92100	0.00	0.00	0.00	0.00	0.00%
4	5970	Printing/Legal/Advertising	92100	4,388.33	4,388.33	4,388.33	0.00	100.00%
5	5890	Program Administration	92100	<u>269,294.75</u>	<u>269,294.75</u>	<u>269,294.75</u>	<u>0.00</u>	100.00%
Total Planning Costs:				\$528,996.68	\$528,996.68	\$528,996.68	\$0.00	
CONSTRUCTION COSTS								
6	6250	Construction Costs	92100	\$1,850,608.99	\$1,850,608.99	\$1,850,608.99	\$0.00	100.00%
7	6272	Construction Management	92100	361,163.48	361,163.48	361,163.48	0.00	100.00%
8	6290	Abatement	92100	0.00	0.00	0.00	0.00	0.00%
9	6278	Labor Compliance	92100	0.00	0.00	0.00	0.00	0.00%
10	6295	Legal Fees - Construction	92100	0.00	0.00	0.00	0.00	0.00%
11	6276	Interim Housing/Moving & Storage	92100	0.00	0.00	0.00	0.00	0.00%
12	6270	Construction Testing/Inspection	92100	105,812.75	105,812.75	105,812.75	0.00	100.00%
13	6450	Technology Improvements	92100	2,219.31	2,219.31	2,219.31	0.00	100.00%
14	6410	Furniture & Equipment	92100	14,855.80	14,855.80	14,855.80	0.00	100.00%
15	6292	Construction Contingency	92100	<u>0.00</u>	<u>0.00</u>	<u>0.00</u>	<u>0.00</u>	0.00%
Total Construction Costs:				\$2,334,660.33	\$2,334,660.33	\$2,334,660.33	\$0.00	
COMBINED PROJECT TOTALS:				\$2,863,657.01	\$2,863,657.01	\$2,863,657.01	\$0.00	100.00%

* Project is complete. Therefore, budget equals total commitments.

District Financial 6-30-2023

2012 GENERAL OBLIGATION BOND MEASURE

Emperor Elementary School – Project Overview



Emperor Elementary School serves grades K-6. Emperor Elementary School received the following improvements under Measure S:

- ✓ Modernized 4 buildings, providing 8 modern classrooms, new administration layout, 8 student restrooms and 2 staff restrooms
- ✓ New HVAC units and ducting
- ✓ New doors and frames
- ✓ New ceiling grid, tiles and lighting
- ✓ New VCT and carpet flooring
- ✓ Interior painting
- ✓ Selective exterior painting
- ✓ New sinks and cabinets
- ✓ Replaced 4 playground slides
- ✓ Repaired rubber play surfacing
- ✓ Provided abatement of old flooring at room 14 and replaced with new carpet
- ✓ New exterior paint at areas not included in modernization



2012 GENERAL OBLIGATION BOND MEASURE

Project Expenditure Breakdown – Emperor



	District Object Code	Cost Category	District Goal Number	Estimated Project Budget *	Project Commitments to Date	Project Expenditures to Date	Remaining Budget (Budget - Exp.)	Budget Percentage Spent
PLANNING COSTS								
1	6210	Architect & Engineering Fees	92200	\$303,985.13	\$303,985.13	\$303,985.13	\$0.00	100.00%
2	6220	DSA Fees	92200	20,818.00	20,818.00	20,818.00	0.00	100.00%
3	5950	Preliminary Tests	92200	7,330.00	7,330.00	7,330.00	0.00	100.00%
4	5970	Printing/Legal/Advertising	92200	5,980.52	5,980.52	5,980.52	0.00	100.00%
5	5890	Program Administration	92200	85,518.42	85,518.42	85,518.42	0.00	100.00%
Total Planning Costs:				\$423,632.07	\$423,632.07	\$423,632.07	\$0.00	
CONSTRUCTION COSTS								
6	6250	Construction Costs	92200	\$1,131,363.89	\$1,131,363.89	\$1,131,363.89	\$0.00	100.00%
7	6272	Construction Management	92200	213,617.12	213,617.12	213,617.12	0.00	100.00%
8	6290	Abatement	92200	0.00	0.00	0.00	0.00	0.00%
9	6278	Labor Compliance	92200	0.00	0.00	0.00	0.00	0.00%
10	6295	Legal Fees - Construction	92200	0.00	0.00	0.00	0.00	0.00%
11	6276	Interim Housing/Moving & Storage	92200	218,911.19	218,911.19	218,911.19	0.00	100.00%
12	6270	Construction Testing/Inspection	92200	102,079.49	102,079.49	102,079.49	0.00	100.00%
13	6450	Technology Improvements	92200	268,154.81	268,154.81	268,154.81	0.00	100.00%
14	6410	Furniture & Equipment	92200	64,685.32	64,685.32	64,685.32	0.00	100.00%
15	6292	Construction Contingency	92200	0.00	0.00	0.00	0.00	0.00%
Total Construction Costs:				\$1,998,811.82	\$1,998,811.82	\$1,998,811.82	\$0.00	
COMBINED PROJECT TOTALS:				\$2,422,443.89	\$2,422,443.89	\$2,422,443.89	\$0.00	100.00%

* Project is complete. Therefore, budget equals total commitments.

District Financial 6-30-2023


2012 GENERAL OBLIGATION BOND MEASURE

La Rosa Elementary School – Project Overview



La Rosa Elementary School serves grades K-3. La Rosa Elementary School received the following improvements under Measure S:

- ✓ Modernized 2 classroom buildings providing 12 modernized classrooms and 4 student restrooms
- ✓ Modernization of 4 remaining buildings providing 7 modern classrooms, new administration layout, 4 student restrooms, 4 staff restrooms
- ✓ New HVAC units
- ✓ New aluminum window system
- ✓ New doors and frames
- ✓ New ceiling grid, tiles and lighting
- ✓ New VCT and carpet flooring
- ✓ Interior painting
- ✓ Exterior painting
- ✓ New sinks and cabinets
- ✓ Technology Package: Interactive whiteboard, short throw projector, speaker system with voice lift microphone

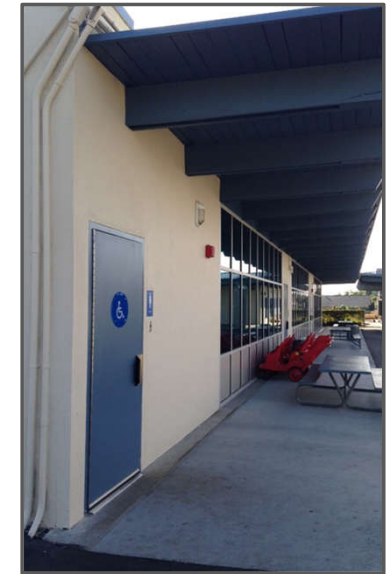

2012 GENERAL OBLIGATION BOND MEASURE

La Rosa Elementary School – Project Overview (Continued)



- ✓ New ceiling grid, tiles and lighting
- ✓ New LVP and carpet flooring
- ✓ Removed planters near Cafeteria and installed new asphalt paving, providing open play surfaces for students
- ✓ Updated all irrigation on the back field and automated the irrigation in the front of the school
- ✓ Increased the thickness wood chips in the playground areas
- ✓ New exterior paint at areas not included in modernization



2012 GENERAL OBLIGATION BOND MEASURE

Project Expenditure Breakdown – La Rosa Phase I



	District Object Code	Cost Category	District Goal Number	Estimated Project Budget *	Project Commitments to Date	Project Expenditures to Date	Remaining Budget (Budget - Exp.)	Budget Percentage Spent
PLANNING COSTS								
1	6210	Architect & Engineering Fees	92300	\$350,404.34	\$350,404.34	\$350,404.34	\$0.00	100.00%
2	6220	DSA Fees	92300	17,443.00	17,443.00	17,443.00	0.00	100.00%
3	5950	Preliminary Tests	92300	9,669.00	9,669.00	9,669.00	0.00	100.00%
4	5970	Printing/Legal/Advertising	92300	12,763.03	12,763.03	12,763.03	0.00	100.00%
5	5890	Program Administration	92300	265,352.17	265,352.17	265,352.17	0.00	100.00%
Total Planning Costs:				\$655,631.54	\$655,631.54	\$655,631.54	\$0.00	
CONSTRUCTION COSTS								
6	6250	Construction Costs	92300	\$2,334,423.22	\$2,334,423.22	\$2,334,423.22	\$0.00	100.00%
7	6272	Construction Management	92300	134,621.50	134,621.50	134,621.50	0.00	100.00%
8	6290	Abatement	92300	0.00	0.00	0.00	0.00	0.00%
9	6278	Labor Compliance	92300	0.00	0.00	0.00	0.00	0.00%
10	6295	Legal Fees - Construction	92300	0.00	0.00	0.00	0.00	0.00%
11	6276	Interim Housing/Moving & Storage	92300	214,797.23	214,797.23	214,797.23	0.00	100.00%
12	6270	Construction Testing/Inspection	92300	82,116.51	82,116.51	82,116.51	0.00	100.00%
13	6450	Technology Improvements	92300	148,318.85	148,318.85	148,318.85	0.00	100.00%
14	6410	Furniture & Equipment	92300	48,081.16	48,081.16	48,081.16	0.00	100.00%
15	6292	Construction Contingency	92300	0.00	0.00	0.00	0.00	0.00%
Total Construction Costs:				\$2,962,358.47	\$2,962,358.47	\$2,962,358.47	\$0.00	
COMBINED PROJECT TOTALS:				\$3,617,990.01	\$3,617,990.01	\$3,617,990.01	\$0.00	100.00%

* Project is complete. Therefore, budget equals total commitments.

District Financial 6-30-2013

2012 GENERAL OBLIGATION BOND MEASURE

Project Expenditure Breakdown – La Rosa Phase II



	District Object Code	Cost Category	District Goal Number	Estimated Project Budget *	Project Commitments to Date	Project Expenditures to Date	Remaining Budget (Budget - Exp.)	Budget Percentage Spent
PLANNING COSTS								
1	6210	Architect & Engineering Fees	92300	\$311,000.00	\$311,000.00	\$311,000.00	\$0.00	100.00%
2	6220	DSA Fees	92300	53,462.05	53,462.05	53,462.05	0.00	100.00%
3	5950	Preliminary Tests	92300	395.00	395.00	395.00	0.00	100.00%
4	5970	Printing/Legal/Advertising	92300	5,325.78	5,325.78	5,325.78	0.00	100.00%
5	5890	Program Administration	92300	<u>337,329.07</u>	<u>337,329.07</u>	<u>337,329.07</u>	<u>0.00</u>	100.00%
Total Planning Costs:				\$707,511.90	\$707,511.90	\$707,511.90	\$0.00	
CONSTRUCTION COSTS								
6	6250	Construction Costs	92300	\$3,262,735.11	\$3,262,735.11	\$3,262,735.11	\$0.00	100.00%
7	6272	Construction Management	92300	361,163.53	361,163.53	361,163.53	0.00	100.00%
8	6290	Abatement	92300	0.00	0.00	0.00	0.00	0.00%
9	6278	Labor Compliance	92300	0.00	0.00	0.00	0.00	0.00%
10	6295	Legal Fees - Construction	92300	0.00	0.00	0.00	0.00	0.00%
11	6276	Interim Housing/Moving & Storage	92300	0.00	0.00	0.00	0.00	0.00%
12	6270	Construction Testing/Inspection	92300	130,012.00	130,012.00	130,012.00	0.00	100.00%
13	6450	Technology Improvements	92300	95,980.90	95,980.90	95,980.90	0.00	100.00%
14	6410	Furniture & Equipment	92300	67,966.33	67,966.33	67,966.33	0.00	100.00%
15	6292	Construction Contingency	92300	<u>0.00</u>	<u>0.00</u>	<u>0.00</u>	<u>0.00</u>	0.00%
Total Construction Costs:				\$3,917,857.87	\$3,917,857.87	\$3,917,857.87	\$0.00	
COMBINED PROJECT TOTALS:				\$4,625,369.77	\$4,625,369.77	\$4,625,369.77	\$0.00	100.00%

* Project is complete. Therefore, budget equals total commitments.

District Financial 6-30-2023

2012 GENERAL OBLIGATION BOND MEASURE

Longden Elementary School – Project Overview



Longden Elementary School serves grades TK-6. Longden Elementary School received the following improvements under Measure S:

- ✓ Modernize existing single and two story classroom buildings providing 20 modern classrooms, new library and new media center
- ✓ New masonry elevator tower with 2 new staff restrooms
- ✓ Modernize 3 existing Kindergarten classrooms
- ✓ New parking and student drop off
- ✓ New ramp, stairs and flagpole at school entrance
- ✓ Technology package: New touch screen interactive displays, speaker system w/ voicelift microphone. Rekeyed the balance of the site
- ✓ Repaired asphalt as needed on the playground and added slurry to the entire playground
- ✓ New fencing around the west playground to separate Little league




2012 GENERAL OBLIGATION BOND MEASURE

Longden Elementary School – Project Overview (Continued)



- ✓ New carpet in rooms 311 & 312
- ✓ New reflective window tint to glass in 311 & 312
- ✓ New sod at the south side of the 100 building.
- ✓ New landscaping at the drive entrance to the school
- ✓ Partnered with the city and installed new irrigation for new trees planted by the city on Longden
- ✓ Increased thickness of wood chips in the playground areas

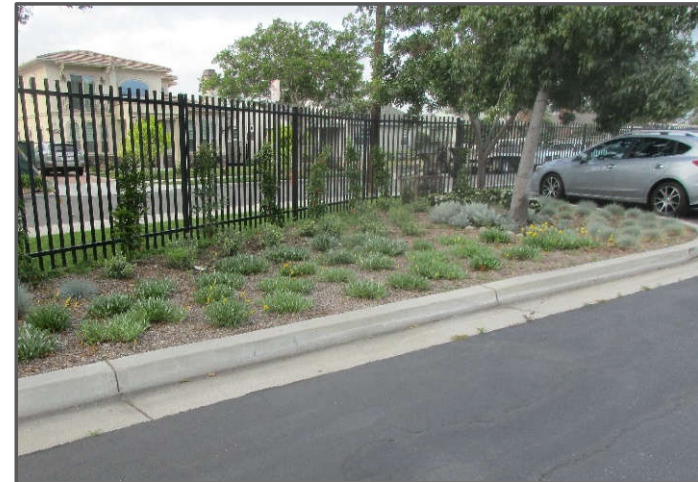

2012 GENERAL OBLIGATION BOND MEASURE

Project Expenditure Breakdown - Longden



	District Object Code	Cost Category	District Goal Number	Estimated Project Budget *	Project Commitments to Date	Project Expenditures to Date	Remaining Budget (Budget - Exp.)	Budget Percentage Spent
PLANNING COSTS								
1	6210	Architect & Engineering Fees	92400	\$1,042,412.34	\$1,042,412.34	\$1,042,412.34	\$0.00	100.00%
2	6220	DSA Fees	92400	99,530.03	99,530.03	99,530.03	0.00	100.00%
3	5950	Preliminary Tests	92400	63,750.32	63,750.32	63,750.32	0.00	100.00%
4	5970	Printing/Legal/Advertising	92400	17,198.17	17,198.17	17,198.17	0.00	100.00%
5	5890	Program Administration	92400	927,826.22	927,826.22	927,826.22	0.00	100.00%
Total Planning Costs:				\$2,150,717.08	\$2,150,717.08	\$2,150,717.08	\$0.00	
CONSTRUCTION COSTS								
6	6250	Construction Costs	92400	\$9,700,868.02	\$9,700,868.02	\$9,700,868.02	\$0.00	100.00%
7	6272	Construction Management	92400	1,109,797.66	1,109,797.66	1,109,797.66	0.00	100.00%
8	6290	Abatement	92400	0.00	0.00	0.00	0.00	0.00%
9	6278	Labor Compliance	92400	0.00	0.00	0.00	0.00	0.00%
10	6295	Legal Fees - Construction	92400	0.00	0.00	0.00	0.00	0.00%
11	6276	Interim Housing/Moving & Storage	92400	295,385.14	295,385.14	295,385.14	0.00	100.00%
12	6270	Construction Testing/Inspection	92400	528,048.25	528,048.25	528,048.25	0.00	100.00%
13	6450	Technology Improvements	92400	158,728.70	158,728.70	158,728.70	0.00	100.00%
14	6410	Furniture & Equipment	92400	13,352.57	13,352.57	13,352.57	0.00	100.00%
15	6292	Construction Contingency	92400	0.00	0.00	0.00	0.00	0.00%
Total Construction Costs:				\$11,806,180.34	\$11,806,180.34	\$11,806,180.34	\$0.00	
COMBINED PROJECT TOTALS:				\$13,956,897.42	\$13,956,897.42	\$13,956,897.42	\$0.00	100.00%

* Project is complete. Therefore, budget equals total commitments.

District Financial 6-30-2023

2012 GENERAL OBLIGATION BOND MEASURE

Oak Intermediate School – Project Overview



Oak Intermediate School serves grades 7-8 Oak Intermediate School received the following improvements under Measure S:

- ✓ Resurfaced asphalt courts with colored coating to help with extending the life of the asphalt, lowering the surface temperature at the play ground and it looks 100% better
- ✓ Provided abatement of existing flooring in the 400 and 500 wings, replacing with new carpet
- ✓ Removed existing grass at the back playfield, installed new irrigation system and planted new grass
- ✓ Installed new drinking fountains at back field
- ✓ Re-keyed and added new hardware to the 100 wing
- ✓ Installed crash padding on the gym walls
- ✓ New exterior paint



2012 GENERAL OBLIGATION BOND MEASURE

Project Expenditure Breakdown - Oak



	District Object Code	Cost Category	District Goal Number	Estimated Project Budget *	Project Commitments to Date	Project Expenditures to Date	Remaining Budget (Budget - Exp.)	Budget Percentage Spent
PLANNING COSTS								
1	6210	Architect & Engineering Fees	92200	\$25,947.50	\$25,947.50	\$25,947.50	\$0.00	100.00%
2	6220	DSA Fees	92200	0.00	0.00	0.00	0.00	0.00%
3	5950	Preliminary Tests	92200	1,480.00	1,480.00	1,480.00	0.00	100.00%
4	5970	Printing/Legal/Advertising	92200	626.01	626.01	626.01	0.00	100.00%
5	5890	Program Administration	92200	<u>112,827.99</u>	<u>112,827.99</u>	<u>112,827.99</u>	<u>0.00</u>	100.00%
Total Planning Costs:				\$140,881.50	\$140,881.50	\$140,881.50	\$0.00	
CONSTRUCTION COSTS								
6	6250	Construction Costs	92200	\$23,135.00	\$23,135.00	\$23,135.00	\$0.00	100.00%
7	6272	Construction Management	92200	0.00	0.00	0.00	0.00	0.00%
8	6290	Abatement	92200	0.00	0.00	0.00	0.00	0.00%
9	6278	Labor Compliance	92200	0.00	0.00	0.00	0.00	0.00%
10	6295	Legal Fees - Construction	92200	0.00	0.00	0.00	0.00	0.00%
11	6276	Interim Housing/Moving & Storage	92200	0.00	0.00	0.00	0.00	0.00%
12	6270	Construction Testing/Inspection	92200	24,852.00	24,852.00	24,852.00	0.00	100.00%
13	6450	Technology Improvements	92200	343,725.94	343,725.94	343,725.94	0.00	100.00%
14	6410	Furniture & Equipment	92200	33.47	33.47	33.47	0.00	100.00%
15	6292	Construction Contingency	92200	<u>0.00</u>	<u>0.00</u>	<u>0.00</u>	<u>0.00</u>	0.00%
Total Construction Costs:				\$391,746.41	\$391,746.41	\$391,746.41	\$0.00	
COMBINED PROJECT TOTALS:				\$532,627.91	\$532,627.91	\$532,627.91	\$0.00	100.00%

* Project is complete. Therefore, budget equals total commitments.

District Financial 6-30-2023

2012 GENERAL OBLIGATION BOND MEASURE

Dr. Doug Sears Learning Center – Project Overview



The Dr. Doug Sears Learning Center is designed to give students an opportunity to complete their high school education in an alternative setting, becoming productive citizens and lifelong learners. Dr. Doug Sears Learning Center received the following improvements under Measure S:

- ✓ Demolished old administration building
- ✓ New premanufactured administration and classroom building
- ✓ New landscaped entry



2012 GENERAL OBLIGATION BOND MEASURE

Project Expenditure Breakdown – Doug Sears



	District Object Code	Cost Category	District Goal Number	Estimated Project Budget *	Project Commitments to Date	Project Expenditures to Date	Remaining Budget (Budget - Exp.)	Budget Percentage Spent
PLANNING COSTS								
1	6210	Architect & Engineering Fees	92600	\$49,491.21	\$49,491.21	\$49,491.21	\$0.00	100.00%
2	6220	DSA Fees	92600	3,845.00	3,845.00	3,845.00	0.00	100.00%
3	5950	Preliminary Tests	92600	1,880.00	1,880.00	1,880.00	0.00	100.00%
4	5970	Printing/Legal/Advertising	92600	6,218.63	6,218.63	6,218.63	0.00	100.00%
5	5890	Program Administration	92600	<u>32,335.29</u>	<u>32,335.29</u>	<u>32,335.29</u>	<u>0.00</u>	100.00%
Total Planning Costs:				\$93,770.13	\$93,770.13	\$93,770.13	\$0.00	
CONSTRUCTION COSTS								
6	6250	Construction Costs	92600	\$503,303.65	\$503,303.65	\$503,303.65	\$0.00	100.00%
7	6272	Construction Management	92600	49,992.50	49,992.50	49,992.50	0.00	100.00%
8	6290	Abatement	92600	23,578.35	23,578.35	23,578.35	0.00	100.00%
9	6278	Labor Compliance	92600	0.00	0.00	0.00	0.00	0.00%
10	6295	Legal Fees - Construction	92600	0.00	0.00	0.00	0.00	0.00%
11	6276	Interim Housing/Moving & Storage	92600	522.92	522.92	522.92	0.00	100.00%
12	6270	Construction Testing/Inspection	92600	40,970.25	40,970.25	40,970.25	0.00	100.00%
13	6450	Technology Improvements	92600	46,179.56	46,179.56	46,179.56	0.00	100.00%
14	6410	Furniture & Equipment	92600	9,679.32	9,679.32	9,679.32	0.00	100.00%
15	6292	Construction Contingency	92600	<u>0.00</u>	<u>0.00</u>	<u>0.00</u>	<u>0.00</u>	0.00%
Total Construction Costs:				\$674,226.55	\$674,226.55	\$674,226.55	\$0.00	
COMBINED PROJECT TOTALS:				\$767,996.68	\$767,996.68	\$767,996.68	\$0.00	100.00%

* Project is complete. Therefore, budget equals total commitments.

District Financial 6-30-2023

2012 GENERAL OBLIGATION BOND MEASURE

Temple City High School – Project Overview



Temple City High School serves grades 9-12. Temple City High School received the following improvements under Measure S:

- ✓ Constructed 3 new masonry buildings connected by exterior walkways
- ✓ 32 new classrooms, 2 new elevators, 4 new student restroom and four new staff restrooms
- ✓ Technology package: interactive display, speaker system, multiple displays
- ✓ Flexible furniture and teaching spaces
- ✓ Exterior learning courts placed at each building
- ✓ Construction of a new competition size pool and modernization of locker/team rooms
- ✓ New masonry pool equipment building
- ✓ New masonry main electrical room and trash enclosure
- ✓ New concession room
- ✓ Expanded locker room layout with new restroom and shower facilities
- ✓ New multi use ball field
- ✓ New softball field and scoreboard
- ✓ Rekeyed and replaced hardware on the 400/500 wing and the portables
- ✓ New bleachers for baseball and new additional bleachers for softball




2012 GENERAL OBLIGATION BOND MEASURE

Temple City High School – Project Overview (Continued)



- ✓ Regraded and resurfaced the track adding twenty yards of fresh track mix
- ✓ New 4' foul line fences at the baseball field
- ✓ New carpet in 3 classrooms in the 500 wing
- ✓ New retaining wall, mow curb, TCHS logo at back field
- ✓ New fencing at tennis courts and along Camino Real
- ✓ Partnered with the city and installed new irrigation for new trees planted by the city on Camino Real
- ✓ Additional new technology and furniture for Phase 1A
- ✓ New roofing system at building 300
- ✓ Install new windows at the facilities office
- ✓ Install new mechanical units at the District Office
- ✓ District wide irrigation improvements
- ✓ District wide keying, hardware and security improvements



2012 GENERAL OBLIGATION BOND MEASURE

Project Expenditure Breakdown – Temple City High Phase I



	District Object Code	Cost Category	District Goal Number	Estimated Project Budget *	Project Commitments to Date	Project Expenditures to Date	Remaining Budget (Budget - Exp.)	Budget Percentage Spent
PLANNING COSTS								
1	6210	Architect & Engineering Fees	92500	\$1,537,472.98	\$1,537,472.98	\$1,537,472.98	\$0.00	100.00%
2	6220	DSA Fees	92500	266,780.49	266,780.49	266,780.49	0.00	100.00%
3	5950	Preliminary Tests	92500	257,210.75	257,210.75	257,210.75	0.00	100.00%
4	5970	Printing/Legal/Advertising	92500	102,341.04	102,341.04	92,541.04	9,800.00	90.42%
5	5890	Program Administration	92500	<u>1,473,616.98</u>	<u>1,473,616.98</u>	<u>1,473,616.98</u>	<u>0.00</u>	100.00%
Total Planning Costs:				\$3,637,422.24	\$3,637,422.24	\$3,627,622.24	\$9,800.00	
CONSTRUCTION COSTS								
6	6250	Construction Costs	92500	\$19,867,007.82	\$19,867,007.82	\$19,867,007.82	\$0.00	100.00%
7	6272	Construction Management	92500	1,252,072.01	1,252,072.01	1,252,072.01	0.00	100.00%
8	6290	Abatement	92500	129,187.00	129,187.00	129,187.00	0.00	100.00%
9	6278	Labor Compliance	92500	2,231.25	2,231.25	2,231.25	0.00	100.00%
10	6295	Legal Fees - Construction	92500	33,690.50	33,690.50	33,690.50	0.00	100.00%
11	6276	Interim Housing/Moving & Storage	92500	1,904,887.00	1,904,887.00	1,904,887.00	0.00	100.00%
12	6270	Construction Testing/Inspection	92500	732,566.13	732,566.13	732,566.13	0.00	100.00%
13	6450	Technology Improvements	92500	508,199.45	508,199.45	508,199.45	0.00	100.00%
14	6410	Furniture & Equipment	92500	299,241.10	299,241.10	299,241.10	0.00	100.00%
15	6292	Construction Contingency	92500	<u>0.00</u>	<u>0.00</u>	<u>0.00</u>	<u>0.00</u>	0.00%
Total Construction Costs:				\$24,729,082.26	\$24,729,082.26	\$24,729,082.26	\$0.00	
COMBINED PROJECT TOTALS:				\$28,366,504.50	\$28,366,504.50	\$28,356,704.50	\$9,800.00	99.97%

* Project is complete. Therefore, budget equals total commitments.

District Financial 6-30-2023

2012 GENERAL OBLIGATION BOND MEASURE

Project Expenditure Breakdown – Temple City Phase II



	District Object Code	Cost Category	District Goal Number	Estimated Project Budget *	Project Commitments to Date	Project Expenditures to Date	Remaining Budget (Budget - Exp.)	Budget Percentage Spent
PLANNING COSTS								
1	6210	Architect & Engineering Fees	92500	\$756,600.37	\$756,600.37	\$756,600.37	\$0.00	100.00%
2	6220	DSA Fees	92500	30,602.26	30,602.26	30,602.26	0.00	100.00%
3	5950	Preliminary Tests	92500	12,389.37	12,389.37	12,389.37	0.00	100.00%
4	5970	Printing/Legal/Advertising	92500	11,817.50	11,817.50	11,817.50	0.00	100.00%
5	5890	Program Administration	92500	<u>919,926.13</u>	<u>919,926.13</u>	<u>919,926.13</u>	<u>0.00</u>	100.00%
Total Planning Costs:				\$1,731,335.63	\$1,731,335.63	\$1,731,335.63	\$0.00	
CONSTRUCTION COSTS								
6	6250	Construction Costs	92500	\$12,365,941.98	\$12,365,941.98	\$12,365,941.98	\$0.00	100.00%
7	6272	Construction Management	92500	960,957.89	960,957.89	960,957.89	0.00	100.00%
8	6290	Abatement	92500	0.00	0.00	0.00	0.00	0.00%
9	6278	Labor Compliance	92500	0.00	0.00	0.00	0.00	0.00%
10	6295	Legal Fees - Construction	92500	0.00	0.00	0.00	0.00	0.00%
11	6276	Interim Housing/Moving & Storage	92500	0.00	0.00	0.00	0.00	0.00%
12	6270	Construction Testing/Inspection	92500	480,208.55	480,208.55	480,208.55	0.00	100.00%
13	6450	Technology Improvements	92500	0.00	0.00	0.00	0.00	0.00%
14	6410	Furniture & Equipment	92500	558.36	558.36	558.36	0.00	100.00%
15	6292	Construction Contingency	92500	<u>0.00</u>	<u>0.00</u>	<u>0.00</u>	<u>0.00</u>	0.00%
Total Construction Costs:				\$13,807,666.78	\$13,807,666.78	\$13,807,666.78	\$0.00	
COMBINED PROJECT TOTALS:				\$15,539,002.41	\$15,539,002.41	\$15,539,002.41	\$0.00	100.00%

* Project is complete. Therefore, budget equals total commitments.

District Financial 6-30-2023

2012 GENERAL OBLIGATION BOND MEASURE

State Modernization & New Construction Grants

STATE SCHOOL FACILITY PROGRAM FUNDING



2012 GENERAL OBLIGATION BOND MEASURE

Summary of State School Facility Program Funds Received

Type of Project	School	Funding Application Number	State Funding Amount	District Required Match	State Eligible Budget	Date Funded by OPSC	Funded from Prop 51 *
Modernization	Cloverly	57/65052-00-009	\$2,507,334	\$1,671,556	\$4,178,890	9/1/2020	Funded
Modernization	La Rosa	57/65052-00-010	2,013,203	1,342,135	3,355,338	9/1/2020	Funded
Modernization	Longden	57/65052-00-012	4,722,658	3,148,439	7,871,097	11/30/2021	Funded
Modernization	TCHS	57/65052-00-011	18,635,247	12,423,498	31,058,745	9/4/2020	Funded
New Construction	TCHS	50/65052-00-003	5,231,260	5,231,260	10,462,520	9/4/2020	Funded
New Construction	D. Sears LC	50/65052-00-002	213,824	213,824	427,648	9/4/2020	Funded
Total Estimated Funding:			\$33,323,526	\$24,030,712	\$57,354,238		

* All of the above projects have been fully funded by the State and the funds will be used for the District's priority school projects.
