


# North Springs HS Replacement Project Updates

June 7, 2023



## North Springs HS

- SCHEMATIC DESIGN 100% – JULY 2023
- DESIGN DEVELOPMENT 100% – OCTOBER 2023
- LAND DISTURBANCE PERMIT SUBMISSION – OCTOBER 2023
- 50% CONSTRUCTION DOCUMENTS – FEBRUARY 2024
- SITE CONSTRUCTION START – MARCH 2024
- 90% CONSTRUCTION DOCUMENTS – MAY 2024
- BID DOCUMENTS – JUNE 2024
- BUILDING CONSTRUCTION START – OCTOBER 2024
- SUBSTANTIAL COMPLETION FOR NEW BUILDING – JUNE 2026
- DEMOLITION OF OLD BUILDING AND COMPLETION OF ATHLETIC FIELDS - FALL  
2027

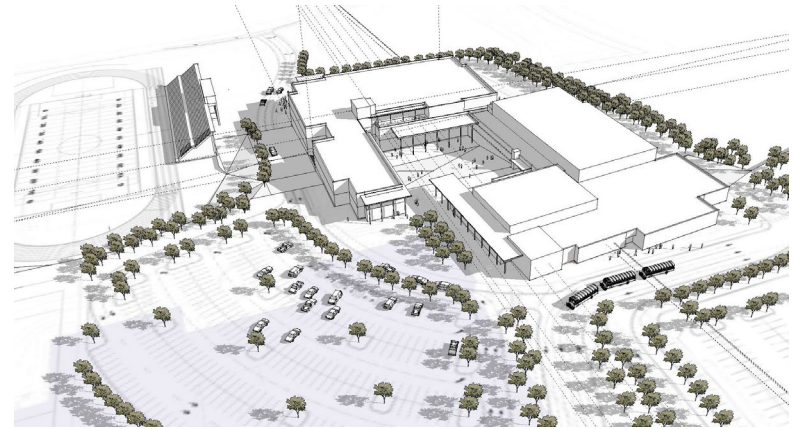

## Geotechnical Testing Activities – Summary Schedule:

Activity	Days Budgeted	Proposed Dates	Notes
Marking/Flagging Borings	4	5/31 to 6/2	Borings in woods may not be accessible. Marking with paint will be minimal. Work on track and football fields will be done on Fri 6/2
Private Utility Locate	4	6/5, 6/6, 6/7, 6/9	Work in track and football fields will be done on Fri 6/9
Clearing	4	6/12, 6/13, 6/14, 6/16	Refer to attached clearing schedule map. Clearing around practice field will be done on Fri 6/16.
Drilling	10	6/19 to 6/30	Refer to attached drilling schedule map. Drilling at track and football fields will be done on Fri 6/23 and Fri 6/30
Infiltration Testing	7	7/3 to 7/11	Testing around the track and football fields will be done on 7/7



# Clearing Schedule Map





# Drilling Schedule Map



Questions?
