DECEMBER 2023



OSHKOSH AREA SCHOOL DISTRICT PROJECT PROGRESS REPORT

CONSTRUCTION UPDATE

Thanks to the mild weather, construction continues to stay on schedule at Menominee Elementary School. The northern portion of the building has walls up to full height with window blocking, exterior insulation, and roofing ongoing. On the interior of the northern portion, concrete floor slabs are being placed on both the first and second floors with ductwork being hung and piping being installed. On the east side of the building, the steel is up at the cafeteria with the crew working their way south to create the administration and media center volume. The south side of the building is now starting to take shape with load bearing walls rising for the single-story portion of the school on the south.

The last of the design efforts for this referendum project are underway with the blue jay selected as the school mascot. The interiors team at Bray is working on environmental graphics within the building. This similar design language was also employed at Vel Phillips Middle School with graphics to help students with wayfinding, create school pride, and also encourage learning opportunities. OASD and Bray will work together over the next two to three months to finalize the graphic designs in order to have them created and installed by the time the school opens in the fall. Look for renderings of this graphics in future progress reports.

WHAT'S NEXT?


- » Interior walls in the northern section will be constructed.
- » Exterior windows will continue with glass being installed.
- » Masons will be finished with the elevator shaft and last stairway, continuing with exterior walls on the south.



LOOKING TOWARDS THE CAFETERIA FROM THE SOUTH



CLASSROOM AREAS BEFORE CONCRETE FLOORS AND DIVIDING WALLS

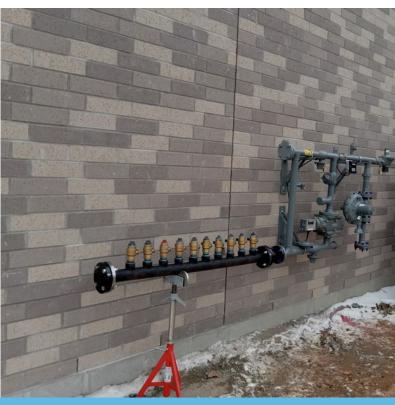

EXTERIOR BRICK INSTALLED ON THE NORTH



RENDERING OF MUSIC AND ART CORRIDOR
