




# Mary E. Britton Middle School

## ➤ **Completed Work:**

- Structural Steel and Decking Area D Complete This Week
- CMU Area E at 90%
- Set Large Columns and Beams at Storm Shelter for Masonry Work
- Cafeteria Decking Complete
- Area C Framing Complete
- Continuing MEP and Sprinkler Area A and Area C
- Block Fill Area A Completed
- Geothermal Vault Rock Excavation Complete

## ➤ **Upcoming Work/Look Ahead:**

- Structural Steel at Storm Shelter
- Handrails and Ladders Area A Platform
- Complete CMU Platform G301
- Install Freezer/Cooler Thermal Break and Prep Slab
- Prep Topping Slab G301 Corridor
- Block Fill Beginning Area C
- Install Trench Drain at Dock
- Dry in Cafeteria and Entrance Lobby
- Complete Domestic and Sanitary Testing Area C
- Complete Domestic and Sanitary Testing at Kitchen
- Continue Pulling Feeder Wire all Panels
- Excavate Geothermal Lines to Building Connection

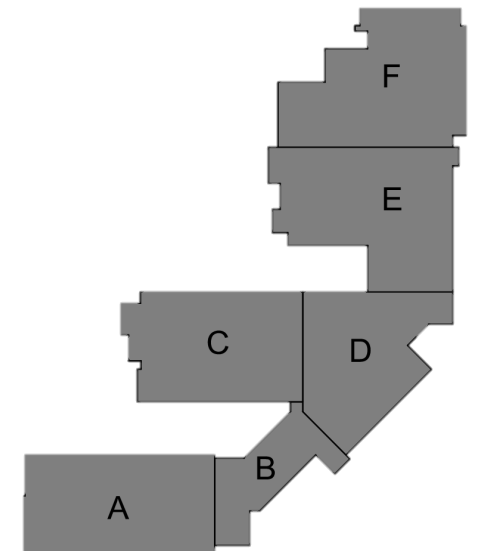

# Mary E. Britton Middle School



Ariel – Front Entry



Week Ending March 29, 2024

# Mary E. Britton Middle School



Ariel – Overall Site



Week Ending March 29, 2024



# Mary E. Britton Middle School



## Area B- Admin Roof Decking



Week Ending March 29, 2024

# Mary E. Britton Middle School



## Area C – Mezzanine MEP & Roof Work



Week Ending March 29, 2024



# Mary E. Britton Middle School



## Area D – Media Center Steel Framing at Window



Week Ending March 29, 2024

# Mary E. Britton Middle School



## Area D – Media Center Steel



Week Ending March 29, 2024



# Mary E. Britton Middle School



## Area E – Cafeteria Roof Decking



Week Ending March 29, 2024



# Mary E. Britton Middle School



Area E – Storm Shelter Walls Topped Out Ready for Joists



Week Ending March 29, 2024
