


A Quarterly Insight into. . .

- *Small-Scale Projects*
- *Projects in Construction Phase*
- *Projects in Design & Bid Phase*

Splost Construction

- **Ash Street Center:** At the Ash Street Center, we were tasked with transforming a training room into a physical education room. The scope includes new paint, rubber flooring, storefront, locker room, and wall padding. In the last few months, we put the finishing touches on the project with some wall padding for added safety. We're now planning phase two of this project which will consist of a basketball goal, rock climbing wall, and a playground right outside the new play room. Estimated completion on the interior is March 2024 and May 2024 for the exterior.
- **Gardenwalk :** At our Garden Walk transportation office, we are working on transforming an old break room to staff restrooms and a kitchenette for our extraordinary drivers. In the last few months, we have completed the demolition, ran all the underground plumbing, framed and hung all the sheetrock walls, and painted. Our contractor is now finishing up the tile and flooring, hanging doors, and setting plumbing fixtures to be ready for a February 2024 completion..
- **Kay R. Pace:** At Kay R. Pace Elementary School of the Arts, we took a cafeteria that wasn't being used and turned it into a physical education room, two offices, and a conference room. We are now adding a third office to this previously unused space to help make the school more efficient. Estimated completion is March 2024.
- **Twelve Oaks Stadium:** Twelve Oaks Stadium is receiving a new video display scoreboard, press box enclosure, and painting of the grandstands. We've begun the pressure washing process for the grandstands. We will begin painting in the next few weeks. In addition, we have a new scoreboard expected to arrive soon, and we will be enclosing the press box in storefront glass as well. Estimated completion is April 2024.



Group A Athletics

Race to the finish line



At Charles R. Drew High School, the baseball field and the facilities are completed. The field has received new sod, fencing, irrigation systems, an Electro-Mech scoreboard, and a windscreen. The existing dugouts and concession/press box buildings received new brick veneer wrapped around the walls and new lighting. The benches, helmets, and bat storage were installed inside the dugouts. The painting was done in the concession and the new press box/storage buildings. The tennis courts received resurfacing, new nets, and fencing as well. The construction of the new football press box is also completed. The football field received new field lights, goal posts, and a scoreboard. The batting cage has also been installed, and new bleachers along with concrete pads were installed throughout the site. Sod was patched, and the irrigation system was repaired at the soccer field. The bin blocks were installed for the infield mix storage. The construction of the monument sign is completed with the new LED message sign. In conclusion, the school vestibule and the weight room are being renovated.



Forest Park High School received new sod, fencing, irrigation systems, an Electro-Mech scoreboard, and windcreens at the baseball field. The home team's dugout storage room has been converted into a locker room and PTAC unit. The construction of the football press box/storage and concession building is completed; however, the MEP work is ongoing inside the buildings. The running track has been refaced and striped. The existing press box building has received new metal roofing. The football field has received new field lights. The batting cage has been installed, and a concrete pad has been poured. New bleachers were installed throughout the fields. The perimeter fencing was installed around the backside of the football field. Paving concrete sidewalks throughout the site are ongoing. Casework has been installed in the concession stand.




Mundy's Mill High School's baseball field, has received new sod, a retaining wall, an irrigation system, a fence, a windscreen, and a scoreboard. The football concession building, press box and bathrooms are completed. The MEP works inside the building are almost completed as well. The construction of the monument sign with the LED message sign is completed. The tennis courts have received resurfacing, new nets, and a fence. The improvements for the baseball field are completed. The existing softball/baseball concession building has received interior and exterior painting, new roofing, rubber flooring, new lighting, and a PA system. The bleachers are installed throughout the fields, and the bin blocks were installed for infield mix storage.

Group B Athletics Continues to Advance

The synthetic turf, fencing, scoreboards, and dugouts for the softball and baseball fields at Jonesboro High School have been installed. The dugouts and press box buildings have split-face block walls and metal roofing. Lights, bleachers, helmets, and bat storage have been installed inside the dugouts. The concession building's electrical, mechanical, and plumbing work is ongoing along with the installation of the sidewalks and the retention ponds.

At Riverdale High School, the baseball/softball field has received new synthetic turf, a scoreboard, dugouts with bleachers, helmets and bat storage. The home team dugout storage room has been converted into a locker storage room with HVAC. A new batting cage has been installed, and the existing concession building has received new HVAC, lighting, plumbing fixtures, casework, roll-up doors and a new staircase. New restrooms were constructed for the softball/baseball field. The school also received a new football press box/storage building and new restrooms/concession building.

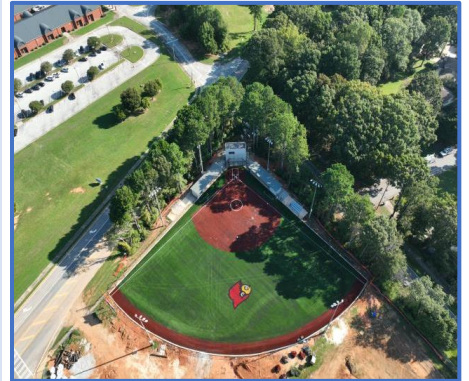

Forest Park Middle Gains Ground

In the preceding months, the job site has been brought to grade, and the grinding and redistribution of rock throughout the site has been completed. Unsuitable soils have been removed from various areas of the site, most notably from the subgrade of the future gymnasium parking area. The site office trailer was delivered and is now utilized for construction team meetings and site management.

The construction crew has continued to work on storm sewer lines throughout the site and are nearing completion of the second and last underground detention pond that will be located under the southern end of the football field. Construction of the four MSE retaining walls on the northern and eastern sides of the campus were completed in the latter half of January.

Aggregate piers were bored for and installed in preparation for foundations in Sectors B, C and D. These sectors comprise areas that include the media center, classroom wing, commons area, and kitchen. Foundations for Sector A, the Administration and front office areas, will begin the final week in January. Preparations have begun for structural steel framing to begin with Sector D the first week of February with multiple steel framing packages delivered and stored on site.




NEW CONVOCATION CENTER AND COLLEGE & CAREER ACADEMY

The new Convocation Center and College & Career Academy project is progressing well. Demolition was completed in early January. With the help from subcontractors, Walker Concrete, B&D Concrete Cutting, and Wurster Betterground, we have now entered a new phase of construction- the process of drilling aggregate piers, pouring footings for new building's structure, and securing Southlake's wall accent with the future convocation site. In the past months, MEJA Construction has been working closely with Southlake Mall, Georgia Power, and Southern Company Gas to relocate utility lines while still keeping the mall area and area surrounding the mall active. Over the next few months, structural concrete will begin to be installed along with the process of erecting the building's structure.




New Team Members ..

We would like to cordially welcome aboard our newest team members **Tammy Walker**, Administrative Assistant II, and **Krystal Ashley**, Procurement Specialist, to CCPS Construction Department. As a team, we strive to build a better tomorrow today, project by project.

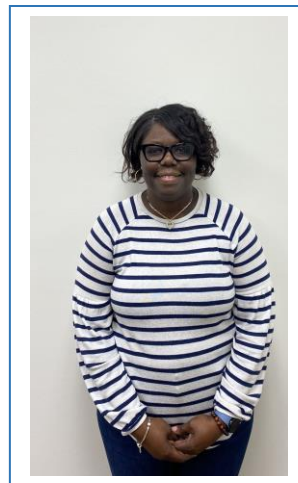

Welcome to the Team



Splost Construction

Projects in Design and Bid Phase

Project	Status	Architect
Group V HVAC Services	Under Design	MSSA-PBK
Group VI HVAC Services	Under Design	MSSA-PBK
Rosenwald School Renovations	Bid Under Review	JW Robinson
Lovejoy High School Renovations	Bid Under Review	CDH Partners
Church Street Elementary School	Under Design	Cooper Carry
West Clayton Elementary School	Under Design	Cooper Carry
Northcutt Elementary & North Clayton Middle School	Under Design	Perkins & Will
North Clayton High School	Under Design	Perkins & Will
Riverdale Early Learning Center	Under Design	MSSA-PBK
Pointe South Elementary School & Middle School	Under Design	MSSA-PBK

Mt. Zion High Athletics	Bid Under Review	SSOE
Tara Elementary School	Under Design	Cooper Carry
Tara Stadium Field House	Under Design	Southern A&E
J.W. Arnold Elementary School	Under Design	CGLS
