


- *Small-Scale Projects*
- *Projects in Construction Phase*
- *Projects in Design & Bid Phase*
- *Community Service Projects*

A Quarterly Insight into. . .

Splost Construction

- **Ash Street Center:** Ash street recently received a renovation in which the school received a playroom that will have a rock climbing wall for students to play and exercise on, and also a basketball goal for more indoor activities. Along with the playroom renovation, the school will also receive a newly renovated playground on their campus. Project is projected to be completed in August of 2024.
- **Gardenwalk :** The Gardenwalk Transportation Facility recently received a restroom renovation, so bus drivers will have access to a restroom while doing overtime or other situations that occur when the building is closed. Within this renovation, the facility also received a new breakroom for the staff. This renovation is completed.
- **Kay R. Pace:** Kay R. Pace received a renovation which transformed the old Kay Pace cafeteria into offices and a conference room. Along with the offices and additional conference room renovations, the school will also receive a newly renovated and bigger black box performance room for theatrical performances. Project is projected to be completed in May of 2024.
- **Twelve Oaks Stadium:** Twelve Oaks Stadium is receiving new paint and an enclosed and newly renovated pressbox. Along with the new paint and pressbox, the stadium will also be receiving a new jumbotron scoreboard and newly installed playclocks. This project is projected to be completed by August 2024.
- **Adaptive Sports Facility-Central Office South:** will also be receiving a renovation to add a facility within the gym area of the building for adaptive sports. This facility will be the new home for the county's adaptive sports teams. Included in this renovation will be a new weight room, bathroom renovations, and a gym renovation along with a small renovation to the cafeteria and concession stand. This project is projected to be completed as soon as August 2024.



New Forest Park Middle School

Construction of the new Forest Park Middle School has advanced considerably in the previous months. Since the last update, the project has come together in many exciting ways. The parking lot, the bus lane, and the athletic track are all on grade, and curbing and gutters have been installed and back filled throughout a large portion of the project site. The fire and water lines have both been installed, buried, and tied to the vaults at the street level. Extensive concrete work has been completed in multiple sectors of the building structure. Foundations are complete in sectors C and D, and nearing completion in sectors B and F. The subgrade utility lines have been installed in C and D, and the slab on grade has been poured for both areas. Additionally, the poured concrete retaining wall that establishes the southern and western exterior subgrade of sectors A, B, C and F is nearing completion. Beginning in February, the structural steel framework of the building began to be assembled. The framework in sector C was completed in mid-April, and sector B is well underway. The exterior masonry walls of sector D, which comprises the kitchen area, have begun and are nearing completion, and interior masonry walls within sector C have begun. With the cooperation of the weather, the metal framework of the entire building should be nearing completion within the next three months.



Group A Athletics Continue

At Charles R. Drew High School, the perimeter fencing has been installed. The tennis courts have received new windscreens, and the school logo has been painted. The weight room has been sectioned off with the CMU wall for the new training room. In addition to the athletic improvements, a section of the school's main lobby was converted into a security vestibule with the reception area and the attendance office. New surveillance cameras will be installed inside the vestibule as well. This will improve safety of the staff and students by controlling and maintaining access to the school. Additionally, Southern Crescent Stadium has received a new video display board.



At Forest Park High School, the bin blocks storage was installed for infield mix. The MEP work for the concession/bathroom/storage building has been completed. All sidewalks and fencing are completed. All of the press boxes have received new PA systems. In addition, the gymnasium is currently being renovated. The painting of the entire gym, resurfacing of the floor, and striping are complete. The installation of the scoreboards and the bleachers is ongoing. The renovation of the gym is expected to be completed May, 2024. Similarly, Mundy's Mill High School's site has been graded and straw throughout the project has been completed. The tennis courts have received new windscreens. The MEP work for the new concession/bathroom/storage building has been completed. The installation of the perimeter fencing has been completed as well.



Group B Athletics Come to a Close

At Jonesboro High School, the batting cages have been installed, and the trees have been removed near the softball and baseball fields. Also, the windscreens are being manufactured for the softball and baseball fields. The MEP work for the new concession/bathroom building is completed, as are other buildings throughout the site. The sidewalks, fencing, sod, retention ponds, and the lift station have been installed. The PA systems were installed in all of the press boxes. The football field has received new field lights and the band tower. At Riverdale High School, the final grading, spreading seeds, straw, and sod were completed. The baseball/softball field has received a new windscreen, and the MEP work for all buildings has been completed. The installation of the batting cage and net was completed. The football field has received new field lights and the band tower.




NEW CONVOCATION CENTER AND COLLEGE & CAREER ACADEMY

The Convocation Center and College & Career Academy job site has been busy this last quarter. MEJA was able to coordinate with Southern Gas Company to relocate a gas line that was impeding grading operations. B&D Concrete Cutting and Complete Demolition Services have finished the selective demolition at the mall's wall, and Keystone Masonry has installed CMU to completely separate the mall from the new building. Wurster Betterground has also finished drilling aggregate piers.

This current phase of the project is all about concrete. Montalvo has installed retaining walls around the college and career academy portion of the project. Those new concrete walls are being waterproofed by Metro Waterproofing and then back filled by Cawthon Grading. Polk County Plumbing and Frontier Electric have also been on site roughing in their underground pipe and conduit.

In the next few months, we should see a lot of the interior structure making progress. We should begin to see shear walls, concrete columns, concrete slabs, and steel members getting installed in our next update. The underground electrical and plumbing will get stubbed up, and we will start to see MEP hangers off of that second level inside the building.

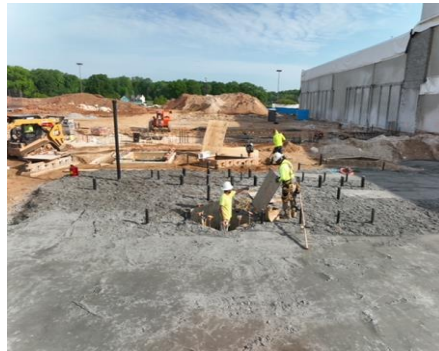

“BUILDING FROM THE INSIDE OUT”

This quarter, CCPS Construction Department expanded its impact and intentionally thought of new ways to make a difference. Caring about the well being of our buildings, also includes caring about the ones who will utilize them. So, our department set way to give back to the community. Aaron Deveaux, Project Engineer, gave several supplies on the behalf of the construction department to the Homeless Education Center. These products will be used to their discretion. As a department, we continue to build a better tomorrow, today, and we look forward to future community service events and opportunities.




New Team Members ..

*We would like to cordially welcome aboard our newest team member **Cephus Jackson**, Project Manager III, to CCPS Construction Department. As a team, we strive to build a better tomorrow today, project by project.*



Welcome to the Team



Splost Construction

Projects in Design and Bid Phase

Project	Status	Architect
Group V HVAC Services	Under Design	MSSA-PBK
Group VI HVAC Services	Under Design	MSSA-PBK
Church Street Elementary School	Bid Under Review	Cooper Carry
West Clayton Elementary School	Bid Under Review	Cooper Carry
Northcutt Elementary & North Clayton Middle School	Under Design	Perkins & Will
North Clayton High School	Under Design	Perkins & Will
Riverdale Early Learning Center	Under Design	MSSA-PBK
Pointe South Elementary School & Middle School	Under Design	MSSA-PBK
Tara Elementary School	Under Design	Cooper Carry
Tara Stadium Field House	Under Design	Southern A&E

J.W. Arnold Elementary School	Under Design	CGLS
W. A Fountain - Unidos Dual Language Elementary School	Under Design	Cooper Carry
