

Project Update

St. Pius X Catholic School

March 15, 2024



WE BUILD GREAT SCHOOLS INDUSTRIAL FACILITIES HEALTHCARE FACILITIES COMMUNITIES LEADERS FUTURES .

Table of Contents



- Team Members
- Summary Report
- Weekly Progress Update
- Subcontractors
- Project Milestones
- Look Ahead Schedule
- Progress Updates
- Project Photos
- Contact Information



PARRISH
CONSTRUCTION GROUP

TEAMS

WE BUILD GREAT

ST. PIUS CATHOLIC SCHOOL TEAM MEMBERS



Owner	Architect/Engineer	Parrish Construction Group
<ul style="list-style-type: none">Catholic Education of North Georgia, Inc.St. Pius X Catholic High School	<ul style="list-style-type: none">CDH Architecture	<ul style="list-style-type: none">David Loudermilk, Project DirectorAlex Johnson, Project ManagerArt Cofelice, SuperintendentTrey DeRieux, Project EngineerDrew Plunkett, Asst. SuperintendentZack Cofelice, Asst. Superintendent



PARRISH
CONSTRUCTION GROUP

SUMMARY REPORT

WE BUILD GREAT

SUMMARY REPORT

Month	Calendar Days	Planned Weather Days	Claimed Weather Days
MARCH 2023	31	6	3
APRIL 2023	30	4	4
MAY 2023	31	2	1
JUNE 2023	30	3	2
JULY 2023	31	4	3
AUGUST 2023	31	3	9
SEPTEMBER 2023	30	2	3
OCTOBER 2023	31	3	1
NOVEMBER 2023	30	5	2
DECEMBER 2023	31	8	1
JANUARY 2024	31	11	7
FEBRUARY 2024	29	8	4
MARCH 2024	31	6	2

Critical Tasks	% Complete
SITWORK	100%
FOUNDATIONS	100%
UNDERGROUND UTILITIES	100%
SLAB ON GRADE/DECK	100%
STEEL	99%
ELECTRICAL	97%
PLUMBING	95%
MECHANICAL	98%
ROOFING	100%



PARISH
CONSTRUCTION GROUP

PROGRESS UPDATE

WE BUILD GREAT

WEEKLY PROGRESS UPDATE

- ELEVATOR WAITING ON INSPECTIONS
- LANDSCAPING FINISHING UP
- PAINTING THE HANDRAILS ON SWITCHBACKS
NEXT WEEK
- INSTALLING STEEL POSTS AND METAL PANEL
WALL NEXT WEEK
- STORAGE ROOM CAGES INSTALLED THIS WEEK



PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
Site Work		
GRADING AND UTILITIES	RUBY-COLLINS	100%
UNDERGROUND GAS LINE	POLK COUNTY PUBLIC SERVICE	100%
Building Systems		
MECHANICAL	GEORGIA MECHANICAL	100%
ELECTRICAL	ALL STATE ELECTRICAL CONTRACTORS	98%
PLUMBING	POLK COUNTY PUBLIC SERVICE	97%
FIRE PROTECTION	GAINESVILLE FIRE PROTECTION	100%
Building Structure		
FOUNDATION AND SLAB ON GRADE (SOG)/DECK	PARRISH CONCRETE	100%
STRUCTURAL STEEL FRAMING	TRINITY FABRICATORS	98%
EXTERIOR WALLS	PARRISH MASONRY	100%
INTERIOR WALLS	PARRISH MASONRY/HOLT & HOLT	100%



PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
Building Envelope		
BRICK	PARRISH MASONRY	100%
WINDOWS/STOREFRONT	COMMERCIAL GLASS & MIRRORS	98%
Building Interiors		
FLOORING	PERIMETER FLOORS	95%
DRYWALL	HOLT & HOLT	100%
CEILINGS	HOLT & HOLT	97%
PAINTING	MCs PAINTING	97%




PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

PROGRESS UPDATE

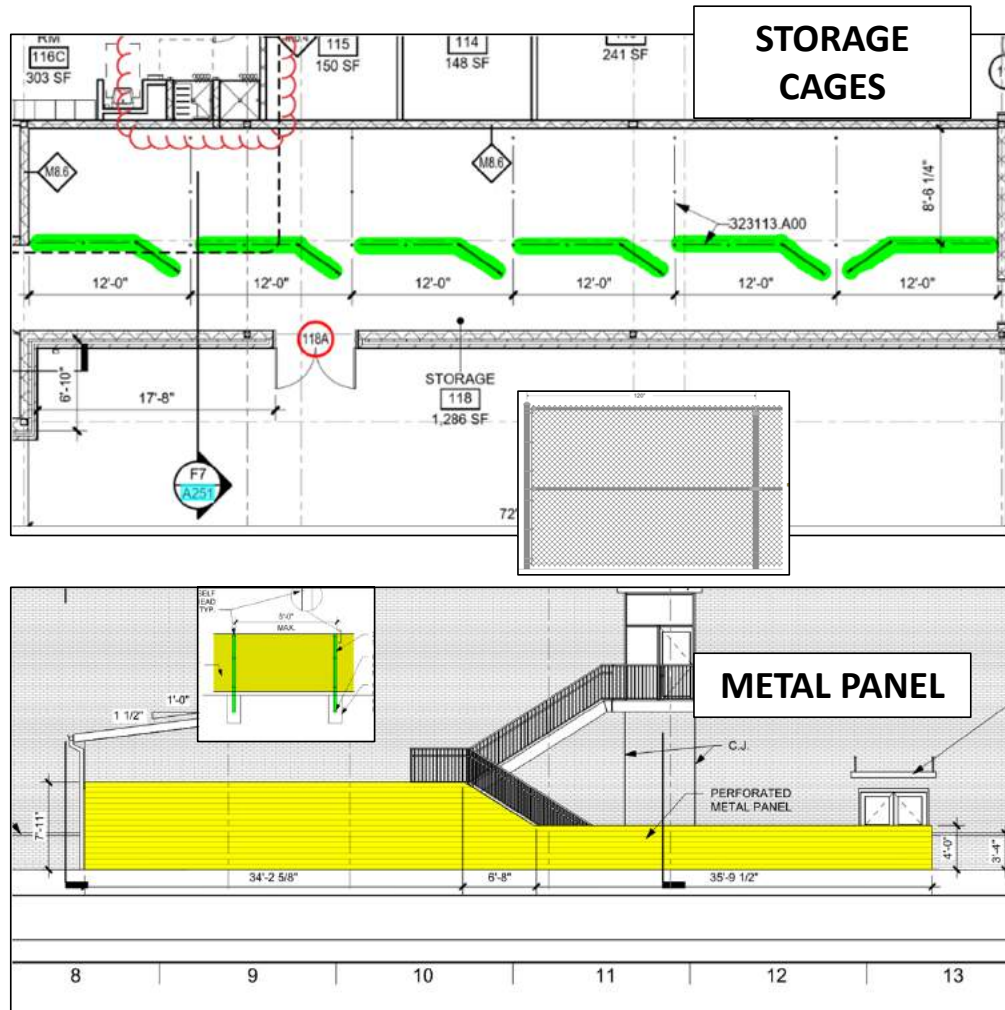

**GREEN HIGHLIGHTED SECTIONS
HAVE BEEN COMPLETED; YELLOW
HIGHLIGHTED IN PROGRESS**

**ELEVATOR IS WAITING ON
INSPECTION; STORAGE ROOM
CHAINLINK CAGES INSTALLED
THIS WEEK; FLOORING RUBBER
BASE INSTALLED; HANDRAILS
FINISHING UP; STEEL POSTS
BEING SET**

**METAL PANEL TO BE INSTALLED
NEXT WEEK; STEEL POSTS TO BE
PAINTED; HANDRAILS TO BE
PAINTED**



PARRISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT _____.

PROJECT PHOTOS



STRENGTH TRAINING ROOM



PARRISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT _____.

PROJECT PHOTOS



LANDSCAPING AND PARKING LOT



PARRISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT

PROJECT PHOTOS

UPSTAIRS MEETING ROOM





PARRISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT _____.

PROJECT PHOTOS



SWITCHBACK RAMPS AND HANDRAILS

Contact Information



David Loudermilk

Project Director
478.256.1839

dloudermilk@parrishconstruction.com



Alex Johnson

Project Manager
470.540.0047


ajohnson@parrishconstruction.com



Art Cofelice

Sr. Superintendent
770.880.3762

acofelice@parrishconstruction.com

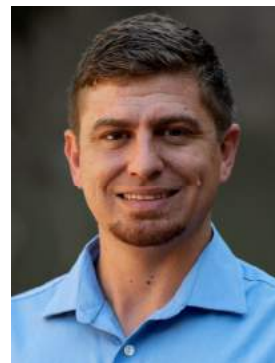

Zack Cofelice

Superintendent
470.925.3525

zcofelice@parrishconstruction.com



Trey DeRieux

Project Engineer
470.442.3169

tderieux@parrishconstruction.com



Drew Plunkett

Asst. Superintendent
678.215.5193

dplunkett@parrishconstruction.com

WE BUILD GREAT SCHOOLS INDUSTRIAL FACILITIES HEALTHCARE FACILITIES COMMUNITIES LEADERS FUTURES .
