

HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



School Site Improvement Projects

Regular Board Meeting
May 9th, 2024

Business Services



PROJECT COMPLETE LIST 2023-2024



Site	Item Description	Funding Source	Completed Date
Los Molinos	Basketball Court Restriping	Facilities	04/2024
Lassalette	Basketball Court Restriping	Facilities	04/2024
Sparks Elementary	Basketball Court Restriping	Facilities	04/2024
Workman Elementary	Basketball Court Restriping	Facilities	04/2024
Del Valle Headstart	Headstart Restroom Flooring	Child Development	04/2024
Winglane Headstart	Headstart Restroom Flooring	Child Development	04/2024
Los Molinos Elementary	Hillside Fencing	Facilities	04/2024
Valinda School of Academics	Flooring Room K3	Facilities	04/2024
Workman Elementary	Flooring Front Office	Facilities	04/2024
La Puente High School	Library Ceiling Repair & Paint	Facilities	04/2024
Workman High School	Exterior Gym Lighting	Facilities	04/2024

NEW!

Projects Completed as of May 9th, 2024

Los Molinos Elementary- Restriping Basketball Courts



BEFORE



AFTER



Projects Completed as of May 9th, 2024

Sparks Elementary- Restriping Basketball Courts

NEW!



BEFORE





AFTER



Projects Completed as of May 9th, 2024

Los Molinos Elementary Hillside Fencing

NEW!

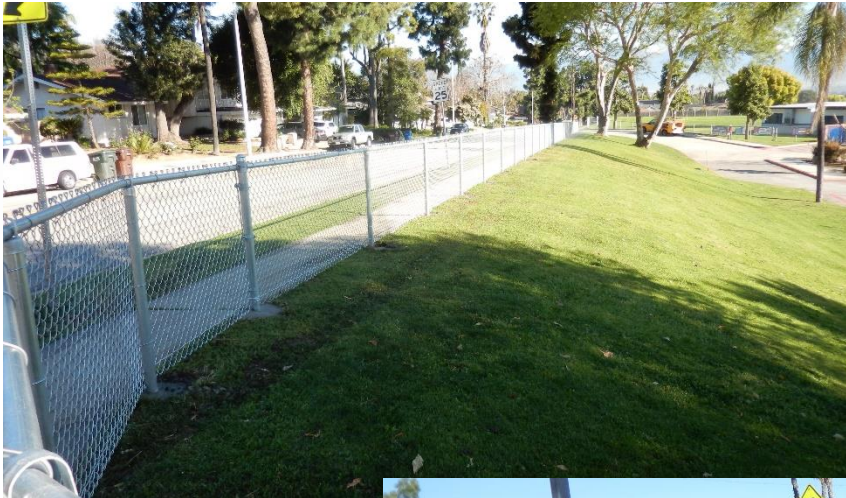


Projects Completed as of May 9th, 2024

Valinda School of Academics- Room K3 Flooring



AFTER

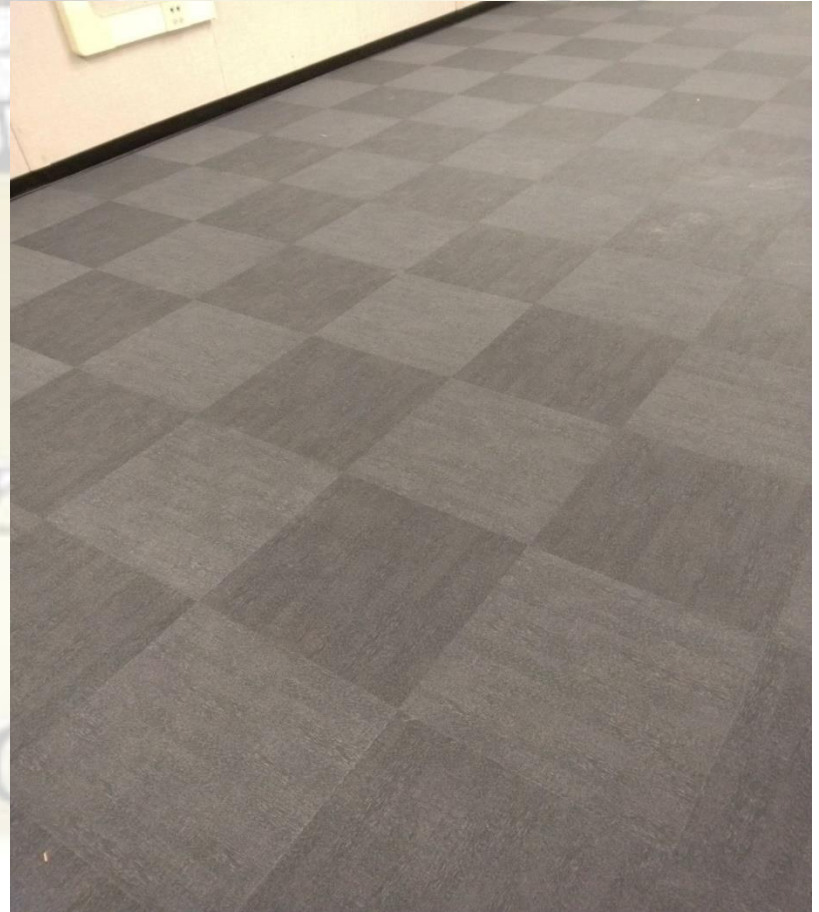

Projects Completed as of May 9th, 2024

Workman Elementary – Front Office Flooring

NEW!



Projects Completed as of May 9th, 2024

La Puente High School – Library Ceiling Repair



BEFORE



AFTER



Projects Completed as of May 9th, 2024

Workman High School – Exterior Gym Lighting

NEW!

BEFORE



AFTER



Projects In Progress

2023-2024



Projects in Progress as of May 9th, 2024

Facilities

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Los Altos High School	Reroof Various Buildings	NA	NA	Complete	Complete	Deferred Maintenance	Complete
Wedgeworth	K-5 Permanent School	Complete	Approved	Complete	In Progress	COPS	06/2025
Los Altos High School	Gym & Locker Room HVAC (65 tons of temporary HVAC units have been installed)	Complete	Approved	Complete	Pending	Facilities	12/2024
Cedarlane Academy	Portable Installation	Complete	Pending (Back Check)	Pending	Pending	Facilities	08/2024
Palm Elementary	Front of School Fencing	NA	NA	In Process	Pending	Facilities	08/2024

Projects in Progress as of May 9th, 2024

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Lassalette Elementary	Inclusive Playground	NA	NA	Pending	Pending	Special Ed	TBD

Adult Ed

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Willow Adult	Two-Story Medical Building	Complete	NA	Complete	In Progress	Adult Ed	05/2024
Dibble Adult	HVAC Replacement - MPR	Complete	NA	Complete	In Progress	Adult Ed	05/2024

Projects in Progress as of May 9th, 2024

Child Development

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Winglane ES Headstart	Portable Installation	Complete	Approved	Complete	In Progress	Child Development	06/2024
Nelson Elementary School Head Start	Playground & Shade Structure	Complete	Approved	Pending	Pending	Child Development	TBD
Workman Elementary School Head Start	Playground & Accessibility Path of Travel	Complete	Pending	Pending	Pending	Child Development	TBD
Fairgrove Academy Headstart	Playground & Shade Structure	Complete	Approved	Pending	Pending	Child Development	TBD
Amar Center	Entry Security Project	Complete	Approved	Pending	Pending	Child Development	TBD
Sierra Vista - SSC	SSC Office Reception Counter	Complete	NA	Complete	Pending	Child Development	05/2024

NEW!

Projects in Progress as of May 9th, 2024

Winglane Headstart Portable Installation-Demolition



Projects in Progress as of May 9th, 2024

Nutrition Services

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
District Office	Warehouse Freezer	Complete	NA	Pending	TBD	Food Services	TBD
Wilson High School	Kitchen Modernization	Complete	Pending	Pending	TBD	Food Services	TBD
Mesa Robles Middle School	Kitchen Renovation	Complete	Pending	Pending	TBD	Food Services	TBD
Baldwin Elementary School	Kitchen Renovation - Three Compartment Sink Installation	Complete	NA	Pending	TBD	Food Services	TBD

Facilities Upcoming Projects

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
District Wide	HVAC System Replacement	Pending	Pending	Pending	TBD	TBD
Kwis Elementary	Baseball Fields	Complete	Approved	Pending	TBD	TBD
Los Altos High School	Stadium Press Box & Bleachers	Complete	Approved	Pending	TBD	TBD
La Puente High School	Custom Shade Structure	Complete	Approved	Pending	TBD	TBD
Wilson High School	Stadium Press Box & Bleachers	Complete	Pending	Pending	TBD	TBD
Workman HS	Phase II Stadium and Baseball Field (Phase I Track & Field and Softball Field Complete) OPTION B	Complete	Pending	Estimated	Estimated	TBD (14-18 months after Board approval of the Bid)



Next Report – June 27, 2024
