



The **HILL** - The **H**ub for **I**nnovative **L**earning & **L**eadership

➤ **Completed Work:**

- CMU work on all floors continued.
- Ceilings continued on Levels 3.
- Metal stud and drywall work continuing on all levels.
- Window glazing continued on all Levels.
- Electrical devices and lighting continued on Levels 4 and 3.
- Plumbing above ceiling continued on all floors.

➤ **Upcoming Work / Look Ahead:**

- CMU work should near completion.
- Ceilings to continue on Levels 3 and 2.
- Curtainwalls and glazing to continue, nearing completion.
- Ductwork installation to continue.
- Electrical and plumbing wall rough-ins to continue with masonry and electrical devices being installed.
- **There will be a partial shutdown, and at times a complete shutdown of Indiana for roofing work.**

The HILL - The Hub for Innovative Learning & Leadership

Micro-pile concrete poured and ready for canopy install



Week Ending May 10, 2024



The HILL - The Hub for Innovative Learning & Leadership

Exterior retaining walls and new wing wall poured and rubbed



Week Ending May 10, 2024

The HILL - The Hub for Innovative Learning & Leadership



Rear parking prepped for new asphalt and pavers



Week Ending May 10, 2024



The HILL - The Hub for Innovative Learning & Leadership

Ductwork progressing in Carpentry lab



Week Ending May 10, 2024



The HILL - The Hub for Innovative Learning & Leadership

Floor prep for quarry tile in Culinary Arts




Week Ending May 10, 2024

The HILL - The Hub for Innovative Learning & Leadership



LVT flooring mockup for Level 4 for install

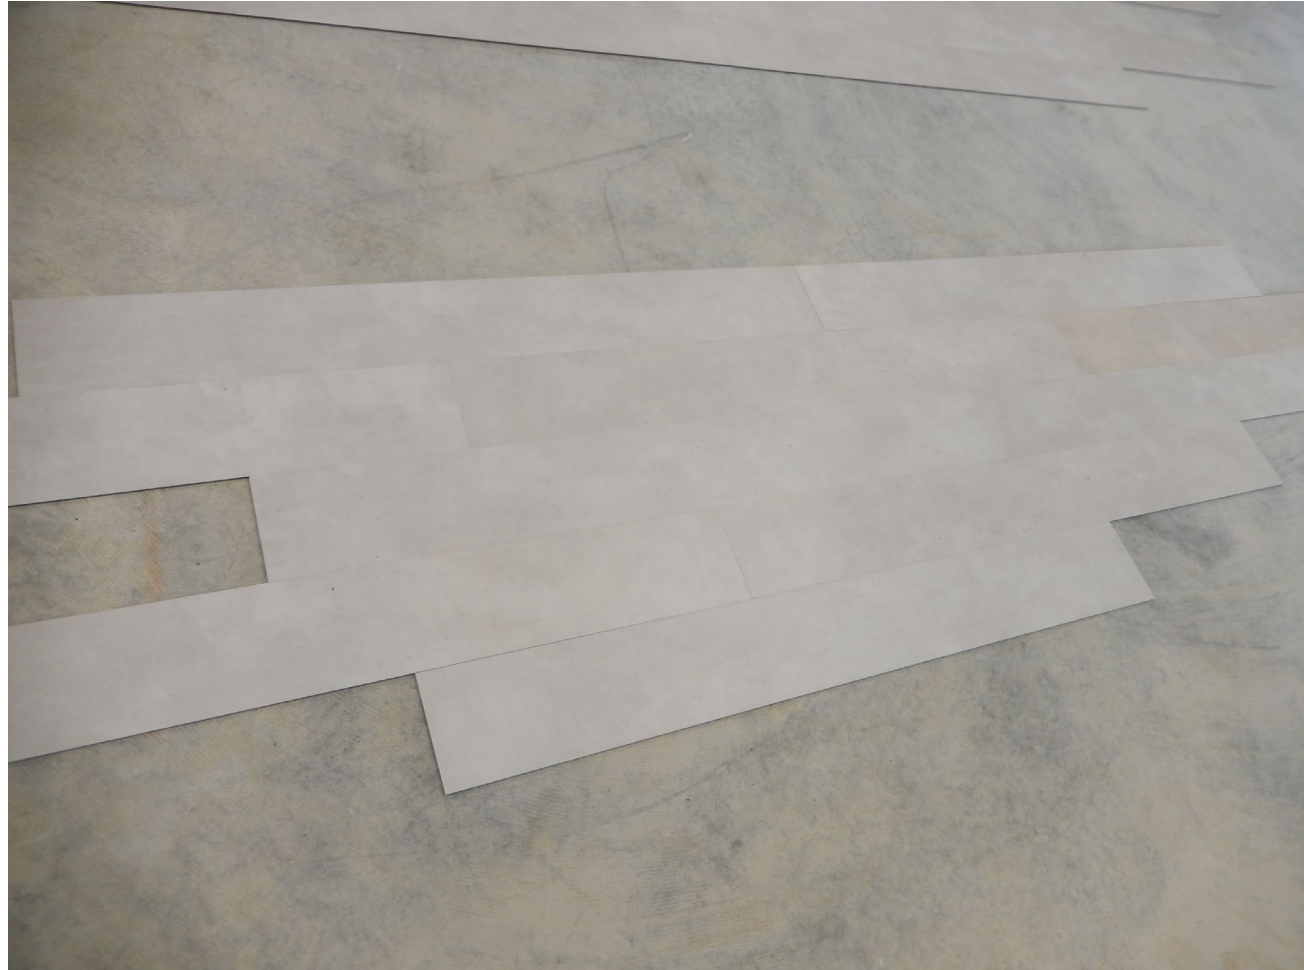

Week Ending May 10, 2024



The HILL - The Hub for Innovative Learning & Leadership

Rubber floor tile staged and ready for install at Law Enforcement



Week Ending May 10, 2024



The HILL - The Hub for Innovative Learning & Leadership

Health Sciences lab prepped for LVT install



Week Ending May 10, 2024
