


#### **Completed Work:**

- Release 1 ACM Panels Complete at Area F
- Prep Mow Strips by Curbs. Pouring on 5/30
- Blackout Ceilings Completed at A 1<sup>st</sup> Floor as well as 1<sup>st</sup> coat in misc. Mechanical Rooms
- Continue Setting Structural Steel at Area E/F G301 Mechanical Platform as well as Bar Joist and Decking at Area E Main Roof
- > Roofing Completed at B Platform. Start at Main Flat Roof of Area B and D
- Continue Exterior Framing at Platform of C ahead of Panels and Area E Cafeteria Walls
- Sheetrock Area A 2<sup>nd</sup> Floor Classrooms as well as Finishing
- Foundation Drain around Area F
- Geothermal Complete

#### Upcoming Work/Look Ahead:

- Start Standing Seam Panels above Brick
- Finish Structural Steel and Decking at Gym Entrance Lobby
- Continue Brick Veneer at Courtyard between C and E as well as Area A South Wall
- Start Stone and Brick Veneer at Area B
- Start Blackout Ceilings at A 2<sup>nd</sup> Floor
- Continue Terrazzo Area A 1<sup>st</sup> Floor A then move to 2<sup>nd</sup> Floor
- Continue Site Work Prep (Prep Island, Sidewalks, etc.)
- Start Installing Sheetrock at Soffits Area C First Floor
- Start Interior Framing in Cafeteria
- Continue Exterior Framing at Area E and Work towards Area A and C ahead of ACM Panels






Aerial – Overall Site





Area A – Terrazzo Layout Beginning

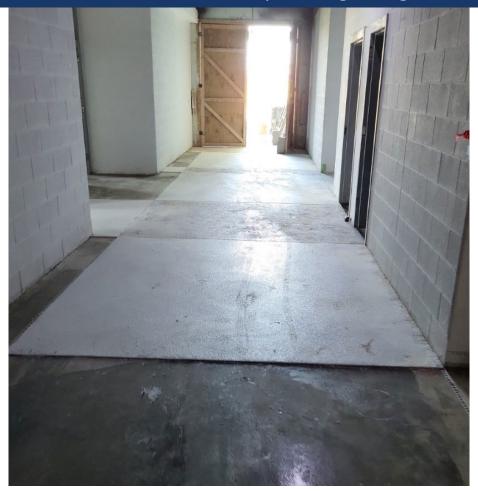




Area E – Brick Continuing around Cafeteria





Area E – Furring for ACM Panels Starting

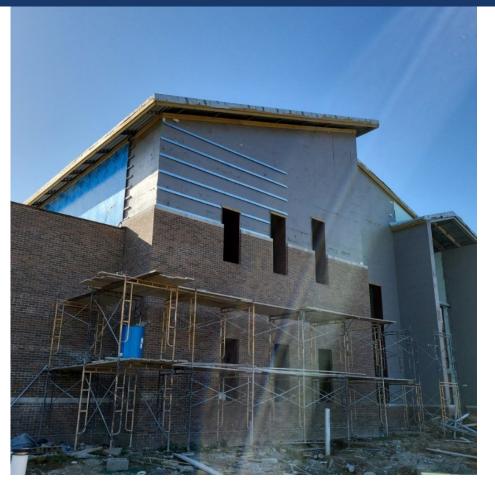



Area F – ACM Panels and Brick at Gym





Area F – Brick Continuing around Cafeteria





Area F – Cooler Freezer Set





Overall – Classroom Wings Air Barrier Continues

