




Mary E. Britton Middle School

➤ Completed Work:

- Start Storm Drain Installation and Layout North of Gym Area F
- Prep Main Islands to Grade and prep Mow Strips at Back of Curb and Gutter
- Fire Sprinkler Rough Ins at Area C 2nd Floor
- Start Blackout Ceiling Area A 2nd Floor. Prime Classrooms Area A 2nd Floor following Drywall
- Continue Setting Bar Joists and Decking at Second Floor/Low Roof Area F beside Gym Lobby Corridor as well as A Frames and bracing at High Roof of Area E/Gym Lobby Entrance
- Continue Roof Insulation, Cover Board and Membrane Roofing at Main Roof of Area D
- Continue Exterior Framing at Stage South Walls ahead of Panels and Area E Cafeteria Walls into Area C Exterior
- Terrazzo Floor Prep at Middle Corridors of A 1st Floor, First Hallway Near Completion

➤ Upcoming Work/Look Ahead:

- Continue Structural Steel and Decking at Gym Entrance Lobby. High Roof and Low Roof
- Continue Brick Veneer at Area C and Area A, Then move to exterior Area B
- Start ACM Panels at Area E Cafeteria Side, then move to Area C and A
- Start Stone and Brick Veneer at Area B
- Continue Terrazzo Area A First Floor
- Continue Membrane Roofing at Flat Roof of Area D then move to Storm Shelter/Area E
- Continue Hanging Sheetrock at Area C 1st Floor
- Continue Blackout Ceilings and Priming Classrooms Area A 2nd Floor

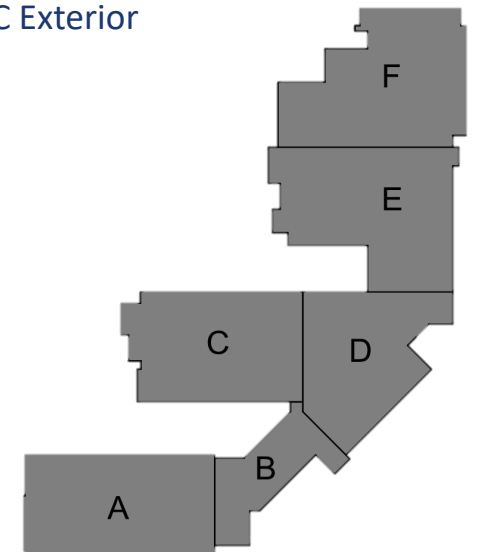

Mary E. Britton Middle School



Area A – Brick Continues



Week Ending June 7, 2024



Mary E. Britton Middle School

Area A – Interior Drywall Finishing Continues






Mary E. Britton Middle School

Area A – Terrazzo in Corridor



Mary E. Britton Middle School



Area B – Admin Stud Walls Complete



Week Ending June 7, 2024

Mary E. Britton Middle School



Area B – Roofing Continues



Week Ending June 7, 2024

Mary E. Britton Middle School



Area C – Brick Continuing




Week Ending June 7, 2024



Mary E. Britton Middle School

Area C – Furring for Metal Panels Continue

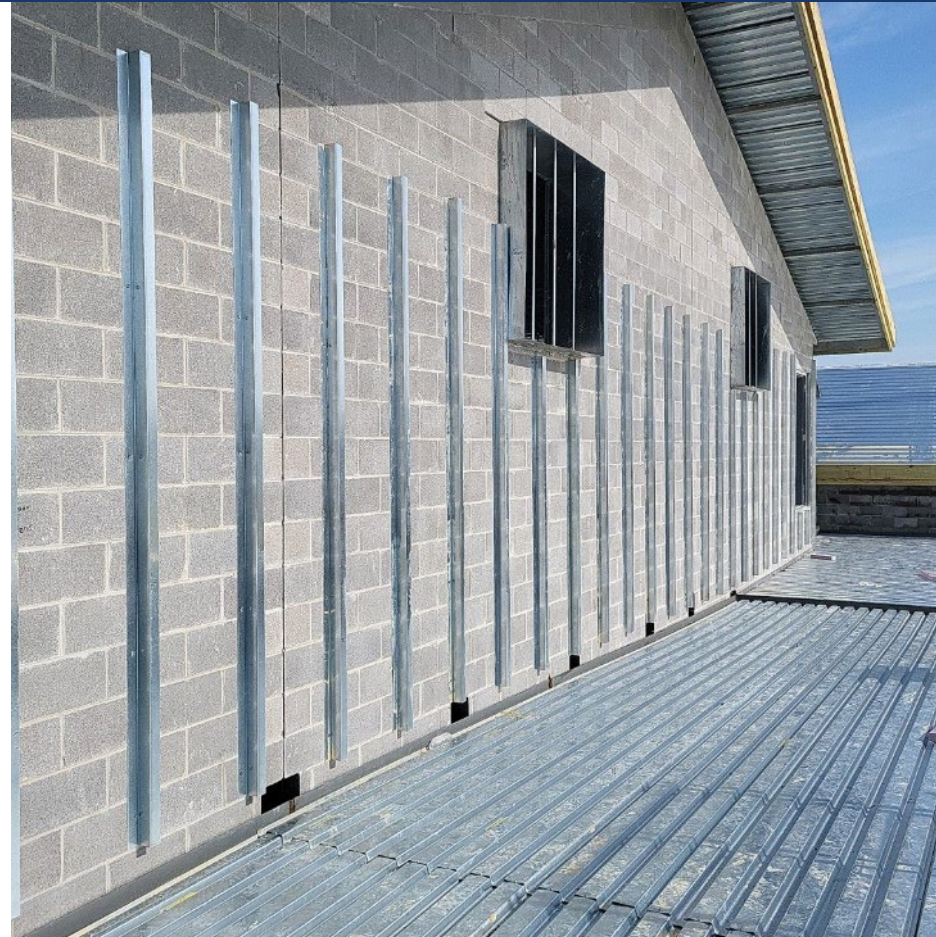


Week Ending June 7, 2024



Mary E. Britton Middle School

Area C – Tile Continues in the Restrooms

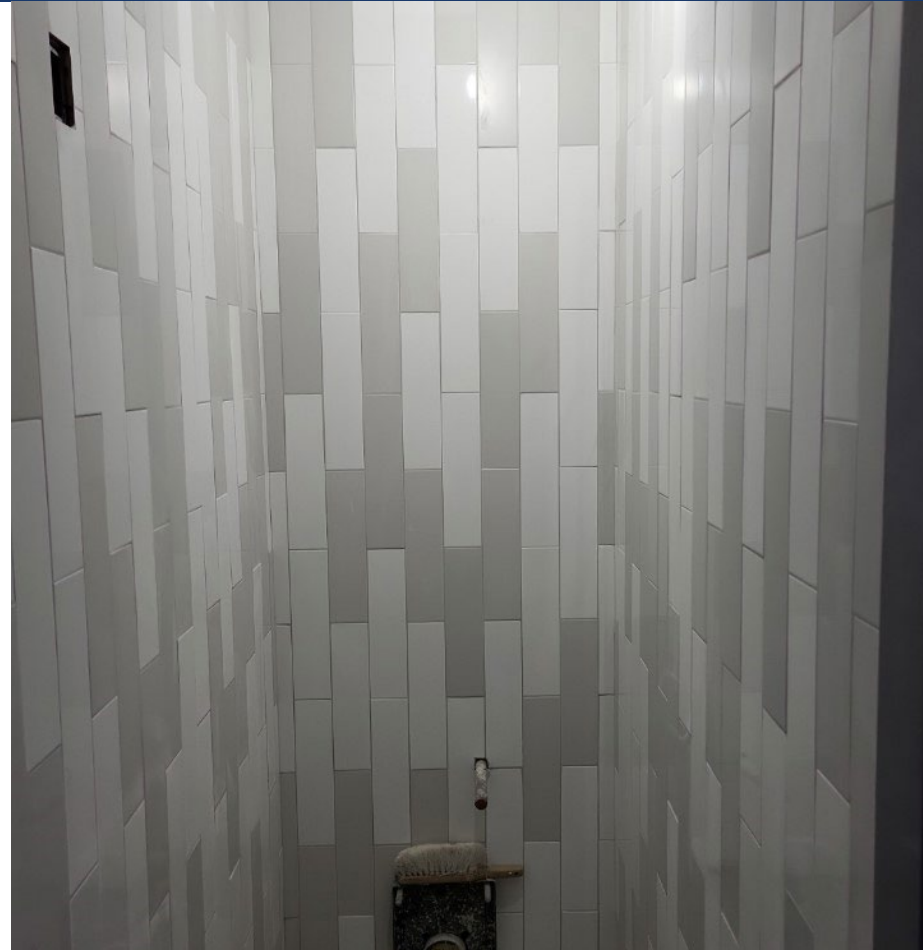

Week Ending June 7, 2024
