




Mary E. Britton Middle School

➤ Completed Work:

- Continuing Storm Sewer Installation
- Starting Site Concrete (Sidewalks)
- Prep for remaining curb and gutter
- Structural Steel Area E/F Corridor and Decking E/F Corridor
- Interior CMU non bearing continuing. All areas to 95%
- Brick Veneer Complete Area C and Area E (Cafeteria) and veneer at Area A at 90%
- Start Stone Veneer Area B
- Mod Bit Roof Area B dried in. Continuing thru Area D
- Received release 2 of MCM Panels
- Remaining Air Barrier will finish this week.

➤ Upcoming Work/Look Ahead:

- Finish All Structural Steel and Decking this week
- Start Stairs at Area A
- Continue Storm Sewer
- Pour Dock Roadway and Sidewalks
- Final Grade Islands behind sidewalk, Seed and Straw
- Continue Stone and Brick Veneer and non-bearing CMU Infills
- Continue Exterior Framing and Waterproofing
- Continue Interior Framing and Sheetrock
- Continue flat roof install and start roof panels
- Continue MEP all areas and continue Controls Install

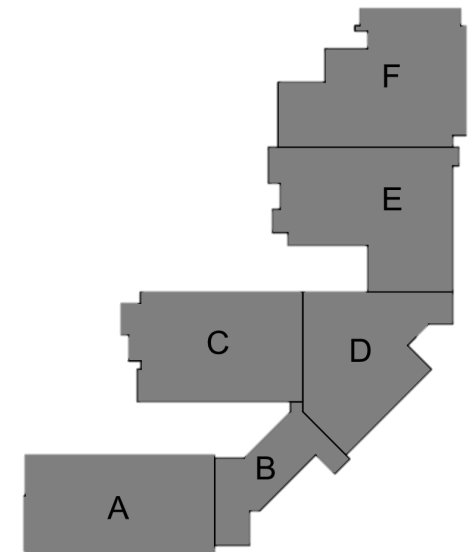

Mary E. Britton Middle School



Area A – Accent Paint Continues



Mary E. Britton Middle School



Area A – Brick Continues



Week Ending June 14, 2024


Mary E. Britton Middle School



Area A – Terrazzo Continues in Corridors



Mary E. Britton Middle School



Area B – Limestone Started at Media Center



Week Ending June 14, 2024

Mary E. Britton Middle School



Area E – Brick Complete at Cafeteria



Week Ending June 14, 2024

Mary E. Britton Middle School



Area E – Brick Complete at the Cafeteria



Week Ending June 14, 2024

Mary E. Britton Middle School




Site- Pouring Concrete Sidewalks



Week Ending June 14, 2024

Mary E. Britton Middle School



Area E – Roofing Continues



Week Ending June 14, 2024
