


#### **Completed Work:**

- Loading Dock Road Prepped and being Poured on 6/20
- Structural Steel at Gym Lobby Corridor 90% Complete
- > Interior CMU Non-Bearing Chase Walls Near Completion Following Other Trades
- Continue Brick Veneer at Loading Dock and Area F Gym Dock Entrance
- Brick Veneer Area A Complete, Continue Brick and Stone Veneer Area B and Working through Area D
- Modified Bit. Roofing Area D 85% then move to Area E
- > Continue Standing Seam Metal Roof Prep Area A (Fascia, Gutter, Ridging, Etc.) Multiple Shipment of Panels has Arrived
- Start Standing Seam Metal Roof Prep Area C
- Sheetrock and Framing Area A 2<sup>nd</sup> Floor Complete
- Interior Framing at B 1<sup>st</sup> Floor Complete


#### Upcoming Work/Look Ahead:

- Finish All Structural Steel and Decking Within Next Week
- Continue Exterior Canopy Work at Area F, Start Canopy Embeds and Installation Around Building
- Continue Storm Sewer and Site Concrete Layout and Installation
- Grade Islands Following Site Concrete Pours
- Blackout Ceiling and Painting Area C
- Continue stone and Brick Veneer Area B and Area D
- Continue Exterior Waterproofing following Framing
- Start Installing roof panels
- Continue Modified Bit. Roofing at Area D and Work to Strom Shelter/E Corridor
- Continue Duct Connections and Rough-Ins





Area A – Brick is Complete

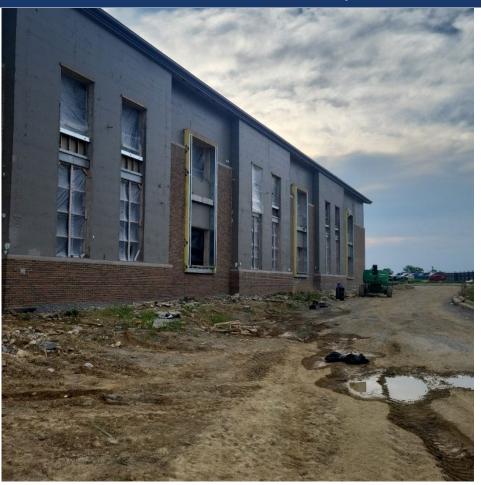



Area B – Low Slope Roofing Continues






Area C – Soffits are Continuing





Area C – Terrazzo has Started

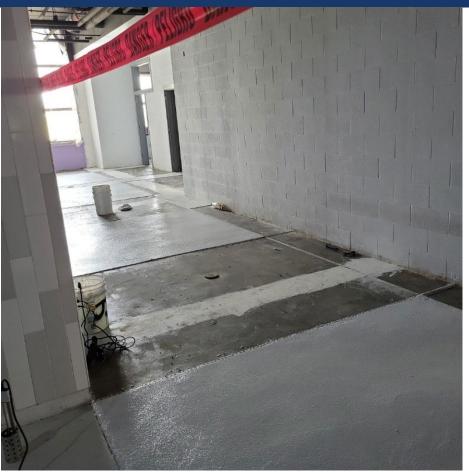



Area C – Vertical Metal Sheathing Installing






#### Area D – Stone has Started at Media Center



Area F – Bus Canopy Framing Continues

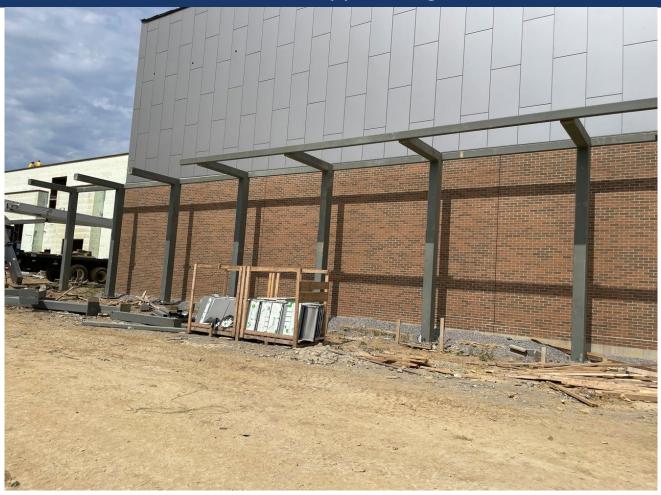



Site – Sidewalks Continue Around Building

