


Completed Work:

- > Stone Complete and Brick at Area D Near Completion
- Continue Brick Veneer into Area E
- Continuing CMU Chase Walls Area E/F and Plumbing Walls at Strom Shelter Restrooms
- Angle Welds at Decking of Main Entrance and Hollow Core Bracing at C 2nd Floor
- > Sheetrock Finishers at Area C 1st Floor Soffits and Classrooms
- Continuing Terrazzo Prep and Pours over Next 3 Days Area A 1st Floor. Tile is Complete at Restrooms
- Continuing Modified Bit Roof at Storm Shelter Roughly 50% Complete
- Water Tie Ins Near Completion Area B 1st Floor
- Control Testing has started at Area C 1st and 2nd Floor and Area E


Upcoming Work/Look Ahead:

- Continue Site Concrete and Layout (Sidewalk Prep), Curb and Gutter Layout
- Continue Spreading Topsoil and Grading of Islands
- Continue Brick at Area E. Brick Completion within 3 weeks
- Continue Site Utility Work
- Continue Exterior Framing at Area C into Area A, Interior Framing and Window Prep
- Continue MCM panel Installation Area E into Area C
- Continue Modified Bit Install at Strom Shelter Roof
- Continue MEP and Sprinkler Rough in Multiple Area
- Continue Controls Testing in Area C as Well as Area E





Area A – Blackout Paint Above Ceiling

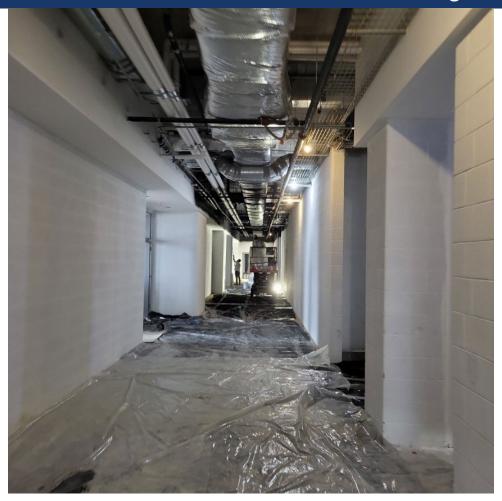



Area C – Drywall Soffits Continue






Area C – Metal Furring For ACM Panels Continues





Area C – Metal Roof Panels Continue

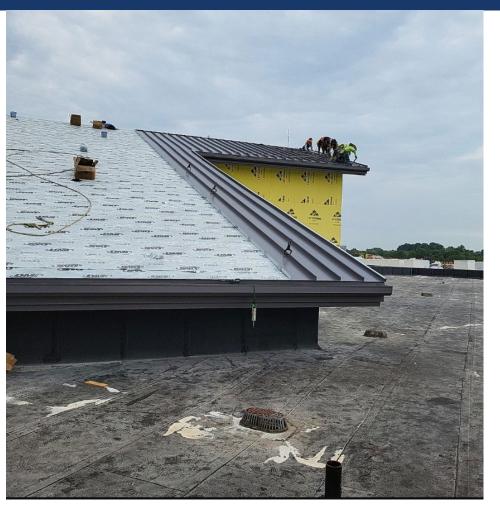



Area D – Media Center Limestone Veneer Complete





Area E – Cafeteria ACM Panels Continue





Site – Curbs and Sidewalks Continue





Site – Seed and Straw has Started

