

# HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



## School Site Improvement Projects

Regular Board Meeting  
July 18, 2024

Business Services



# PROJECT COMPLETE LIST

## 2023-2024/2025



Site	Item Description	Funding Source	Completed Date
Los Altos Elementary	Basketball Court Restriping	Facilities	05/2024
Valinda School of Academics	Basketball Court Restriping	Facilities	05/2024
Grandview College Preparatory Academy	Kitchen Upgrade (Serving Areas and Walls)	Facilities	05/2024
Palm Elementary	Campus Safety Fencing	Facilities	06/2024
La Puente High School	Little Theatre Improvement	CTE Grant	06/2024
Nelson Elementary Child Development	Restroom Flooring	Child Development	06/2024
Lassalette Elementary Child Development	Restroom Flooring	Child Development	06/2024
Sierra Vista SSC	Front Office Counter	Child Development	06/2024
Wilson High School	Little Theatre Improvement	CTE Grant	07/2024
Districtwide	Banners	Facilities	07/2024

# Projects Completed as of July 18, 2024

## Los Altos Elementary - Restriping Basketball Courts

**NEW!**



**BEFORE**



**AFTER**



# Projects Completed as of July 18, 2024

**NEW!**

## Valinda School of Academics - Restriping Basketball Courts

**BEFORE**




**AFTER**



# Projects Completed as of July 18, 2024

## Grandview – Before Kitchen Improvements

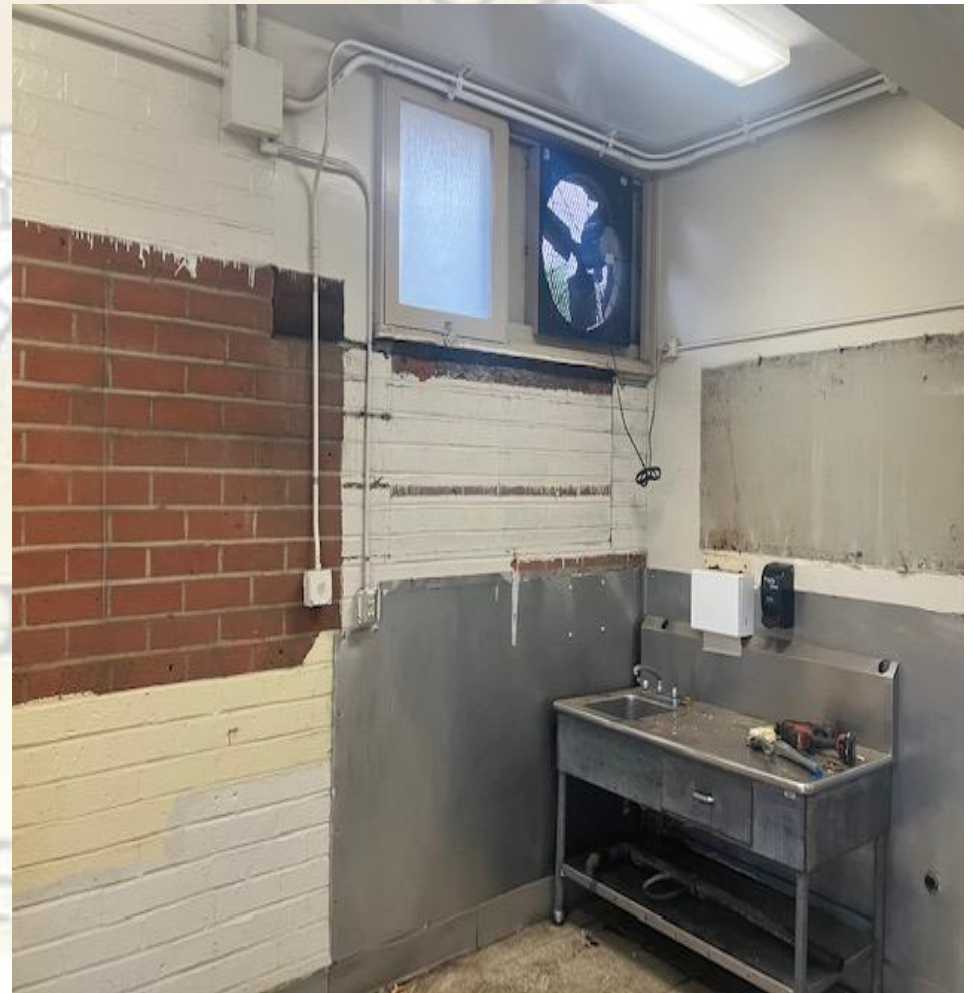

# Projects Completed as of July 18, 2024

## Grandview – After Kitchen Improvements



# Projects Completed as of July 18, 2024

## Palm Elementary – Safety Fencing

**NEW!**

**BEFORE**



**AFTER**




# Projects Completed as of July 18, 2024

La Puente High School - Little Theatre

**NEW!**

**BEFORE**

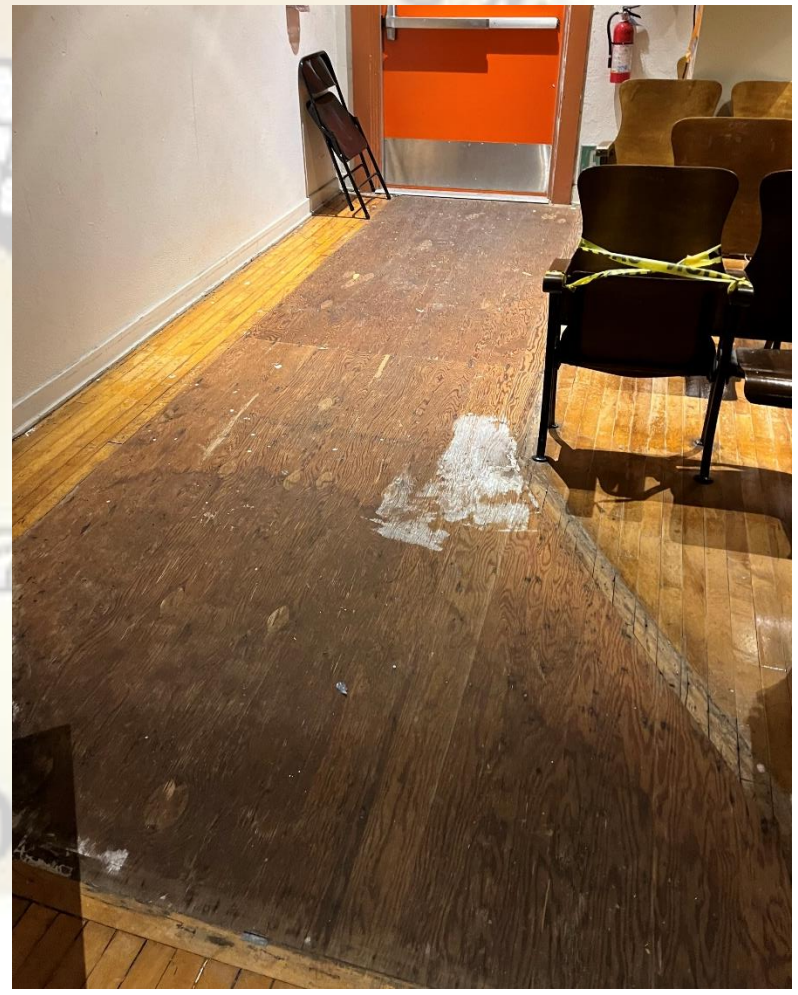





# Projects Completed as of July 18, 2024

## La Puente High School - Little Theatre

**NEW!**


**AFTER**

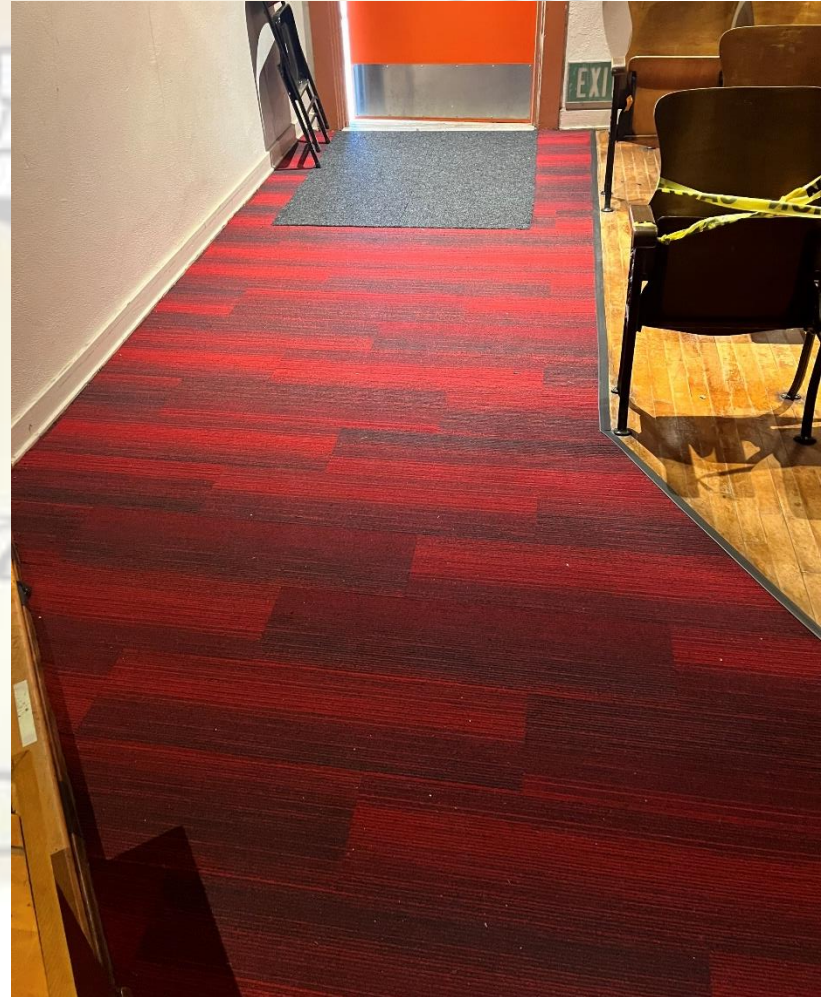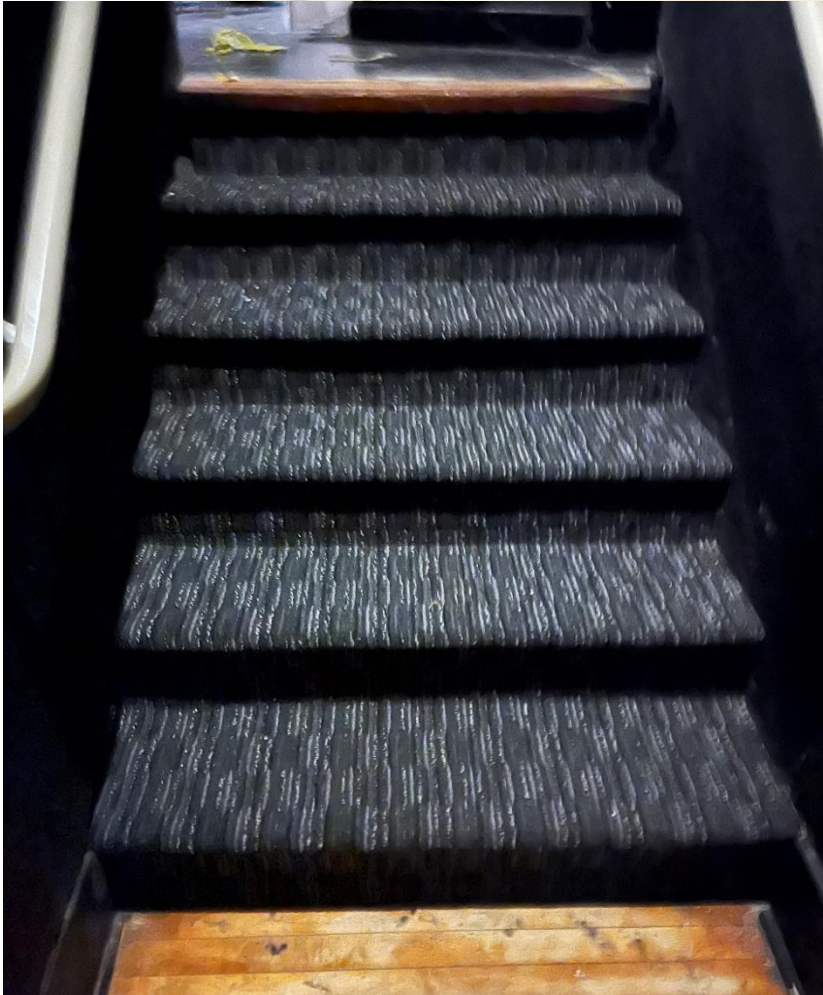


# Projects Completed as of July 18, 2024

## Lassalette Elementary Child Development - Restroom Flooring

**BEFORE**

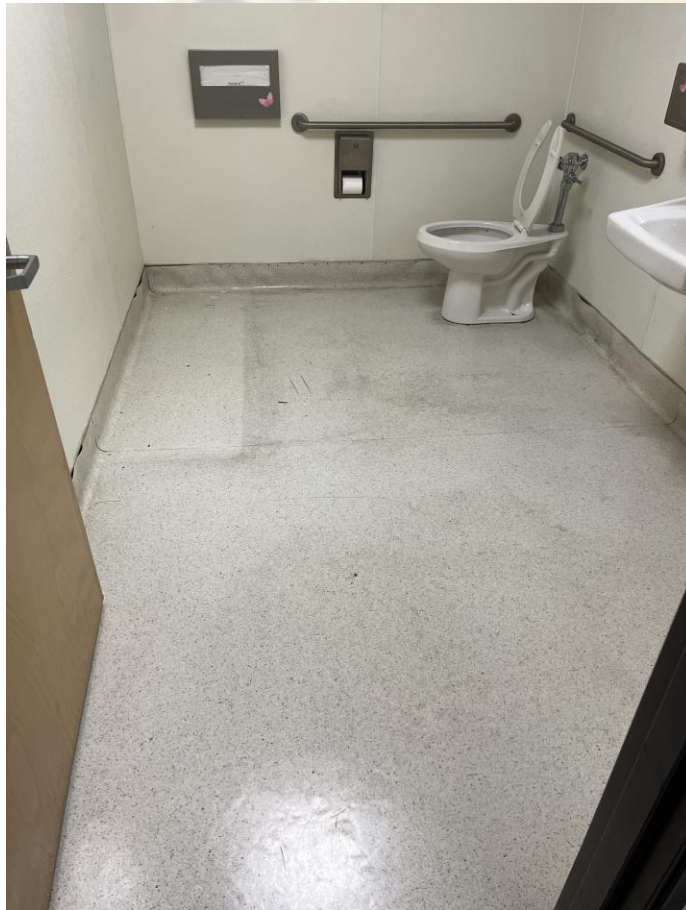

**AFTER**

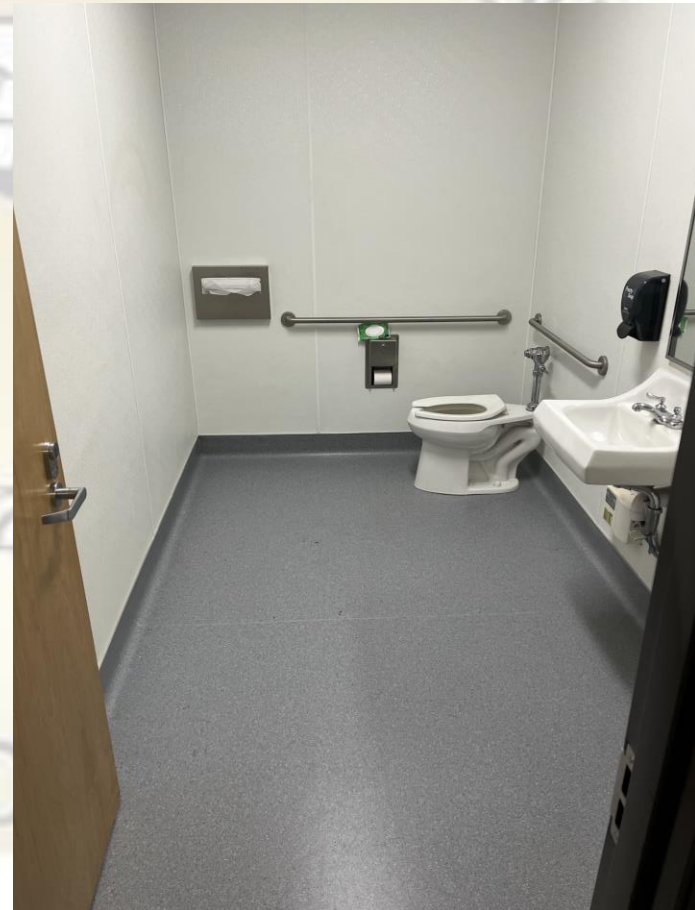

# Projects Completed as of July 18, 2024

## Sierra Vista SSC - Front Office Counter

**NEW!**

### NEW FRONT COUNTER



# Projects Completed as of July 18, 2024

## Districtwide - Banners

**NEW!**



# Projects In Progress

2024-2025



# Projects in Progress as of July 18, 2024


## Facilities

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Wedgeworth	K-5 Permanent School	Complete	Approved	Complete	In Progress	COPS	06/2025
Los Altos High School	Gym & Locker Room HVAC (65 tons of temporary HVAC units have been installed)	Complete	Approved	Complete	In Progress	Facilities	12/2024
Cedarlane Academy	Portable Installation	Complete	Approved	Complete	In Progress	Facilities	08/2024
Sparks Middle School	Front Office Counter	NA	NA	Pending	Pending	Facilities	TBD

# Projects In Progress as of July 18, 2024

Los Altos High School - Locker Room

**NEW!**

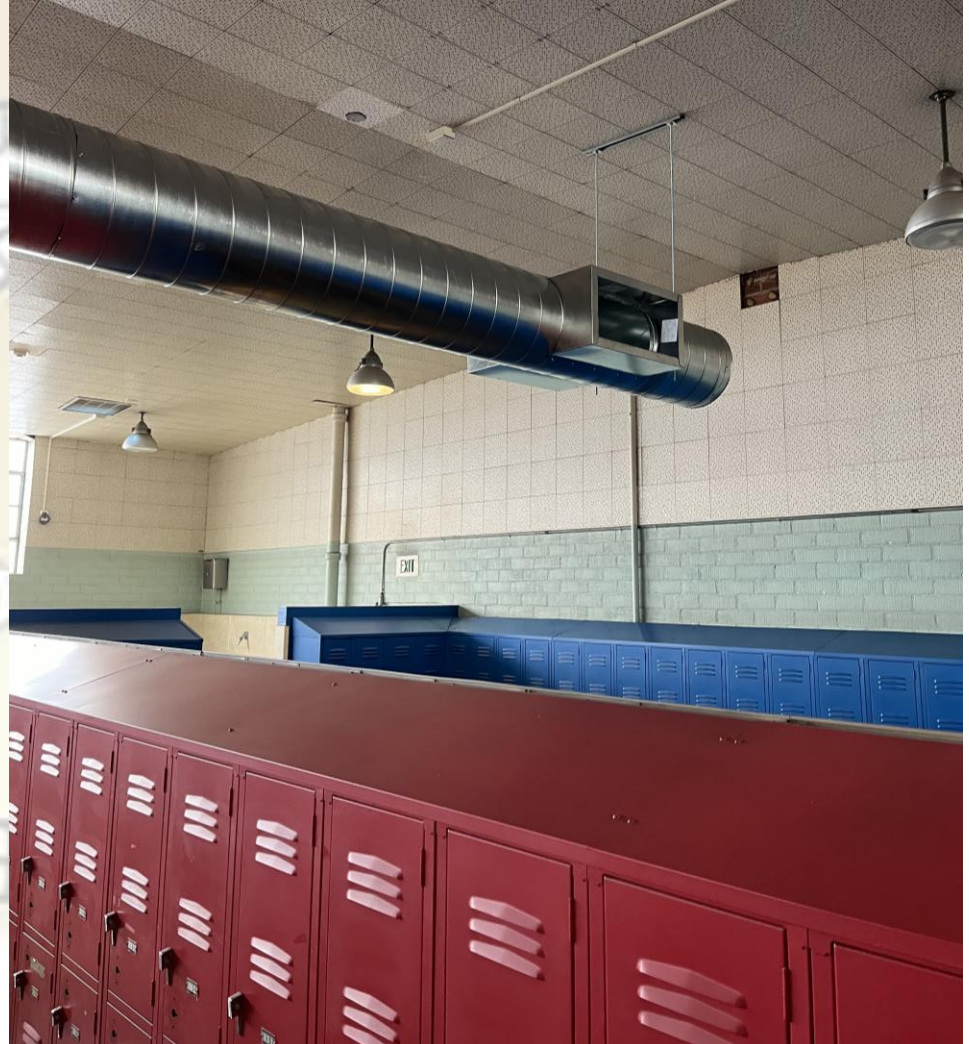

# Projects in Progress as of July 18, 2024

## Facilities

Site	Item Description	Procurement	Construct	Funding Source	Target Completion Date
Amar Children's Center	Phase II of re-roofing	Complete	In Progress	Facilities	TBD
Baldwin Academy	Phase II of re-roofing	Complete	In Progress	Facilities	TBD
Dibble Adult	Phase II of re-roofing	Complete	In Progress	Facilities	TBD
Grazide Elementary	Phase II of re-roofing	Complete	In Progress	Facilities	TBD
Kwis Elementary	Phase II of re-roofing	Complete	In Progress	Facilities	TBD
La Puente High School	Phase II of re-roofing	Complete	In Progress	Facilities	TBD
Los Molinos Elementary	Phase II of re-roofing	Complete	In Progress	Facilities	TBD
Stimson Learning Center	Phase II of re-roofing	Complete	In Progress	Facilities	TBD
Wilson High School	Phase II of re-roofing	Complete	In Progress	Facilities	TBD



# Projects In Progress as of July 18, 2024

## Kwis Elementary - Roofing



# Projects In Progress as of July 18, 2024

## Los Molinos Elementary - Roofing



# Projects in Progress as of July 18, 2024

## Child Development

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Winglane Elementary Head Start	Portable Installation	Complete	Approved	Complete	Complete	Child Development	07/2024
Nelson Elementary Head Start	Playground, Shade Structure, & Accessibility Path of Travel	Complete	Approved	Complete	In Progress	Child Development	TBD
Fairgrove Academy Head Start	Playground & Shade Structure	Complete	Approved	Complete	In Progress	Child Development	TBD
Workman Elementary Head Start	Playground & Accessibility Path of Travel	Pending	Pending	Complete	In Progress	Child Development	TBD
Amar Children's Center	Entry Security Project	Complete	Approved	Pending	Pending	Child Development	TBD

# Projects in Progress as of July 18, 2024

**NEW!**

## Winglane Elementary Head Start Portable Installation- Demolition

**BEFORE**



**AFTER**



# Projects in Progress as of July 18, 2024

## Special Education

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Lassalette Elementary	Inclusive Playground	NA	NA	Complete	Pending	Special Ed	TBD

## Adult Education

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Willow Adult Ed	Marquee	Complete	NA	Pending	Pending	Adult Ed	TBD
Dibble Adult Ed	Admin Upgrade	In Progress	NA	Pending	Pending	Adult Ed	TBD
Center for the Performing Arts	Construction of NEW Performing Arts Center @ Temple Academy	Complete	Complete	Pending	TBD	Adult Ed	TBD

# Projects in Progress as of July 18, 2024

## Nutrition Services

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
District Office	Warehouse Freezer	Complete	NA	Pending	TBD	Food Services	TBD
Wilson High School	Kitchen Modernization	Pending	Pending	Pending	TBD	Food Services	TBD
Mesa Robles Middle School	Kitchen Renovation	Complete	Pending	Pending	TBD	Food Services	TBD
Baldwin Academy	Kitchen Renovation - Three Compartment Sink Installation	Complete	NA	Pending	TBD	Food Services	TBD

# Facilities Upcoming Projects

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
Districtwide	HVAC System Replacement	Pending	Pending	Pending	TBD	TBD
Kwis Elementary	Baseball Fields	Complete	Approved	Pending	TBD	TBD
Los Altos High School	Stadium Press Box & Bleachers	Pending	Pending	Pending	TBD	TBD
<b>La Puente High School</b>	<b>Custom Shade Structure</b>	<b>Complete</b>	<b>Approved</b>	<b>In Process</b>	<b>TBD</b>	<b>TBD</b>
Wilson High School	Stadium Press Box & Bleachers	Complete	Pending	Pending	TBD	TBD
Workman High School	Phase II Stadium and Baseball Field (Phase I Track & Field and Softball Field Complete) OPTION B	Complete	Approved	Pending	Estimated	TBD (14-18 months after Board approval of the Bid)
<b>Workman High School</b>	<b>Shade Structure, Wall, &amp; Lighting</b>	<b>In Progress</b>	<b>Pending</b>	<b>Pending</b>	<b>TBD</b>	<b>TBD</b>



**Next Report – August 22, 2024**
