


Mary E. Britton Middle School

➤ Completed/Work in Progress:

- Continue Site Concrete at Loading Dock and continue Geothermal Field Grading
- Continue MCM Panels at Stage High Roof
- Continue Stair and Rails Area A1 and D1
- Continuing Exterior Framing at Area A and C Ahead of Panels
- Continue Interior Stud Framing at Area B and C
- Continue Peel and Stick Membrane at Area E Windows into C Ahead of Panels and a Main Roof
- Continue Prime and Paint in Mechanical Rooms and blackout ceilings
- Continuing Sheetrock Finishing at Soffits and Classrooms
- Continue Terrazzo Pours 1st floor Area A and Tile at 2nd Floor Area A
- Continuing Modified Bit at Storm Shelter and Finish Standing Seam Panels at Area A and C Roof

➤ Upcoming Look Ahead:

- Continue Site Concrete at Courtyards and Layout and Curb and Gutter Grading
- Continue Stair and Rail Install and Welds
- Continue Peel and Stick Exterior
- Continue Exterior Furring, Interior Framing and Sheetrock Hanging and Finishing
- Continue MCM Panel Installation Area F and Area E Above Flat Roof
- Start Standing Seam Panels at Cafeteria Roof
- Start Terrazzo at Area A 2nd Floor and Continue Tile at Area A 2nd Floor
- Continue Modified Bit Install at Strom Shelter Roof
- Continue Standing Seam Panels at Area C Roof then move to cafeteria Roof
- Continuing MEP and Sprinkler Rough in

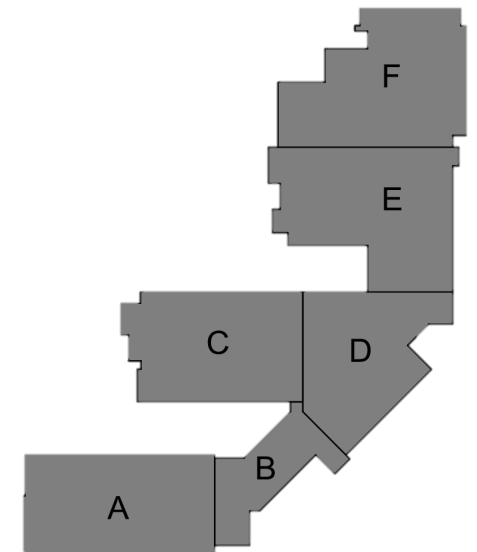

Mary E. Britton Middle School



Overall Aerial – Site Progress



Week Ending July 26 2024

Mary E. Britton Middle School



Overall Aerial – Classroom Wings Progress



Week Ending July 26, 2024

Mary E. Britton Middle School



Site – Building Sign Started



Week Ending July 26, 2024

Mary E. Britton Middle School



Area A – Stair and Railings to 2nd Floor Installed



Week Ending July 26, 2024

Mary E. Britton Middle School



Area B – Front Entry Ready for ACM panels



Week Ending July 26, 2024

Mary E. Britton Middle School



Area B – Furring on Mechanical Room Started



Mary E. Britton Middle School



Area C – Terrazzo Continues



Week Ending July 26, 2024

Mary E. Britton Middle School



Area F – Kitchen Loading Dock



Week Ending July 26, 2024
