


# Mary E. Britton Middle School

## ➤ Completed/Work in Progress:

- Final Grading Finished Areas
- Masonry and Veneer Finishing and Demobilizing
- Installing Dense Glass Area A/C Courtyard
- Continue Soffit Framing Area B
- Continue Block Fill and caulking Area E and F
- Continue Tile Work at Bathrooms Area A 2
- Continue Terrazzo Install at Area A Second Floor
- Continue Prep of Window Openings
- Continue Sprinkler System Area B
- Continue Testing Plumbing, Hydronic Piping, Roof Drains and Equipment Install

## ➤ Upcoming Look Ahead:

- Finish Masonry CME and Veneers
- Continue Stairs, Handrails and Misc Steel
- Continue Exterior Framing and Gyp Install Area A. Area C Finished
- Finish Window Prep at Stala Frames
- Hanging and Finishing Area C Continuing and Finish Soffit Framing in Area B
- Tile Area A 2 and Terrazzo Install Area A2
- Continue Block Fill, Painting and Caulking Area E and F
- Finish Dry in all Flat Roofs
- Area E High Roof Standing Seam Panels to Begin
- Start Vertical Wall Panels area E and Courtyard

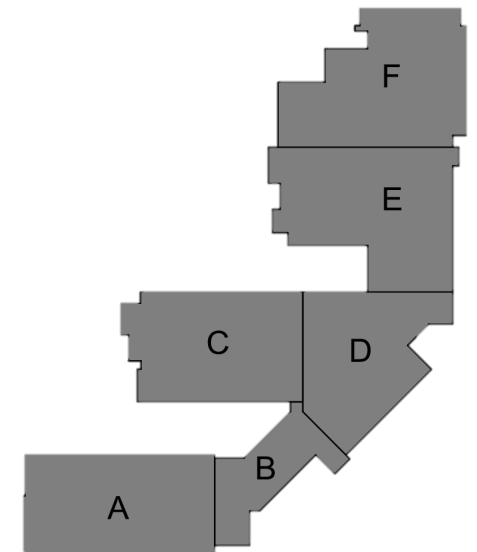

# Mary E. Britton Middle School



Site – Curbs and Sidewalks Continue



Week Ending August 2, 2024



# Mary E. Britton Middle School

Area A – Stair A at End Wall in Place



Week Ending August 2, 2024





# Mary E. Britton Middle School

## Area A – Accent Wall Paint Continues



Week Ending August 2, 2024



# Mary E. Britton Middle School

Area B – Block filler continues in Main Entry



Week Ending August 2, 2024

# Mary E. Britton Middle School

## Area B – Entry Roofing Continues



Week Ending August 2, 2024



# Mary E. Britton Middle School

## Area C – ACM Panels at Window Boxouts Continue



# Mary E. Britton Middle School



## Area D – Main Stair in Place



Week Ending August 2, 2024



# Mary E. Britton Middle School

## Area D – MEP Above Ceiling Continues

