


Mary E. Britton Middle School

➤ Completed/Work in Progress:

- Continuing Site Concrete
- CMU/Brick Complete
- Continuing Exterior Framing Area A
- Continuing Drywall Installation Area C1, Completed Drywall Area C 2nd Floor
- Continuing Exterior Metal Composite Panel at Area C
- Continuing Roof Installation Area E Cafeteria
- Continuing Exterior Membrane Waterproofing Area A and Area C
- Delivered Exterior Batten Seam Panels and Trim
- Continuing Sprinkler System Area D

➤ Upcoming Look Ahead:

- Continue Site Concrete at Ramp Area A and Prep For Curb Installation
- Continue Hauling Spoil Materials
- Install Stairs Area C
- Complete Roof Panels Area E Cafeteria
- Start Window Install Area F and Area B/D
- Start Soffit and Batten Seam Panels Area at Cafeteria/Area C Courtyard
- Continue Sheetrock Area D, Start Sheetrock Area B
- Complete Tile Area A2, Start Quarry Tile At Kitchen
- Complete Sprinkler Install Area D, Start Cafeteria

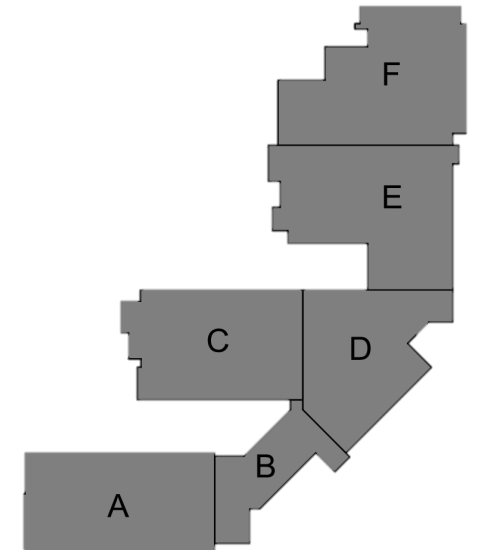

Mary E. Britton Middle School



Area A – 2nd Floor Terrazzo Prep



Week Ending August 16, 2024



Mary E. Britton Middle School

Area B – Electrical Rough Ins Continue In Admin Area



Week Ending August 16, 2024

Mary E. Britton Middle School



Area C – ACM Panels at Penthouse Continues



Week Ending August 16, 2024

Mary E. Britton Middle School

Area C – Canopy Embed Pocket Patching Continues at VoAG Lab




Week Ending August 16, 2024

Mary E. Britton Middle School



Area D – Stairs Pan and Railing Continue

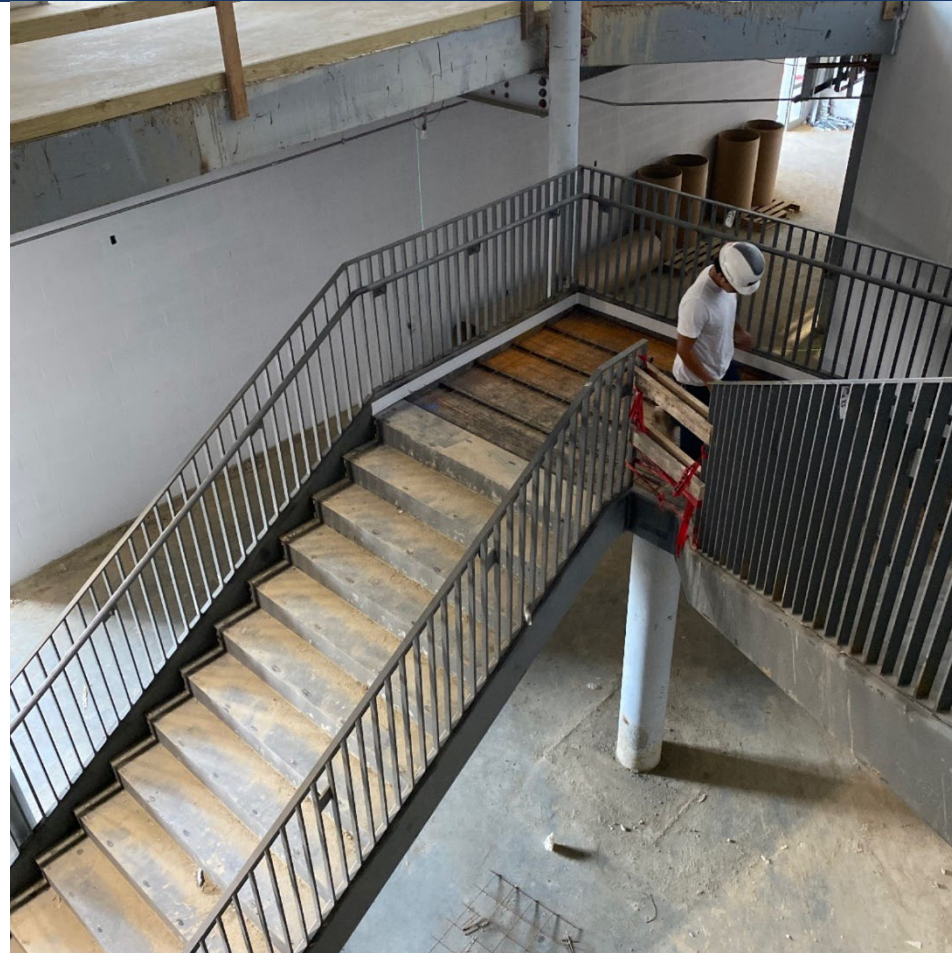

Week Ending August 16, 2024

Mary E. Britton Middle School



Area E – Cafeteria ACM Panels Continue



Week Ending August 16, 2024

Mary E. Britton Middle School



Area F - Bus Canopy Sidewalk



Week Ending August 16, 2024

Mary E. Britton Middle School



Area F - Kitchen Floor Ready for Quarry Tile



Week Ending August 16, 2024
