

# Measure BB Bond

21st Century Classroom Improvements  
August 22, 2024




CUMMING  
GROUP



# HLPUSD MEASURE BB - SUMMARY

## SCHOOLS IN PROGRESS

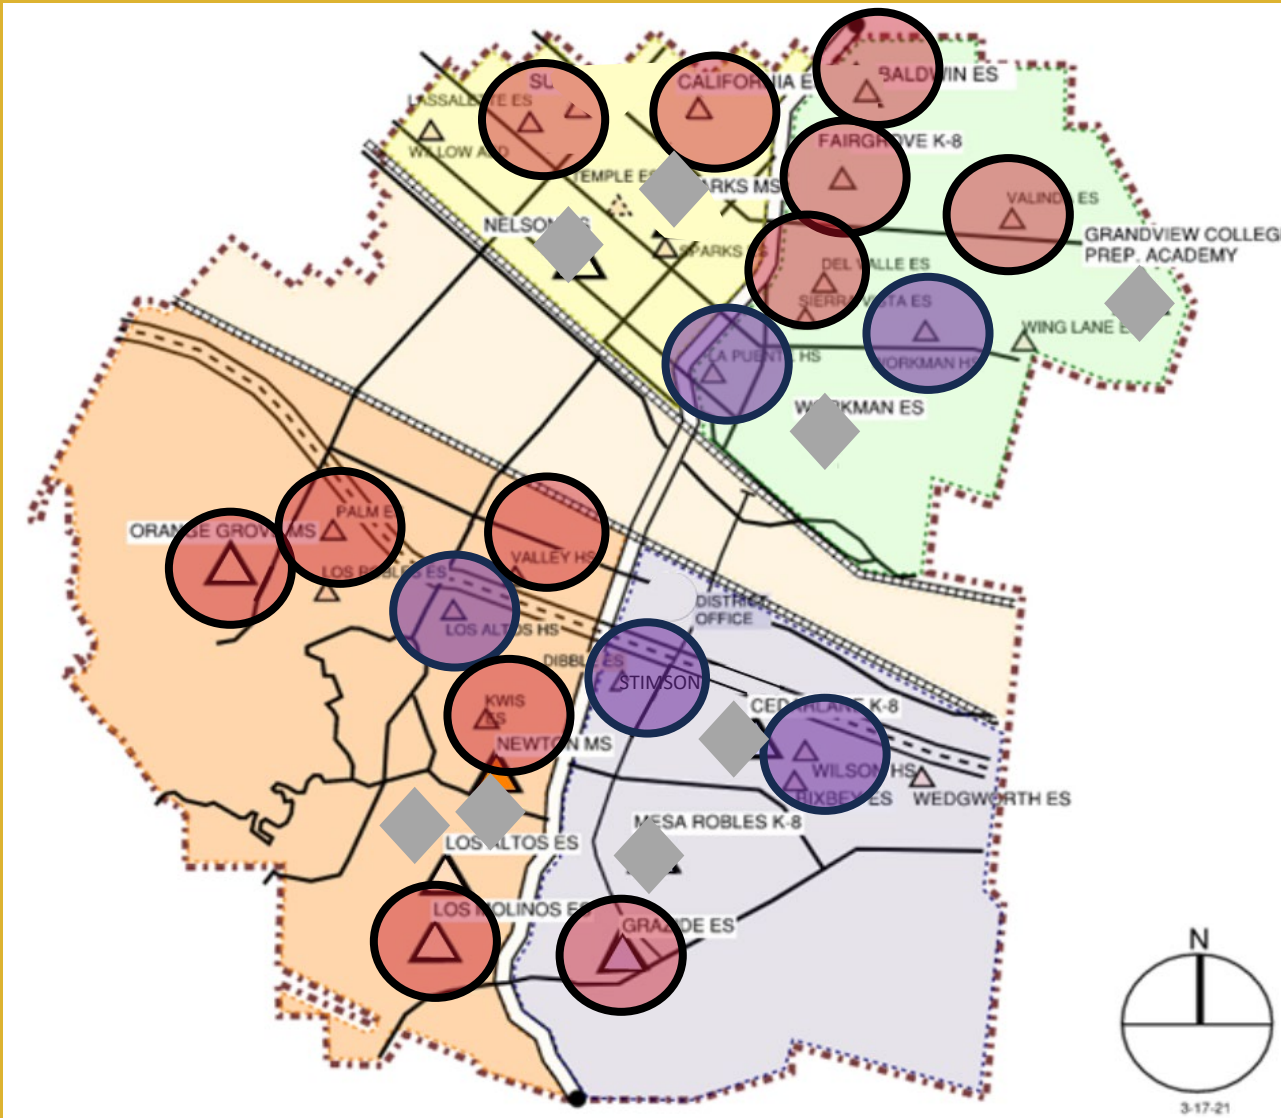

### IN PROGRESS CONSTRUCTION

- La Puente HS
- Workman HS
- Los Altos HS
- Wilson HS
- Stimson EC

### PREP FOR BID

- California ES
- Baldwin ES
- Los Molinos ES
- Grazide ES

### AT DSA FOR REVIEW

- Kwis ES
- Lassalette ES
- Fairgrove K-8

### IN DESIGN

- Orange Grove MS
- Sierra Vista MS
- Palm ES
- Valinda ES
- Sparks ES
- Wing Lane ES
- Valley Alternative

### COMPLETED

- Nelson ES
- Los Altos ES
- Workman ES
- Mesa Robles K-8
- Cedarlane K-8
- Sparks MS
- Newton MS
- Grandview K-8

# PHASE B PROGRESS

- |                  |                        |                                   |                    |
|------------------|------------------------|-----------------------------------|--------------------|
| 1. Baldwin ES    | Construction Documents | First Bid advertisement 8/14/2024 | Open Sept 17, 2024 |
| 2. California ES | Construction Documents | First Bid advertisement 8/14/2024 | Open Sept 17, 2024 |

## Anticipated Construction Start Fall of 2024

- |  |                        |                                   |                    |
|--|------------------------|-----------------------------------|--------------------|
| 3. Los Molinos ES                        | Construction Documents | First Bid advertisement 8/14/2024 | Open Sept 17, 2024 |
| • Interim Housing Los Robles (Tentative) |                        |                                   |                    |
| 4. Graziade ES                           | Construction Documents | First Bid advertisement 8/14/2024 | Open Sept 17, 2024 |
| • Interim Housing Bixby (Tentative)      |                        |                                   |                    |

## Anticipated Construction Start Winter of 2024

- |                  |                        |                               |                    |
|------------------|------------------------|-------------------------------|--------------------|
| 5. Kwis ES       | Construction Documents | <b>At DSA for Plan Review</b> | Submitted 8/9/2024 |
| 6. Lassalette ES | Construction Documents | <b>At DSA for Plan Review</b> | Submitted 8/9/2024 |

## Anticipated Construction Start New Year of 2025

- |  |                        |                         |                           |
|--|------------------------|-------------------------|---------------------------|
| 7. Palm ES                               | Construction Documents | <b>50% Const. Docs.</b> | District Review 8/16/2024 |
| • Interim Housing Los Robles (Tentative) |                        |                         |                           |
| 8. Valinda ES                            | Construction Documents | <b>50% Const. Docs.</b> | District Review 8/16/2024 |

## Anticipated Construction Start Spring of 2025

- |   |                        |                               |                     |
|---|------------------------|-------------------------------|---------------------|
| 9. Fairgrove K-8                        | Construction Documents | <b>At DSA for Plan Review</b> | Submitted 8/12/2024 |
| • Interim Housing Del Valle (Tentative) |                        |                               |                     |
| 10. Orange Grove MS                     | Construction Documents | <b>Schematic Design</b>       |                     |

## Anticipated Construction Start Summer of 2025

- |                                      |                        |                           |                            |
|--------------------------------------|------------------------|---------------------------|----------------------------|
| 11. Sierra Vista                     | Construction Documents | <b>Design Development</b> | District Reviewed 8/2/2024 |
| 12. Sparks ES                        | Construction Documents | <b>Design Development</b> | District Reviewed 8/2/2024 |
| • Interim Housing Sunset (Tentative) |                        |                           |                            |

## Anticipated Construction Start Summer -Fall of 2025

- |                        |                        |                           |                             |
|------------------------|------------------------|---------------------------|-----------------------------|
| 13. Wing Lane ES       | Construction Documents | <b>Design Development</b> | District Reviewed 9/17/2024 |
| 14. Valley Alternative | Construction Documents | <b>Design Development</b> | District Reviewed 9/17/2024 |

## Anticipated Construction Start Fall of 2025

# DSA PLAN APPROVAL GRAZIDE ELEMENTARY



Los Angeles Basin Regional Office | (213) 897-3995  
355 South Grand Ave. Suite 2100  
Los Angeles, CA 90071  
www.dsa.dgs.ca.gov

STATE OF CALIFORNIA  
GOVERNOR GAVIN NEWSOM

## 8/9/2024 - APPROVAL OF PLAN(S)

Dr. Alfonso Jimenez  
HACIENDA-LA PUENTE UNIFIED SCHOOL DISTRICT  
15959 EAST GALE AVENUE  
CITY OF INDUSTRY, CA 91745

**Project:** Grazide Elementary School  
**Total Scope of Project:** Alterations to 9-C.R. Bldgs. A, B, P3, P4, P8, P9, P10, P11, & P12. (A-22945, A03-100741, A03-105985, A03-111221).

**Increment #:** 0  
**Application #:** 03-124133  
**File #:** 19-38

Drawings and specifications for the subject project have been examined and stamped by the Division of the State Architect (DSA) for identification on 8/9/2024. This letter constitutes the "written approval of the plans as to the safety of design and construction" required before letting any contract for construction, and applies to the work shown on these drawings and specifications. The date of this letter is the DSA approval date.

Approval is limited to the particular location shown on the drawings and is conditioned on construction starting within four years from the stamped date. The inspector must be approved and the contract information, including the construction start date, must be given to DSA prior to start of construction.


DSA does not review drawings and specifications for compliance with Parts 3 (California Electrical Code), 4 (California Mechanical Code), and 5 (California Plumbing Code) of Title 24. It is the responsibility of the professional consultants named on the application to verify this compliance.

“Drawings and specifications for the subject project have been examined and stamped by the Division of the State Architect (DSA) 8/9/2024.”




HIGH SCHOOL  
REFRESH  
PROJECTS

# HIGH SCHOOL REFRESH GROUP 1

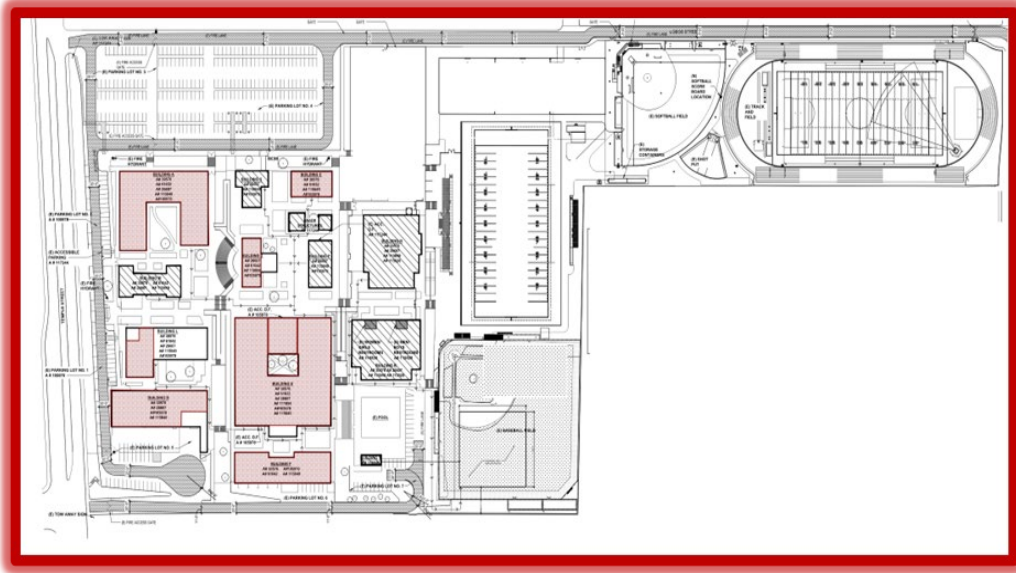

## WORKMAN HIGH SCHOOL

43 CLASSROOMS

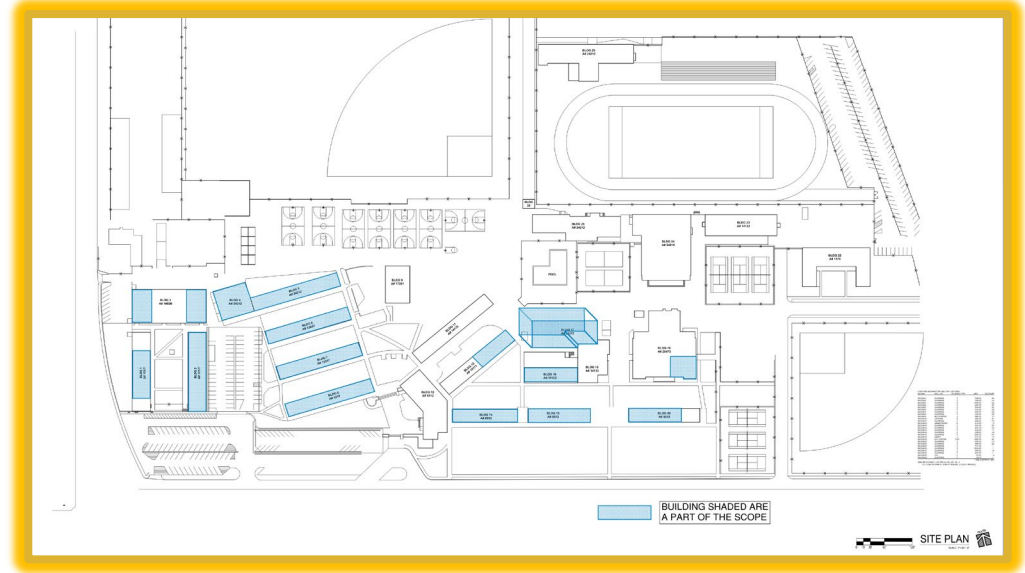

## LA PUENTE HIGH SCHOOL

55 CLASSROOMS

SCHOOL	START DATE	ANTICIPATED COMPLETION DATE
WORKMAN HS	1/16/2024	9/13/2024* 50 Days ahead of Schedule
LA PUENTE HS	1/16/2024	11/1/2024

# REFRESH GROUP 1

## Workman HS Phase 4: Classroom C-2



# REFRESH GROUP 1

## La Puente HS Phase 4: Classroom 106 Before and Progress




Before




In Progress




# HIGH SCHOOL REFRESH GROUP 2

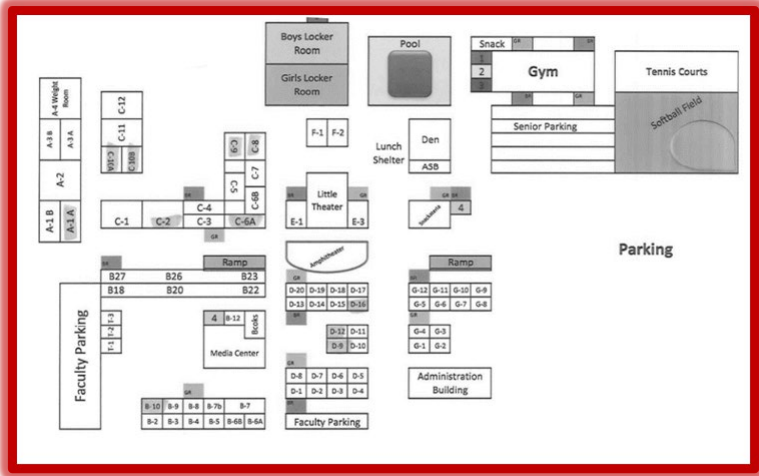

**WILSON HIGH SCHOOL**  
59 CLASSROOMS

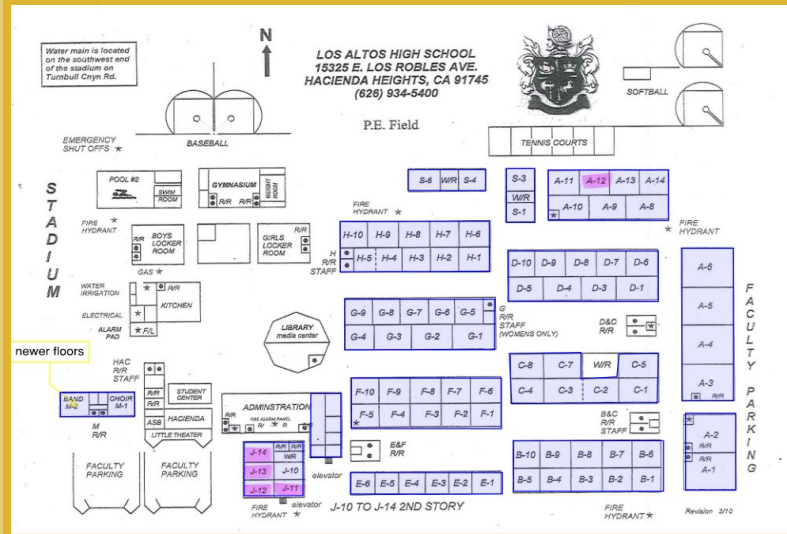

**LOS ALTOS HIGH SCHOOL**  
69 CLASSROOMS

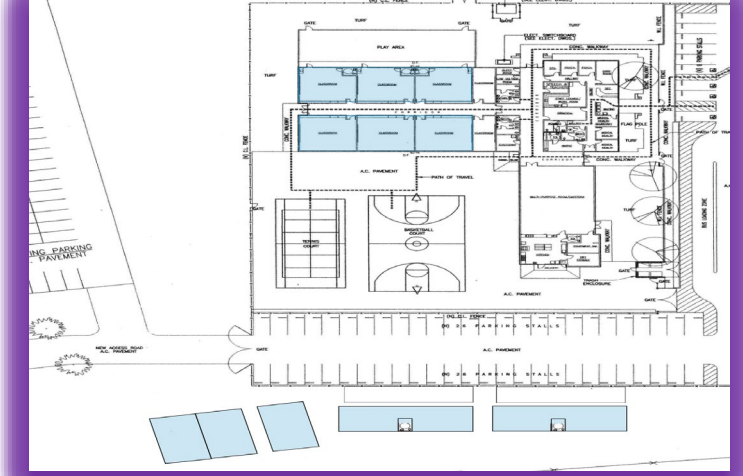

**STIMSON LEARNING CENTER**  
10 CLASSROOMS

SCHOOL	START DATE	ANTICIPATED COMPLETION DATE
WILSON HS	3/4/2024	2/21/2025
LOS ALTOS HS	3/4/2024	4/18/2025
STIMSON EC	7/1/2024	7/31/24 Completed

REFRESH GROUP 2  
Wilson HS Phase 2  
Classroom B-7 Before  
and After




# REFRESH GROUP 2

## Los Altos HS Phase 2 Classroom M-1.



REFRESH GROUP 2  
Stimson Learning Center  
Classroom Before and After





QUESTIONS
