# HACIENDA LA PUENTE UNITED SCHOOL DISTRICT











# School Site Improvement Projects

Business Services



# PROJECT COMPLETE LISTAPLETED 2024/2025

Site	Item Description	Funding Source	Completed Date
California	Bottle Filling Station	Facilities	08/2024
Cedarlane	Playground Asphalt	Facilities	08/2024
Cedarlane	Portable Installation	Facilities	08/2024
Grandview	Parking Lot Restriping	Facilities	08/2024
Los Molinos	Bottle Filling Station	Facilities	08/2024
Mesa Robles	Classroom Flooring	Facilities	08/2024
Wing Lane	Playground Restriping	Facilities	08/2024
Wing Lane	Portable Installation	Facilities	08/2024
Districtwide	Banners	Facilities	07/2024
Wilson High School	Little Theatre Improvement	CTE Grant	07/2024

199770

Cedarlane Academy - Playground Asphalt





Cedarlane Academy - Portable Installation


#### **WORK IN PROGRESS**






Grandview Academy - Parking Lot Restriping

#### **BEFORE**

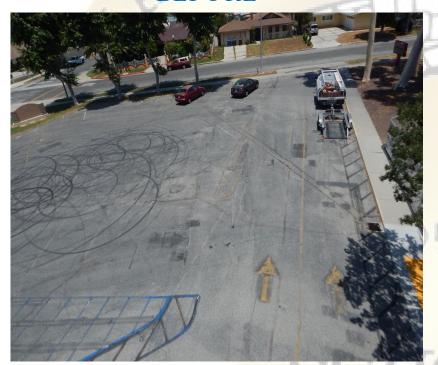





Los Molinos Elementary – Bottle Filling Station

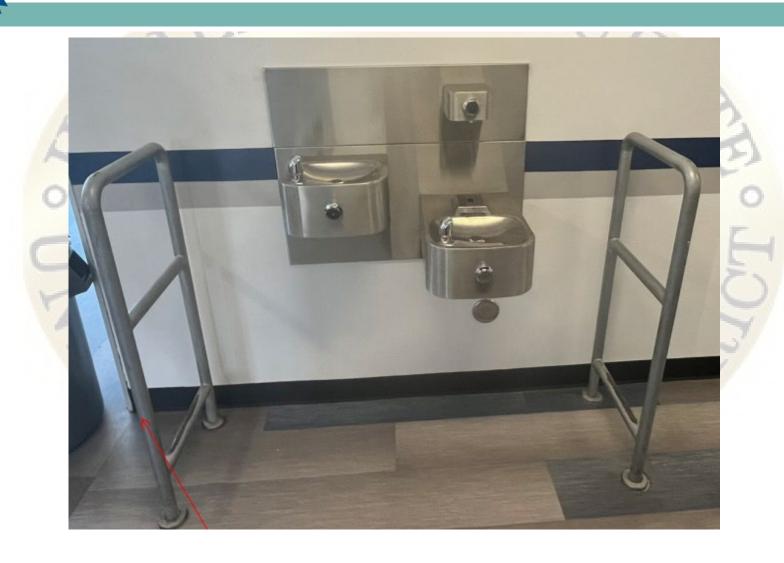

Mesa Robles Academy - Classroom Flooring

#### BEFORE

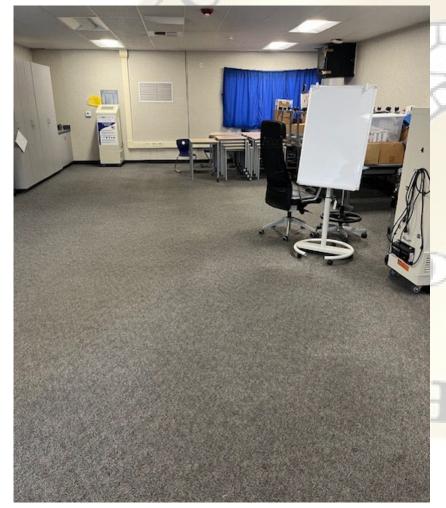

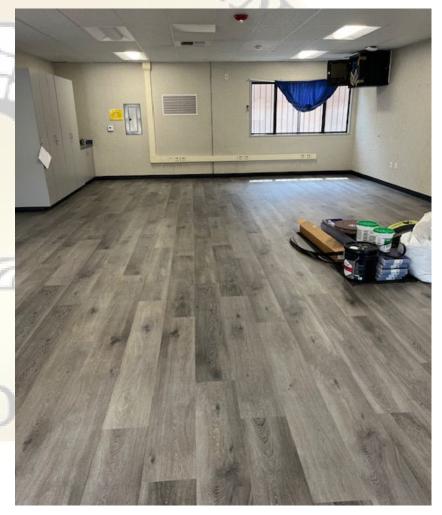


Wing Lane Elementary – Portable Installation

#### **BEFORE**





# Projects In Progress 2024-2025



#### **Facilities**

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
District Wide	HVAC System Replacement	Pending	Pending	Pending	TBD	Fa cilities	TBD
Kwis Elementary	Baseball Fields	Complete	Approved	Pending	TBD	Fa cilities	TBD
La Puente High School	Custom Shade Structure	Complete	Approved	Pending	TBD	Fa cilities	TBD
Los Altos High School	Gym & Locker Room HVAC (65 tons of temporary HVAC units have been installed)	Complete	Approved	Complete	In Progress	Fa cilities	12/2024
Los Altos High School	Stadium Press Box & Bleachers	Pending	Pending	Pending	TBD	Facilities	TBD
Sparks Middle School	Front Office Counter	NA	NA	Pending	Pending	Facilities	TBD
Wedgeworth	K-5 Permanent School	Complete	Approved	Complete	In Progress	COPS	06/2025
Wilson High School	Stadium Press Box & Bleachers	Complete	Pending	Pending	TBD	Facilities	TBD
Workman HS	Phase II Stadium and Baseball Field (Phase I Track & Field and Softball Field Complete) OPIION B	Complete	Approved	Approved	TBD	Facilities	TBD
Workman HS	Shade Structure, Wall, & Lighting	In Progress	Pending	Pending	TBD	Facilities	TBD

#### **Facilities**

Site	Item Description	Procurement	Construct	Funding Source	Target Completion Date
Baldwin Elementary Grazide Elementary Kwis Elementary La Puente High School Los Molinos Elementary Wilson High School	Roofing	Complete	In Progress	Fa cilities	10/2024
Stimson Learning Center	Roofing	Complete	Pending	Facilities	TBD

19770

ED SCHO

#### **Child Development**

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Amar Children's Center	Entry Security Project	Complete	Approved	Pending	Pending	Child Development	TBD
Amar Children's Center	Roofing	N/A	N/A	Pending	Pending	Child Development	TBD
Fairgrove Academy Head Start	Playground & Shade Structure	Complete	Approved	Complete	In Progress	Child Development	09/2024
Nelson Hementary Head Start	Playground, Shade Structure, & Accessibility Path of Travel	Complete	Approved	Complete	In Progress	Child Development	09/2024
Workman Hementary Head Start	Playground & Accessibility Path of Travel	Pending	Pending	Pending	Pending	Child Development	TBD

#### **Special Ed**

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
La ssa lette Hementary	Inclusive Playground	NA	NA	Complete	In Progress	General	09/2024

#### **Adult Ed**

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Center for the Performing Arts	Construction of NEW Performing Arts Center @ Temple Academy	Complete	Complete	Pending	TBD	Adult Ed	08/2025
Dibble Adult	Admin Upgrade	In Progress	NA	Pending	Pending	Adult Ed	TBD
Dibble Adult	Roofing	N/ A	N/ A	Complete	In Progress	Adult Ed	10/2024
Willow Adult	Marquee	Complete	NA	Pending	Pending	Adult Ed	TBD

#### **Nutrition Services**

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Baldwin Hementary School	Kitchen Renovation - Three Compartment Sink Installation	Complete	NA	Pending	TBD	Food Services	TBD
District Office	Warehouse Freezer	Complete	NA	Pending	TBD	Food Services	TBD
Mesa Robles Middle School	Kitchen Renovation	Complete	Approved	Pending	TBD	Food Services	TBD
Wilson High School	Kitchen Modernization	Pending	Pending	Pending	TBD	Food Services	TBD

19970

RED SCT

