



---


## New Construction

PROGRESS UPDATE  
August 2024

---

# Fairport Harbor New Pre K-12 School



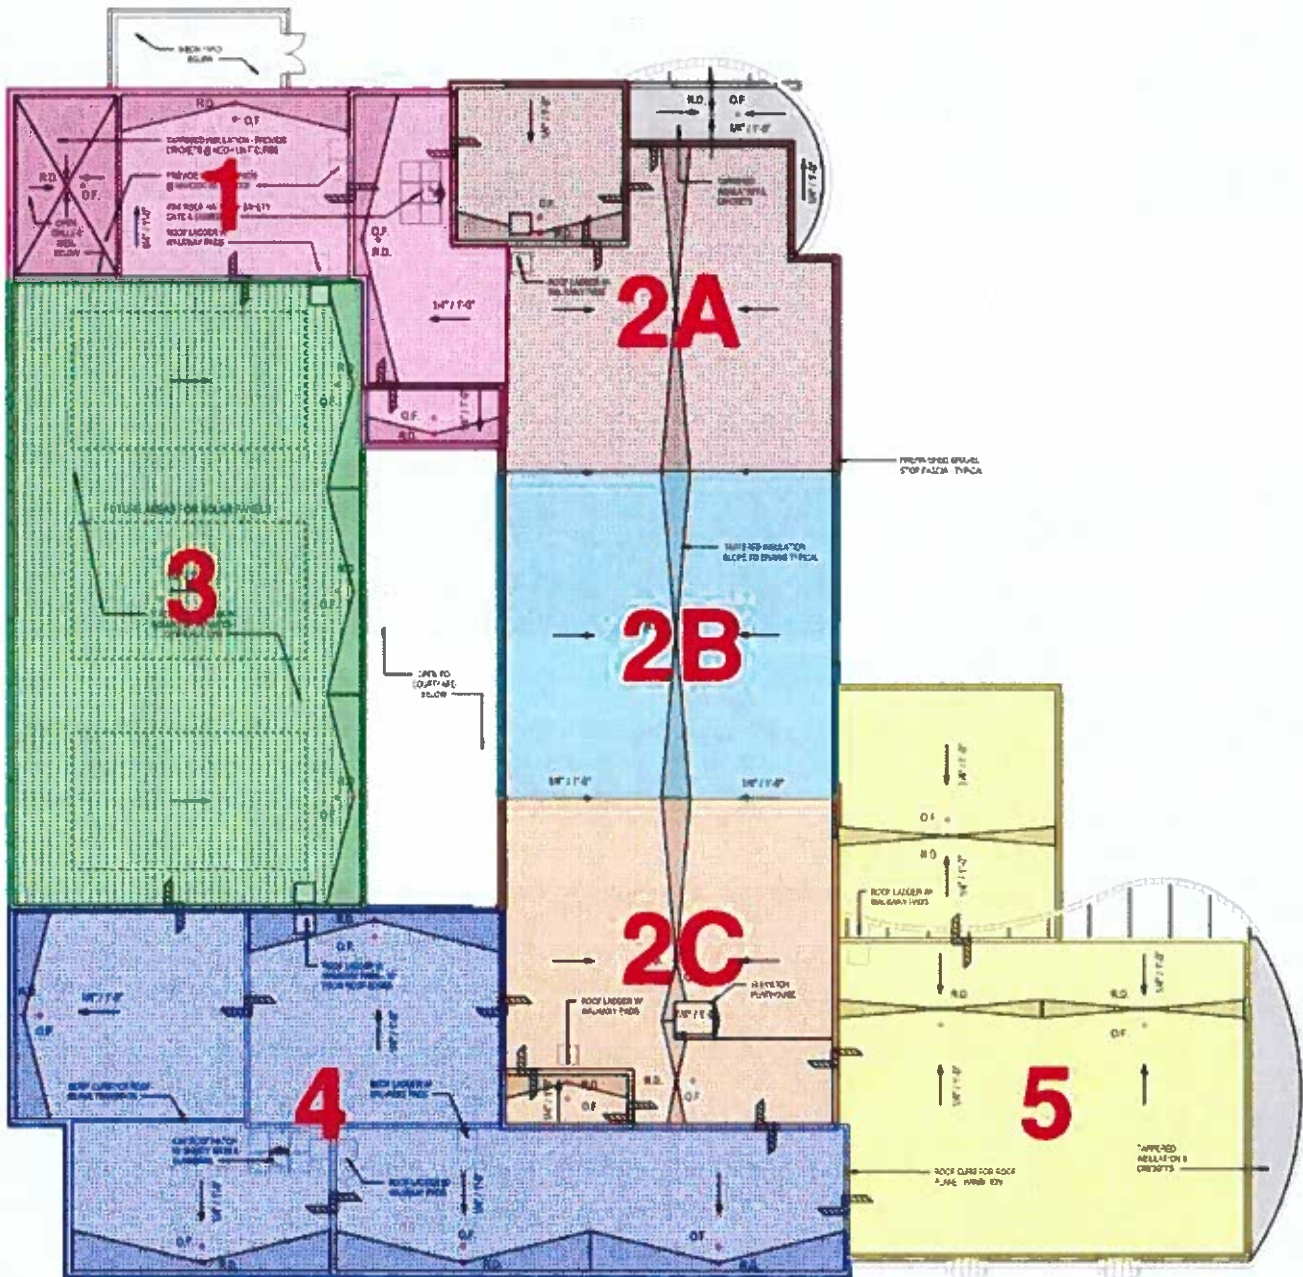

## PROJECT SUMMARY

### North 1/3 of Area 3 (Phase 1)


- Accessory Storage Areas
- Main Electrical Room
- Locker Rooms
- Exercise Rooms
- Mechanical Equipment Room

### August 2024 Progress


- Brick Veneer—Complete
- Setting Air Handling Equipment—Complete
- Setting Chiller—Complete
- Setting Bar Joist and Deck—In Progress
- Overhead Ductwork—In Progress
- Mechanical Piping—In Progress
- Stair Tower #4—In Progress

### Upcoming Progress

- Roof Blocking
- Roof Membrane

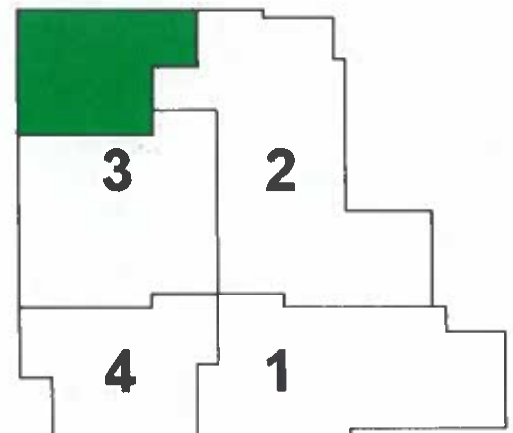

**PROJECT SUMMARY**

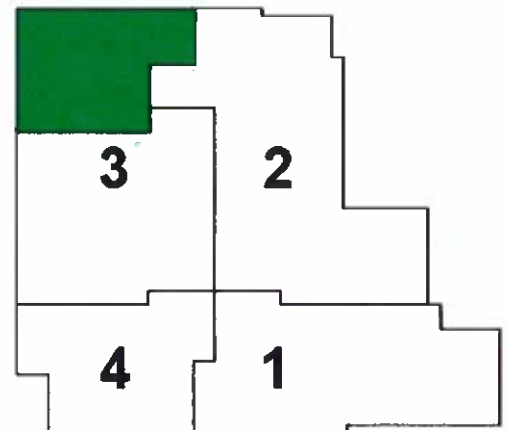

## PROJECT SUMMARY

### North 1/3 of Area 2 (Phase 2A)


- Educational Classrooms

### August 2024 Progress


- Fire Alarm Piping—Complete
- Cold Formed Metal Framing—Complete
- Setting Bar Joist and Deck—In Progress
- Window Blocking and Sheeting—In Progress
- Brick Veneer—In Progress

### Upcoming Progress

- Roof Blocking
- Roof Membrane

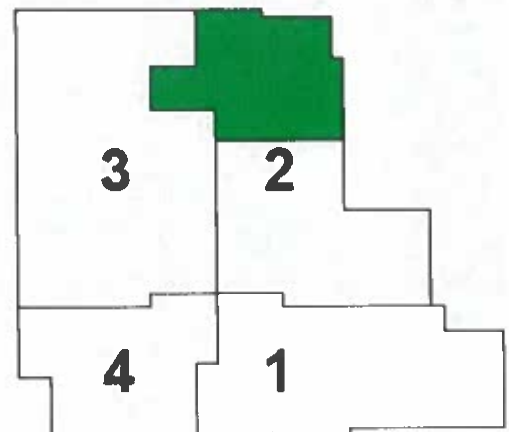

**PROJECT SUMMARY**

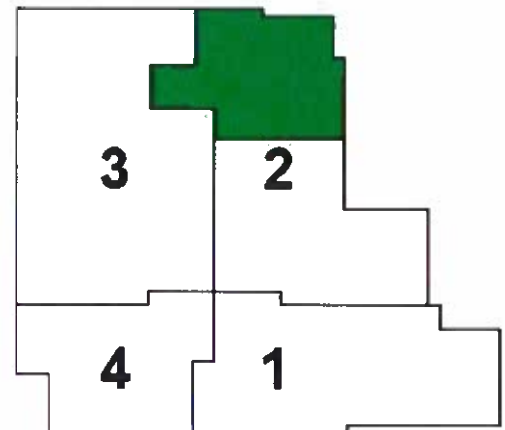

## PROJECT SUMMARY

### South 2/3 of Area 2 (Phase 2B and 2C)


- Educational Classrooms

### August 2024 Progress


- Elevator Pit—Complete
- Foundations—Complete
- Underground Plumbing—Complete
- Underground Electrical—Complete
- Masonry to Grade—Complete
- Slab On Grade—In Progress
- 1st Floor Masonry to Bearing—In Progress
- 1st Floor Structural Steel—In Progress

### Upcoming Progress

- Second Floor Precast Plank
- Masonry Bearing on Second Floor
- Overhead Plumbing Rough In
- Overhead Electrical Rough In

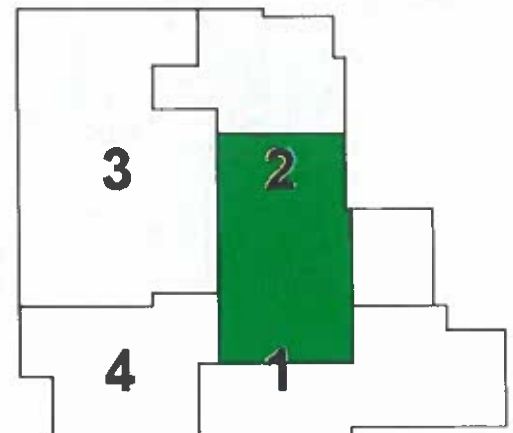

**PROJECT SUMMARY**

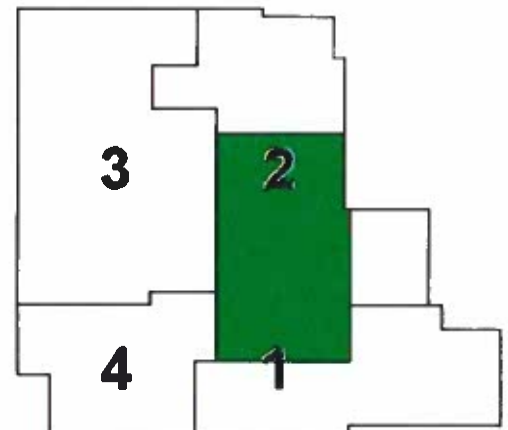





## PROJECT SUMMARY

### South 2/3 of Area 3 (Phase 3)


- Auxiliary GYM
- Gymnasium

### August 2024 Progress

- Footers—Complete

### Upcoming Progress

- Precast Wall Panels
- Joist and Decking

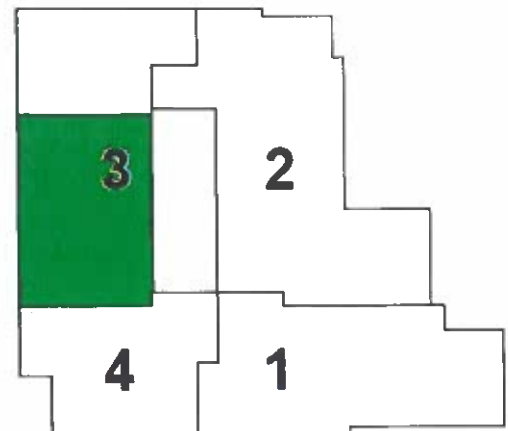

**This page intentionally  
left blank**
