


Completed/Work in Progress:

- ➤ Hauling Spoil Materials-Finish this week
- Prep for curb and gutter along west wall and placing topsoil at Geothermal Field
- Roof Panels seaming area A and C
- Installing Roof Panels at Entrance Roofs
- Installing MCM Panels Area C and A
- Installing Batten Seam Trim and Panels Area A and C
- Installing Window Frames (Storefront) at A, C and F
- Continuing Interior Framing at Area D Ceilings and Soffits
- Elevator Installation to be complete by early next week
- Finish Sprinkler in Area D


Upcoming Look Ahead:

- Begin Curb and Gutter
- Complete Stair C1. Receive Stair at B Area
- Exterior Furring and Sheathing at Area A Complete. Move to Area E
- Roof Panels seaming area A and C
- Installing Window Frames (Storefront) at A, C and F
- Continuing Interior Framing at Area D Ceilings and Soffits, Framing in Media Room
- Finish tile Area A Second Floor, Move to Area C Second Floor
- Complete Terrazzo Area A Second Floor, Move to Area C Second Floor
- Start Sprinkler in Cafeteria and Continuing Plumbing Above Ceiling Area E (Strom Shelter)
- Continue Controls Area E and Area F
- Continue Electrical Rough in Throughout Building






Area A – 2nd Floor Terrazzo Continues

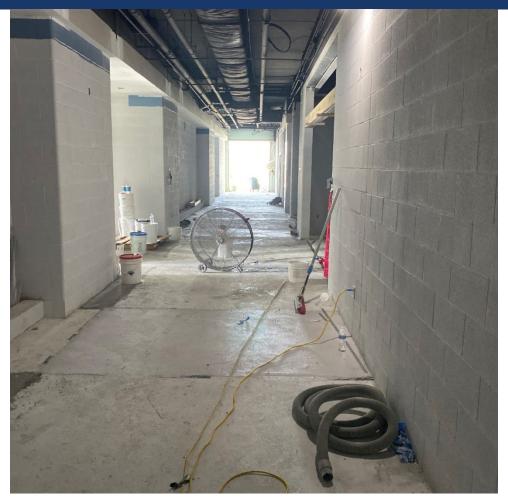




Area C – Metal Roof Panels Continue

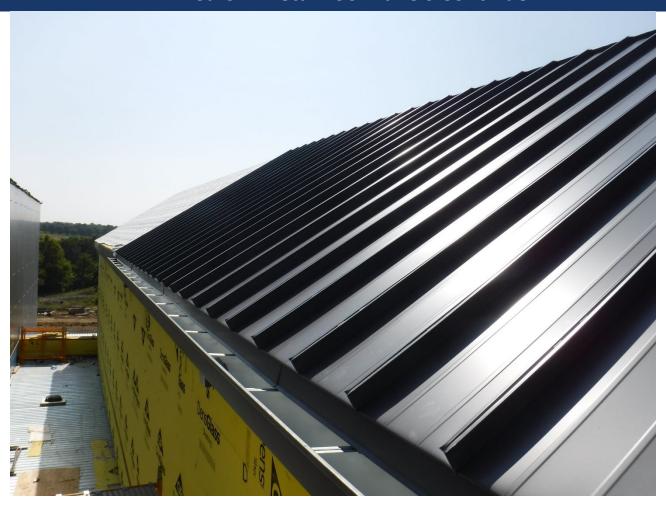



Area D – Elevator Cab Install

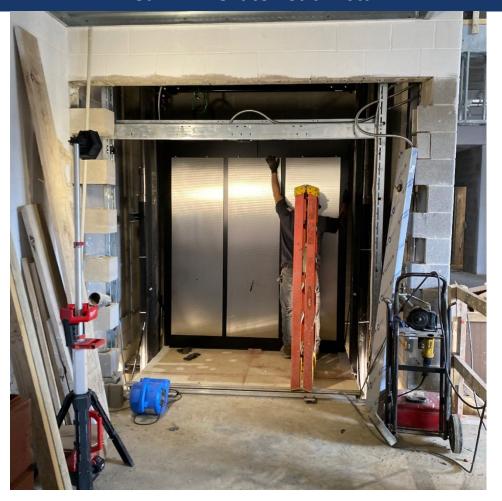



Area D – Elevator Door Install






Area D – Media Center Windows Continue in Stala Frames





Area D – Soffit Framing at 2nd Floor Openings

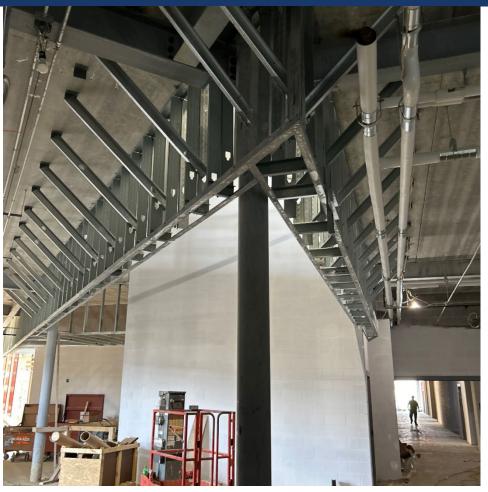



Area E – Vertical Metal Panels in Art Courtyard Continues





Site – Sidewalk and Steps to Football Field Complete

