

Dear SLP School Community,

The recent storms caused power outages in the area, leaving the High School without power and causing final inspection delays for occupancy clearance. As a result, the first day of school for High School students (grades 9-12) is postponed until Thursday, September 5, 2024, to allow time for required final building inspections. This does not impact the last day of school because the District has sufficient instructional days in the school calendar to allow for weather emergencies.

As planned, grades 1-8 will begin their first day of school on September 3, 2024. Kindergarten students will begin their first day of school on September 4, 2024. Please note that 9th Grade Orientation is canceled with revised plans to be announced. The 10-12th Grade Meet and Greet is cancelled.

PROJECT MILESTONES

- 8.05.24** SLP Central Community Center Demolition Began
- 8.19.24** SLP Park Central Operations Center Street Utility Tie-Ins Completed
- 8.20.24** SLP HS Classroom Furniture Move In Began
- 8.27.24** SLP Central Community Center Utility Tie-In Complete
- 8.30.24** SLP HS Parking Lot Completed

Construction Progress

SLP High School Additions/Renovations and Track and Field Reconstruction

- The project consisted of both additions and renovations of the existing High School. The scope included: Level 2 & 3 Classroom Renovations, Media Center Renovations, Storm Shelter Reconstruction, New Cafeteria and Link Addition, Parking Lot Reconstruction, Implementing a Stormwater Retention System, and Reconstruction of the Track & Field Facilities.

SLP High School Music Room Renovations

- The High School Music Rooms Renovations projects consisted of door replacements, new room finishes of floors, walls, ceiling and acoustical panels, replacement of three air handling units and two fan coil units, creation of a hydronic heating loop for the air handlers, electrical lighting upgrades and other electrical modifications. Also included in the scope were refresh renovations to the B150 & B174 main lobby and corridor. Including new wall tile, paint, ceiling tile, and lighting.

SLP High School Classroom Renovations Phase 2

- The project consisted of renovations of the existing High School. The scope included a refresh of twenty-seven existing classrooms along with hallways, and stairwells stretching across three floors.

Park Central Operations Center


- Construction Duration: December 2023 – November 2024
- MEP rough ins are complete.
- Exterior Metal Panels and Window install complete.
- Sheetrock installation has begun.

SLP Central Community Center

- Construction Duration: July 2024 – August 2025
- Locker Demolition is complete.
- Floor Removal is complete.
- MEP demolition is complete.




SLP High School - Kitchen Serving Area

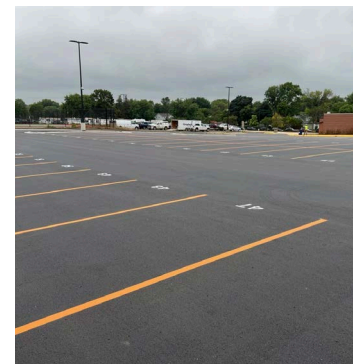

SLP High School - Parking Lot Reconstruction




SLP High School Classroom Renovations Phase 2 – Classroom Renovation

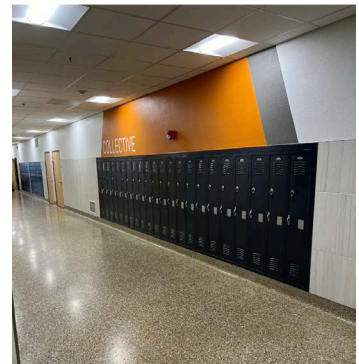

SLP High School Classroom Renovations Phase 2 – Hallway Renovations



SLP High School Music Renovations – Band Room

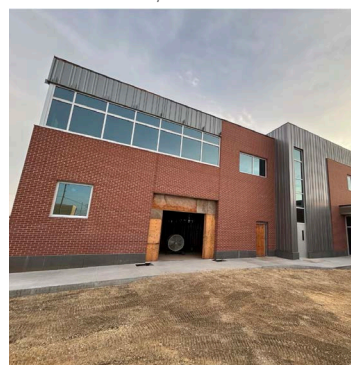

SLP Park Central Operations Center – Exterior
