
Tomahawk Elementary OWNER: Shawnee Mission School District School **CONSTRUCTION UPDATE** 6301 W 78th St. Shawnee Mission **ARCHITECT:** DLR Group KS, 66204 8/23/2024 CM: JE DUNN 2 WEEK LOOK AHEAD CURRENT PROGRESS -Area A/B Roof Install - Area B Exterior Stud Framing/Sheathing -Area A Interior Framing - Area A Overhead MEP -Area B Overhead MEP - Area A Weatherproofing -Area B Weatherproofing -Gym Roof Install -Exterior Masonry Install -Gym Masonry Wall Install SHAWNEE MISSION SCHOOL DISTRICT TOMAHAWK ELEMENTARY SCHOOL **OPENING FALL 2025** R SHAWNEE MISSION DLR Group \bigcirc **SMSD Tomahawk Elementary School** JEDUNN







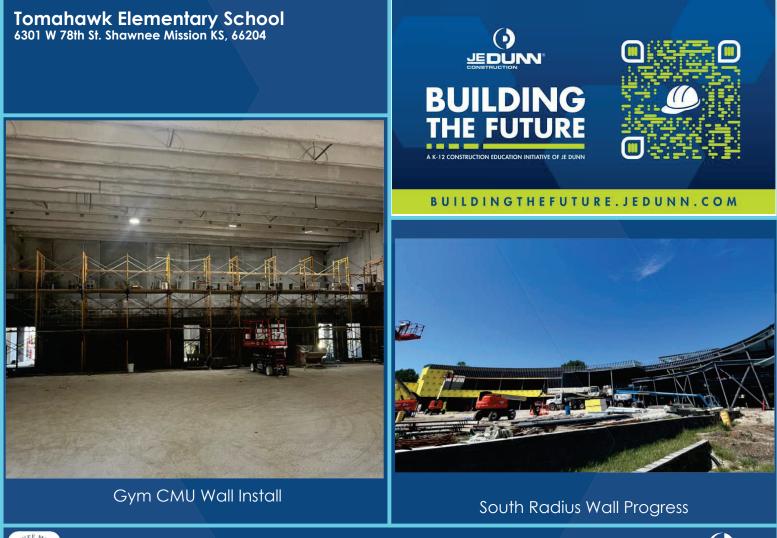


Overhead MEP Progress


SAFETY EVERYONE. EVERYWHERE. ALL THE TIME.



Gym Roof Install



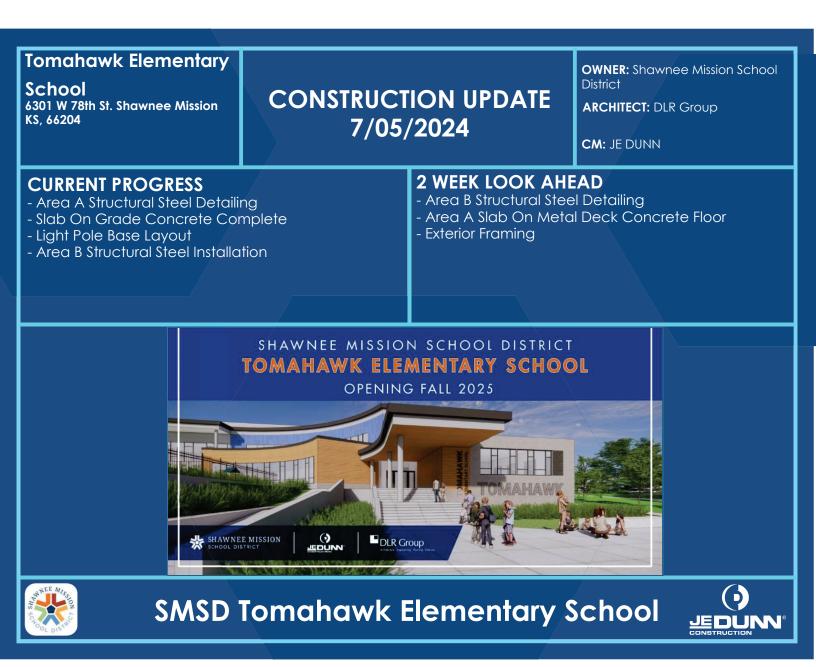

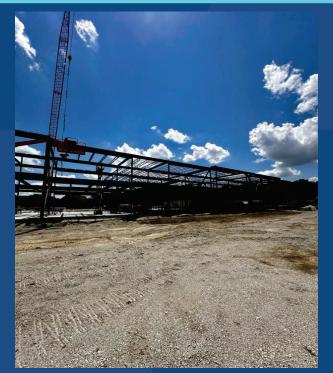

Area A Structural Steel Detailing



BUILDINGTHEFUTURE.JEDUNN.COM



Completed Concrete Slab







Kitchen Structural Steel Erection


SAFETY EVERYONE. EVERYWHERE. ALL THE TIME.




West Side Site View





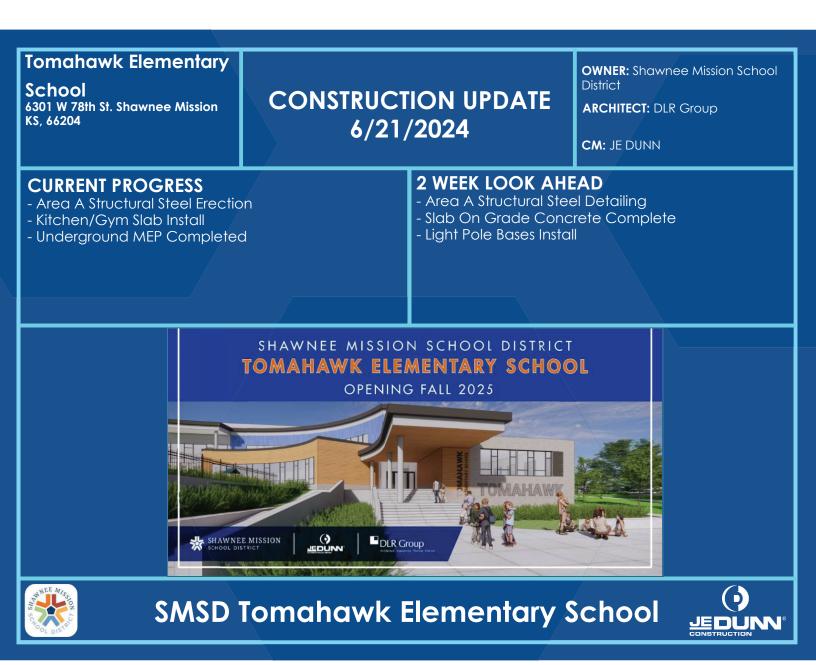

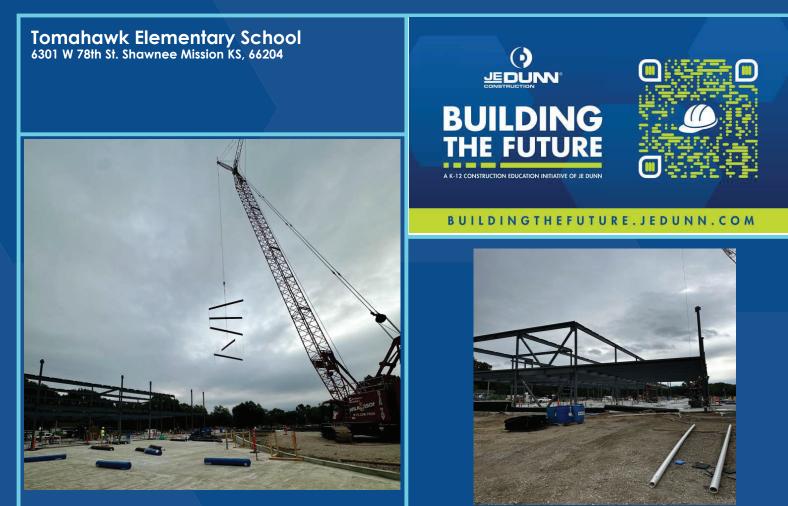

Area A Structural Steel Install

Area A Steel







Kitchen Concrete Slab Preparation


SAFETY EVERYONE. EVERYWHERE. ALL THE TIME.



North West Corner Site View





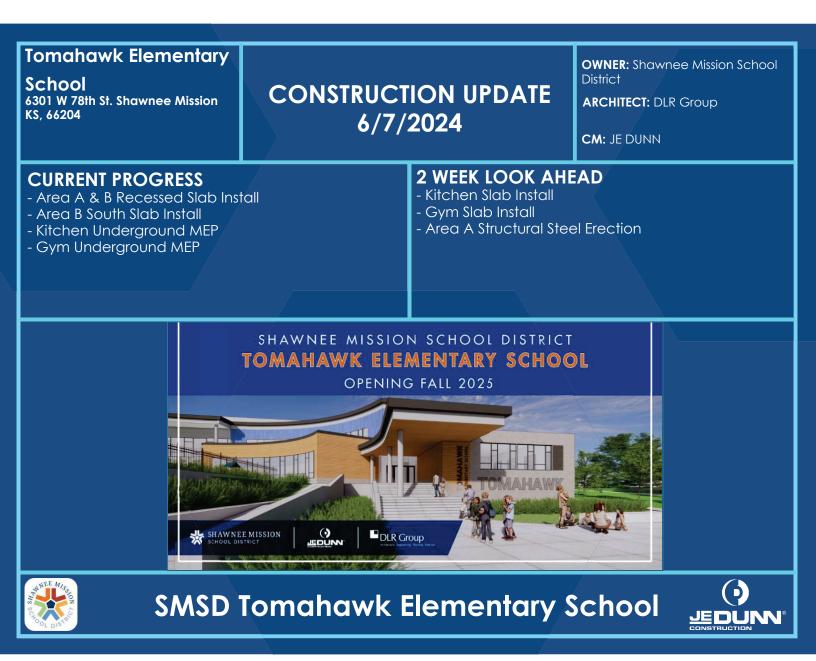



Area A Slab Install



BUILDINGTHEFUTURE.JEDUNN.COM









Completed FEMA Gym Install


SAFETY EVERYONE. EVERYWHERE. ALL THE TIME.



Kitchen Underground MEP





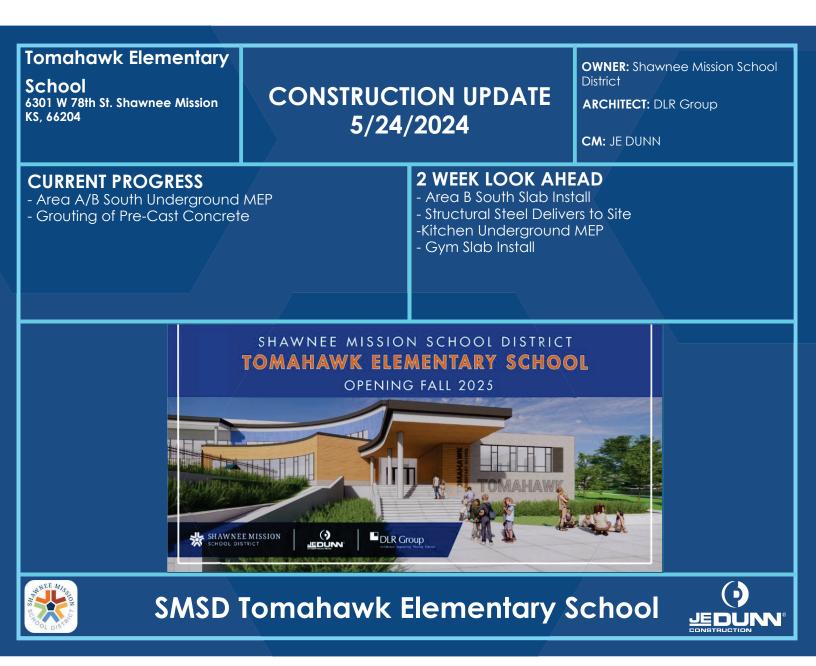



Ongoing Underground MEP

Area B North Slab Install







Installed FEMA Gym


SAFETY EVERYONE. EVERYWHERE. ALL THE TIME.




FEMA Gym Install





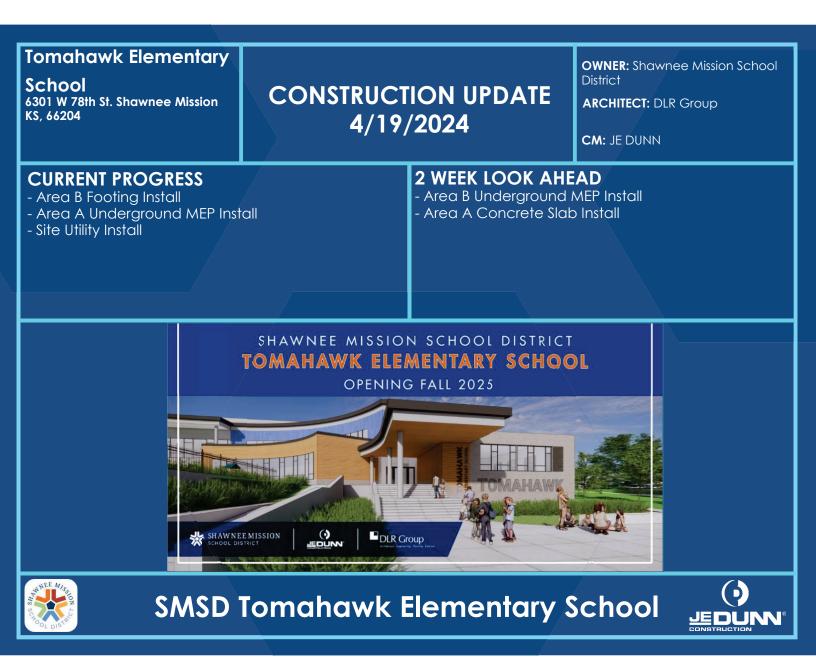

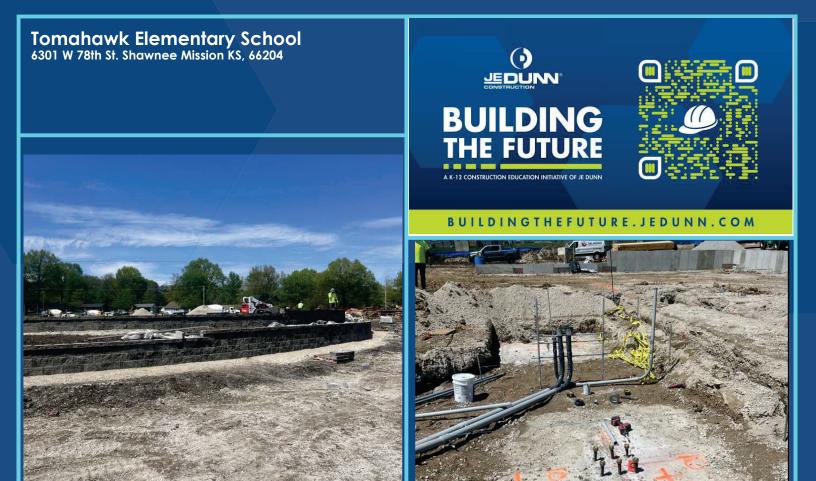

Retaining Wall Progress

Underground MEP Area A







Area B Footing Install


SAFETY EVERYONE. EVERYWHERE. ALL THE TIME.



Admin Area Concrete Install





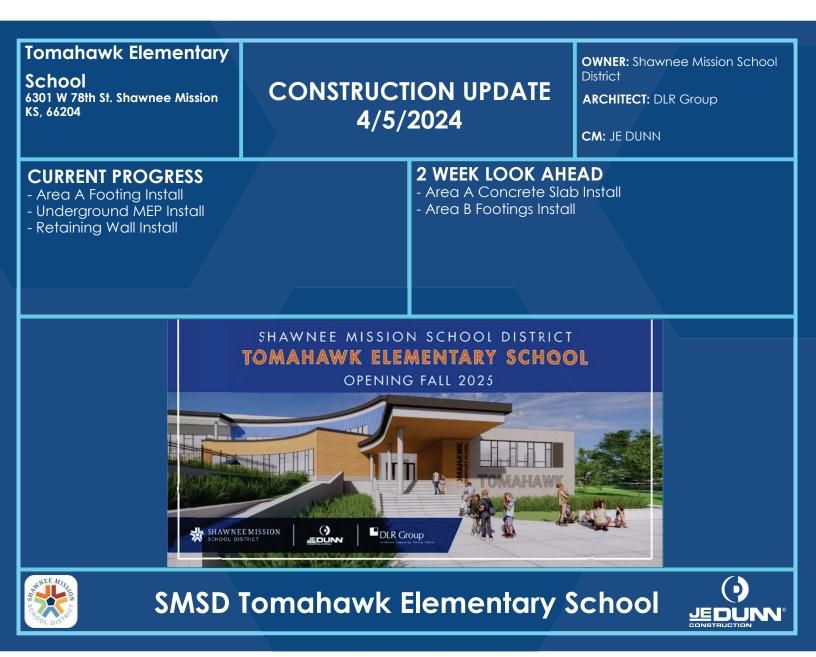









BUILDINGTHEFUTURE.JEDUNN.COM



Radius Storefront Footings







Gym Footing Install

SAFETY EVERYONE. EVERYWHERE. ALL THE TIME.




Site Utilities Install







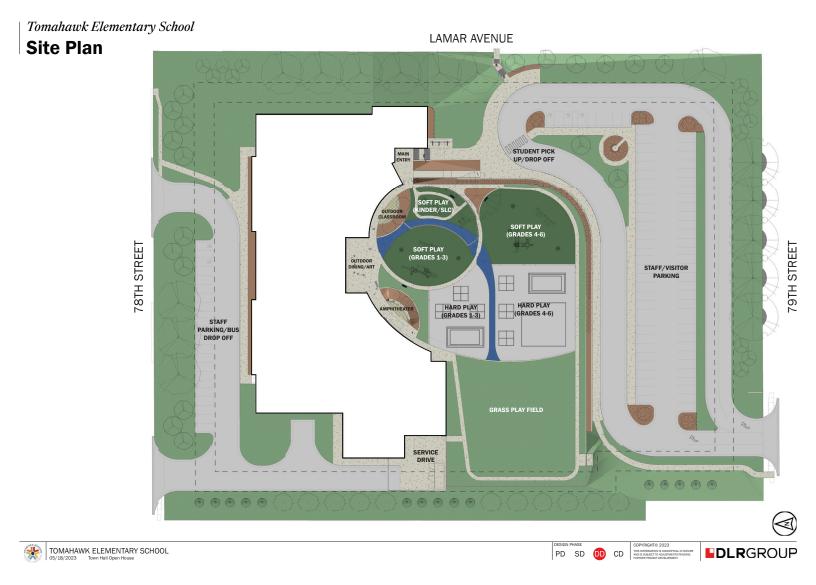





Tomahawk Elementary School Floor Plan: Level 02









