


Completed/Work in Progress:

- Installed 3000 LF of Curb and Gutter
- Completed Stone Reservoir and Base for Permeable Paving
- Completed Install Structural Steel at Stair C1
- > Continue MCM and Batten Seam Panels on Area C and A (Trim/Finish on entire areas and West Elevations)
- Completed Exterior Dense Glass and Furring on Area A and Exterior Furring and Dense Glass Area B
- Metal Framing at Kitchen complete except soffit at Cooler/Freezer
- Continue Window Frame Installation
- Completed Tile in Area A and Area A Terrazzo Install (50% grinding complete on first floor)
- Completed Sprinkler Area A-D rough-in (Except Stairways and Elevator)

Upcoming Look Ahead:

- Area B stairs scheduled for delivery 9-11-24 and install will be started
- Continue Stone Reservoir and Base for Permeable Paving
- Start Installing Curtain Wall Windows Area A and C
- Continue MCM and Batten Seam Panels Area A and Exterior Furring Area B/D
- Finish Hanging Sheetrock Area B
- Start Installing Ceiling Grid Area A 1st Floor
- Finish Area D Sprinkler Rough in and Pressure Testing
- Plumbing vent penetrations through roof
- Continue Tile work in Area C and move forward to Area D





Area A – Operable Windows Starting to be Installed






Area A – Terrazzo Layout on 2nd Floor






Area B – Admin Corridor Drywall Install

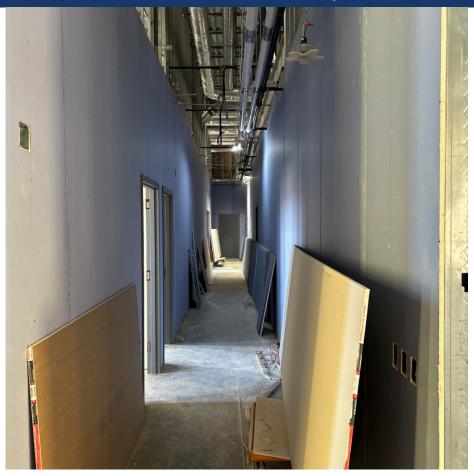



Area C- 2nd Floor Windows and ACM Panel

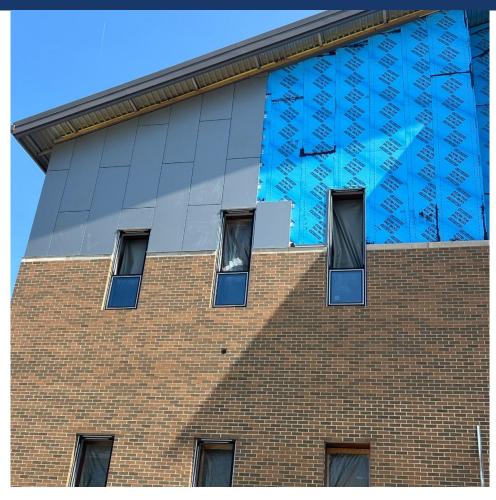



Area C – Vertical Metal Panels at Outdoor Classroom






Area C – Vertical Metal Panels





Area F – Bus Canopy Fascia has begun

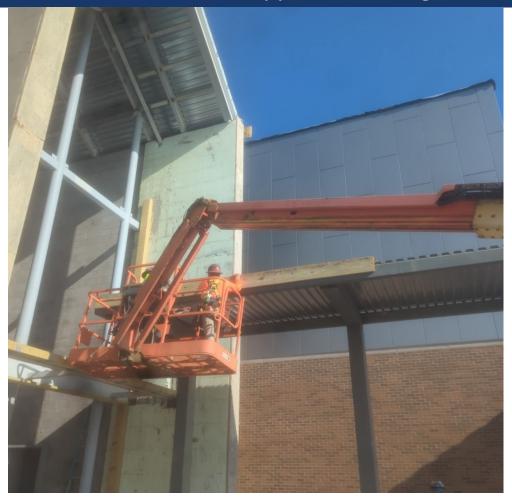



Area F – Kitchen Soffit Framing Continues

