

Harrison ES – Preschool Classrooms Addition & HVAC Upgrades



Harrison ES – Preschool Classrooms Addition & HVAC Upgrades



➤ **Completed Work:**

- Poured the new sidewalk adjacent to the playground and along the school building, improving the pathway for student access.
- 80% of the concrete footers have been poured.
- 50% of the foundation walls have been completed.

➤ **Upcoming Work / Look Ahead:**

- Complete pouring of the remaining foundation walls.
- Begin excavation and pouring of the remaining footers.
- Start backfilling the slab area.
- Commence installation of drainage lines in the parking lot area.
- Reopen the egress path for safe access.

Harrison Elementary – Preschool Classrooms Addition & HVAC


Concrete footer and foundation are in progress.



Harrison Elementary – Preschool Classrooms Addition & HVAC



New sidewalk adjacent to the playground is in Progress.

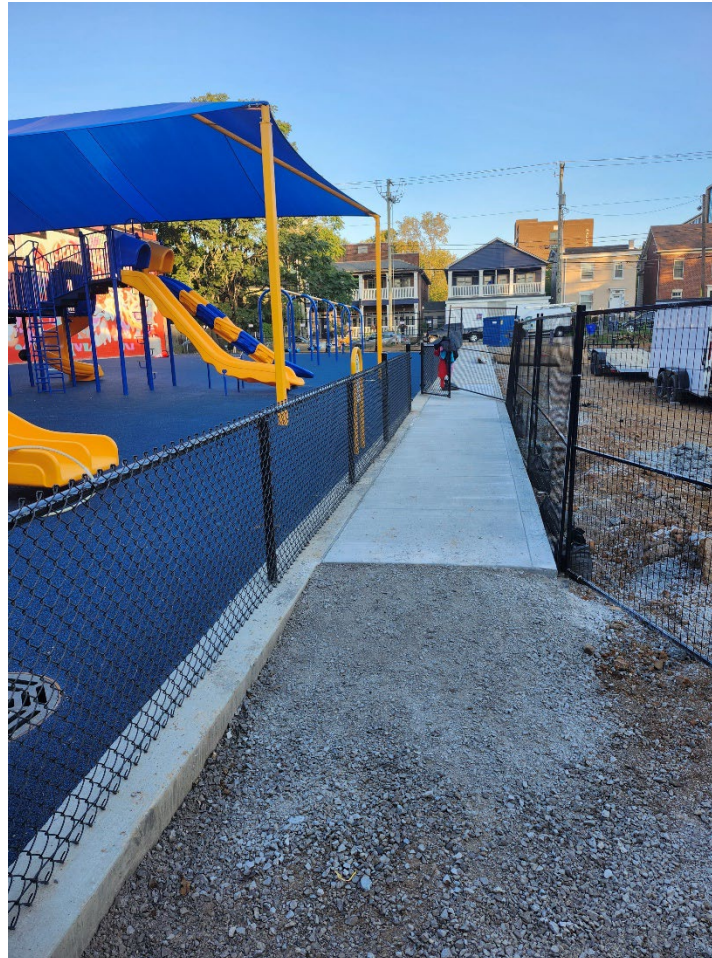

Week Ending September 20, 2024

Harrison Elementary – Preschool Classrooms Addition & HVAC



New sidewalk adjacent to the school building improving the playground access.



Week Ending September 20, 2024

Harrison Elementary – Preschool Classrooms Addition & HVAC



Poured sidewalk to the storage container



Week Ending September 20, 2024
